

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending December of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U45201BR2008PTC014135	Name of Firm	SIDHANTA ESTATE PRIVATE LIMITED
Firm Address :	DAUD BIGHA, NEAR HANUMAN MANDIR, NICHOLAS GODOWN, BUILDING, KANKARBAGH MAIN ROAD, PATNA-800020		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA	07 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP00907-4/1242/R-1232/2021	Name of Project/Phase of Registered Project	USHA TOWER
Name of Promoter	SIDHANTA ESTATE PRIVATE LIMITED	Project Address	KHATA NO. -140, PLOT NO.- 334(P), MAUZA-KUMHRAR, DIST. -PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	15/08/2022		
Starting date of Project or Phase of the Project	26/10/2021		
Type of Project or Phase of the Project	COMMERCIAL		
Period of validity of map by the Competent Authority	15/08/2022		

Sidhanta Estate Private Limited

Rakesh Kumar
Director

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - 50% Of Total Built Area	Total Number of Apartments in Landowner's share - 50% Of Total Built Area
	1. 1 BHK			03	1. Booked / Allotted -NIL	3. Booked/ Allotted-NIL
	2. 2 BHK, -				2. Sold-NIL	Sold -NIL
	3. 3 BHK					
	4. Shop					
	5. Bungalow					
	6. Plot etc.					
					Percentage of booking 0%	Percentage of booking 0%

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)
------	---------	----------------	--------------------

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	- NIL
		2. Sold	- NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.				
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

Sidhanta Estate Private Limited

Rakesh Kumar
Director

Sidhanta Estate Private Limited

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. _____ (To be filled for each Building / Wing)

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	NO	
3.	Podiums (if any)	100%	
4.	Plinth	100%	
5.	Stilt Floor	100%	
6.	Slabs of Super Structure	100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100% 100% 100% 100%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	100% 100%	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100% 100% 100%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	100% 100% 100% 100%	

Sidhanta Estate Private Limited

Rakesh Kumar

Director

11.	<p>Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale.</p> <p>Any other activities</p>	<p>50%</p> <p>100%</p> <p>N/A</p> <p>100%</p> <p>100%</p> <p>100%</p>	30-01-2025
-----	--	---	------------

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yy y) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	100%	
2.	Water Supply	YES	100%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	100%	
4.	Storm Water Drains	YES	100%	
5.	Landscaping & Tree Planting	YES	100%	
6.	Street Lighting	YES	100%	
7.	Community Buildings	NO	N/A	

Sidhanta Estate Private Limited

Rakesh Kumar
Director

8.	Treatment and Disposal of Sewage and Sullage Water	NO	N/A	
9.	Solid Waste Management & Disposal	YES	100%	
10.	Water Conservation / Rain Water Harvesting	YES	100%	
11.	Energy Management	YES	100%	
12.	Fire Protection and Fire Safety Requirements	YES	0%	
13.	Closed Parking	YES	100%	
14.	Open Parking	YES	100%	
15.	Electrical Meter Room, Sub-Station, Receiving Station	NO		
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			

Sidhanta Estate Private Limited


Rakesh Kumar

Director

8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

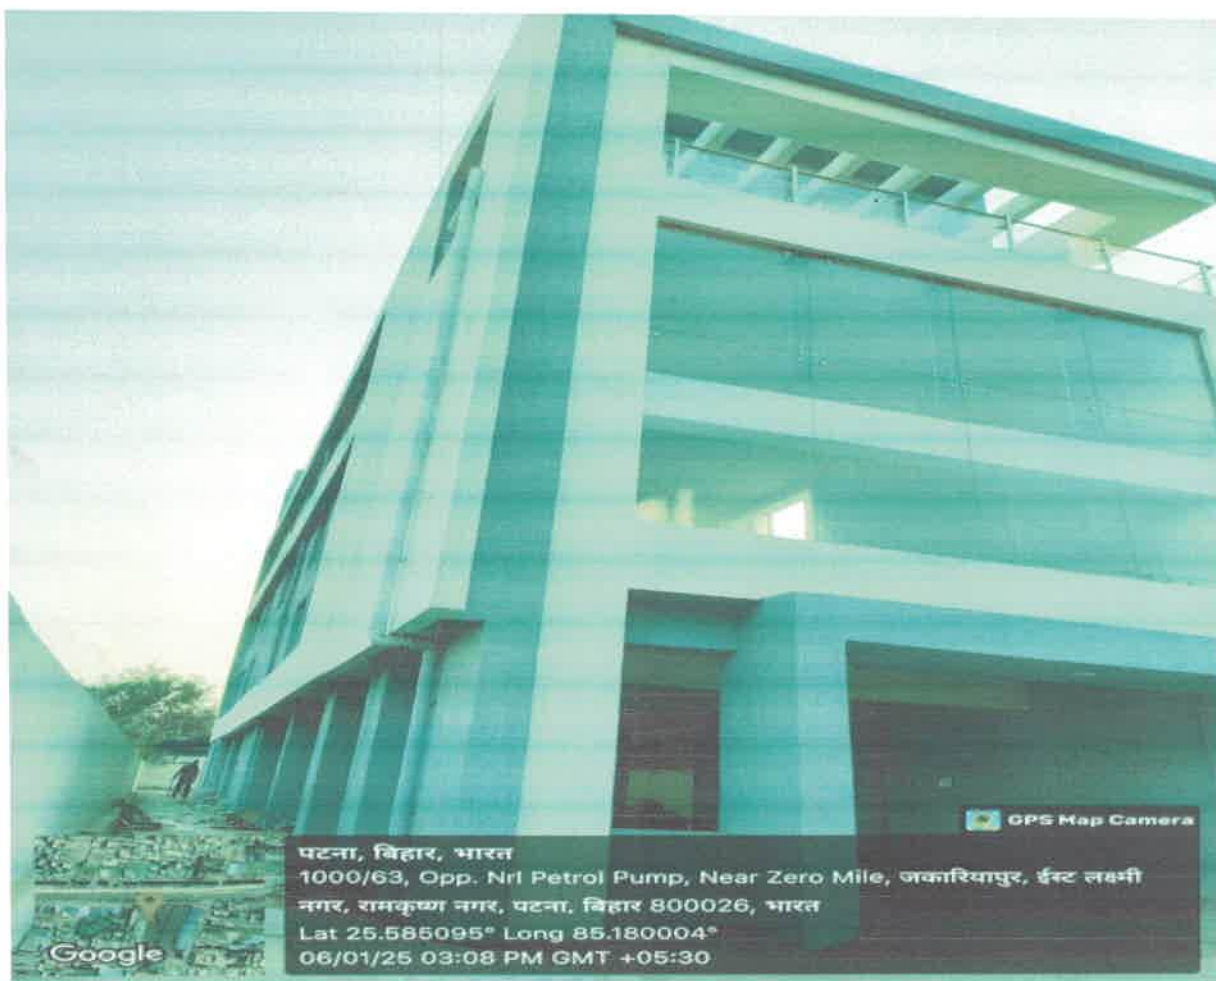

Sidhanta Estate Private Limited
 Rakash Kumar
 Director



Sidhanta Estate Private Limited
 Rakesh Kumar
 Director



X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	625905051140
2.	Estimated Cost of the Project including land cost at the start of the Project	4,60,68,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	1,32,62,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	00=00
6.	Actual Cost Incurred during the Quarter	00=00
7.	Net amount at end of the Quarter	00=00
8.	Total expenditure on Project till date	00=00
9.	Cumulative fund collected till the end of Quarter in question	
10.	Cumulative expenditure done till the end of Quarter in question	

Sidhanta Estate Private Limited

Rakesh Kumar

Director

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS

A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

XIV UNITS ALLOCATION DETAILS

Total Number of sanctioned apartments 1 BHK- 2 BHK, - 3 BHK 4 BHK- Shop- Bungalow - Plot etc	Details of allotment made so far with Flat number/ Bungalow - Plot etc	Cancellation of flat allotment, If any with Flat number/ Bungalow – Plot etc
---	--	--

Sidhanta Estate Private Limited

Rakesh Kumar
Director

XV. BROCHURE /Prospectus**XVI Grievance Redressal Officer****Name :** Rakesh Kumar**Contact No :** 9835409830**Email id :** sidhantaestate@gmail.com**Address :** Daud Bigha, Near- Hanuman Mandir, Nicholas Godwon Building, Kankarbagh Main Road, Patna**Undertaking:**

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Sidhanta Estate Private Limited

*Rakesh Kumar**Director*

Signature of Promoter

Name:

Date:
