

Date: 15-04-2025

To,
The Chairman,
Real Estate Regulatory Authority,
Bihar, Patna.

SUB:- Submission of Quarterly Progress Report of Fourth Quarter (2024-2025) i.e. 01.01.2025 to 31.03.2025 of "WINSOME EMPIRE BLOCK E", Danapur, Patna, RERA Regn. No.- BRERAP2611201700038-7/1250/R-1069/2020.

Dear Sir,


With reference to the above mentioned subject and as per the requirement of quarterly Progress reports compliance, we are hereby submitting the project quarterly Report for the Fourth Quarter (2024-2025) for the project named "Winsome Empire Block E" located at Biscuit Factory Road Nasriganj, Danapur, Patna, Bihar.

A detailed quarterly report of the project is attached along with this letter as Form-7

Kindly acknowledge the receipt of the same.

Thanking You

WINSOME INFRASTRUCTURE



PARTNER

Sanjeev Kumar

(For, Winsome Infrastructure)

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending March/~~June/sept/December~~ of
2024 - 25 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration- Number/CIN No/Partnership deed no/LLP Details/ Any other registration with MSME Or Govt. Bodies		Name of Firm	Winsome Empire Block-E
Firm Address :	101, Suksha Presidency, Ram jaipal Nagar, Baily Road, Danapur, Patna - 801503		
Total Experience of promoter in Real Estate sector	16 Years.		
Total Experience in Real Estate after Implementation of RERA			
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	04	
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	06	

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP261120170 0038-7/1250/R- 1069/2020	Name of Project/Phase of Registered Project	WINSOME EMPIRE BLOCK E
Name of Promoter	WINSOME INFRASTRUCTURE	Project Address	Biscuit Factory Road, Nasriganj, Danapur, Patna
Name of Co-promoter			
Project Registration is valid up to	01/10/2024		
Starting date of Project or Phase of the Project	20/11/2020		
Type of Project or Phase of the Project	1. Residential 2. Commercial 3. Residential- cum-Commercial 4. Plotted project		
Period of validity of map by the Competent Authority	Map Sanctioned on		



III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building / Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share – 34	Total Number of Apartments in Landowner's share – 22
	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow - 6. Plot etc.			56	1. Booked / Allotted -33	3. Booked/ Allotted - 0
					Percentage of booking- 97.00%	Percentage of booking

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	- 33
	100	2. Sold	- 00

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				



VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. _____ (To be filled for each Building / Wing)

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	100%	
3.	Podiums (if any)		
4.	Plinth	100%	
5.	Stilt Floor	100%	
6.	Slabs of Super Structure	100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	95%	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	95%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	95%	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other	95%	



	requirements as may be required to complete project as per Specifications in Agreement of Sale. Any other activities.		
--	--	--	--

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	yes	60%	
2.	Water Supply	yes	65%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	yes	65%	
4.	Storm Water Drains			
5.	Landscaping & Tree Planting	yes	25%	
6.	Street Lighting	yes	0%	
7.	Community Buildings			
8.	Treatment and Disposal of Sewage and Sullage Water	NO		
9.	Solid Waste Management & Disposal	No		
10.	Water Conservation / Rain Water Harvesting	yes	0%	
11.	Energy Management	No		



12.	Fire Protection and Fire Safety Requirements	yes	85%	
13.	Closed Parking	yes	95%	
14.	Open Parking	no		
15.	Electrical Meter Room, Sub- Station, Receiving Station	yes	45%	
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE


O

F PLOTTED DEVELOPMENT


		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths	Yes	55%	
2.	Water Supply	yes	45%	
3.	Sewerage Chambers Septic Tank	yes	65%	
4	Drains	Yes	45%	
5.	Parks, Land Scaping and Tree Planting	Yes	0%	
6.	Street Lighting	Yes	0%	
7.	Disposal of sewage & sullage water	No		
8.	Water conservation/Rain Water Harvesting	Yes	0%	
9.	Energy Management	No		



IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

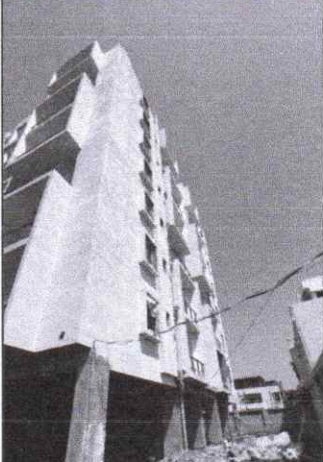(A)	Sr. No.		
	1.	Front Elevation	 <p>Patna, Bihar, India Bisuit Factory Road, Danapur, Patna, Bihar 800018, India Lat: 25.699287, Long: 85.068766 04/05/2025 10:24 AM GMT+05:30 Note: Captured by GPS Map Camera</p>
	2.	Rear Elevation	 <p>Patna, Bihar, India Bisuit Factory Road, Danapur, Patna, Bihar 800018, India Lat: 25.629051, Long: 85.069470 04/05/2025 10:27 AM GMT+05:30 Note: Captured by GPS Map Camera</p>
	3.	Side Elevation	 <p>Patna, Bihar, India Bisuit Factory Road, Danapur, Patna, Bihar 800018, India Lat: 25.629057, Long: 85.069457 04/05/2025 10:22 AM GMT+05:30 Note: Captured by GPS Map Camera</p>

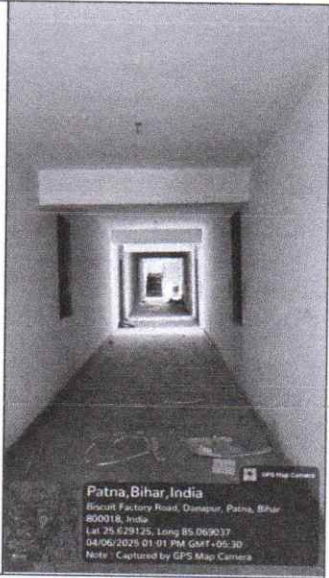

(B)	Photograph of each floor	
-----	--------------------------	---

X. FINANCIAL PROGRESS OF THE PROJECT

S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	4090012997523
2.	Estimated Cost of the Project including land cost at the start of the Project	Rs. 15,93,29,000/-
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	Rs. 12,00,00,000/-
4.	Any Variation in Development Cost which is declared at the start of the Project .	
5.	Amount received during the Quarter	Rs. 21,68,630/-
6.	Actual Cost Incurred during the Quarter	Rs. 1,62,76,579/-
7.	Net amount at end of the Quarter	Rs. 3,82,954/-
8.	Total expenditure on Project till date	Rs. 18,50,63,389/-
9.	Cumulative fund collected till the end of Quarter in question	Rs. 21,67,36,055/-
10.	Cumulative expenditure done till the end of Quarter in question	Rs. 18,50,63,389/-

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED



XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	None
2.	Name of Parties	
3.	No of Execution Cases against this project Case No. Name of Parties	None
4.	No of Suo - Moto cases against this project Case No. Name of Parties	None
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	None
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	01
2.	Agreement for Sale	
3.	No. of possessions given to allottees	
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.



WINSOME INFRASTRUCTURE

Sanjeev Kumar
PARTNER

Signature of Promoter

Name: **Sanjeev Kumar**

Date: 15.04.2025

Date: 11/04/2025

TO WHOMSOEVER IT MAY CONCERN

Sub: Construction work progress report in Quarter **January – March 2024-25** of the Project- **Winsome Empire Block-E**, Biscuit Factory Road, Nasriganj, Danapur, Patna, (Survey Plot No.-614, Tauzi No.- , Thana No.-17, Mauza-Rustampur, Sahpur, Danapur, Patna) On the request of Client, visited the Site on 08/04/2025. It's a Residential Project located at Survey Plot No.-614, Tauzi No.-....., Thana No-17, Mauza-Rustampur, Sahpur, Danapur, Factory Road, Nasriganj, Danapur, Patna, Bihar.

RERA Registration No- **BRERAP2611201700038-7/1250/R-1069/2020**

Developer – **Winsome Infrastructure**

Current Construction Status on Site:

Internal wall plaster completed.
External wall plaster completed.
External Paint work on going.
Internal Paint on going.
Tiles work progress.
Sewerage Chambers completed
Plumbing Work on going
D/W Fitting on going



ARCHITECT
UMA SHANKAR KUMAR
Urban Development & Housing Dept.
Govt. of Bihar
Reg. No. - CA/2011/54023

AR. Uma Shankar Kumar

WINSOME EMPIRE BLOCK-E

Front



Rear



GPS Map Camera

Patna, Bihar, India

Biscuit Factory Road, Danapur, Patna, Bihar
800018, India

Lat 25.629261, Long 85.069470

04/05/2025 10:27 AM GMT+05:30

Note : Captured by GPS Map Camera



Side



GPS Map Camera

Patna, Bihar, India

Biscuit Factory Road, Danapur, Patna, Bihar
800018, India

Lat 25.629539, Long 85.068832

04/05/2025 10:25 AM GMT+05:30

Note : Captured by GPS Map Camera



Maps
