FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending December of 2024 (year

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U74999BR2017PTC035439	Name of Firm	SCB ENGICON PRIVATE LIMITED
Firm Address :	AT NEAR-PETROL PUMP,NEW BYPASS,ALKAPURI,PATNA		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA			
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP02626-2/75/R-1402/2022	Name of Project/Phase of Registered Project	RAM NAGINA ENCLAVE
Name of Promoter	SCB ENGICON PRIVATE LIMITED	Project Address	AT NEAR PETROL PUMP NEW BYPASS ALKAPURI LANE PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	05/12/2024		
Starting date of Project or Phase of the Project	31/05/2022		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	3 YEARS		

SCB ENGICON PVT. LTD.
Rajeev Ram
DIRECTOR

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - FLAT-12	Total Number of Apartments in Landowner's share - FLAT-12
	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.	8 16	5536.00 15064.00	24	1. Booked / Allotted -02 2. Sold-NIL	3. Booked/ Allotted-NIL Sold -NIL
					Percentage of booking 16%	Percentage of booking 0%

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
	24	1. Booked/Allotted -	02
		2. Sold -	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	DIG HG & FS CUM STATE FIRE OFFICER, BIHAR, PATNA		31-01-2019	
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

SCB ENGICON PVT. LTD.
Rajeev Rajan
DIRECTOR

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. P/HARNICHAK/PRN/G+4/142/2020

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	N/A	
3.	Podiums (if any)	N/A	
4.	Plinth	100%	
5.	Stilt Floor	100%	
6.	Slabs of Super Structure	100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100% 100% 100% 100%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	100% 100%	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100% 100% 100%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	100% 100% 100% 100%	

SCB ENGICON PVT. LTD.

DIRECTOR

11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	100% 100% 100% 100% 100%	

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	100%	
2.	Water Supply	YES	100%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	100%	
4.	Storm Water Drains	YES	100%	
5.	Landscaping & Tree Planting	YES	100%	
6.	Street Lighting	NO	N/A	
7.	Community Buildings	NO	N/A	

SCB ENGICON PVT. LTD.

Rajeev Kaur

DIRECTOR

8.	Treatment and Disposal of Sewage and Sullage Water	NO	N/A	
9.	Solid Waste Management & Disposal	YES	100%	
10.	Water Conservation / Rain Water Harvesting	YES	100%	
11.	Energy Management	NO	N/A	
12.	Fire Protection and Fire Safety Requirements	YES	100%	
13.	Closed Parking	YES	100%	
14.	Open Parking	NO	N/A	
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	100%	
16.	Others (Option to Add More)	NO	N/A	

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			


SCB ENGICON PVT. LTD.
Rajeev Kiran
DIRECTOR

8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX.	GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT		
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	



SCB ENGICON PVT. LTD.
DIRECTOR

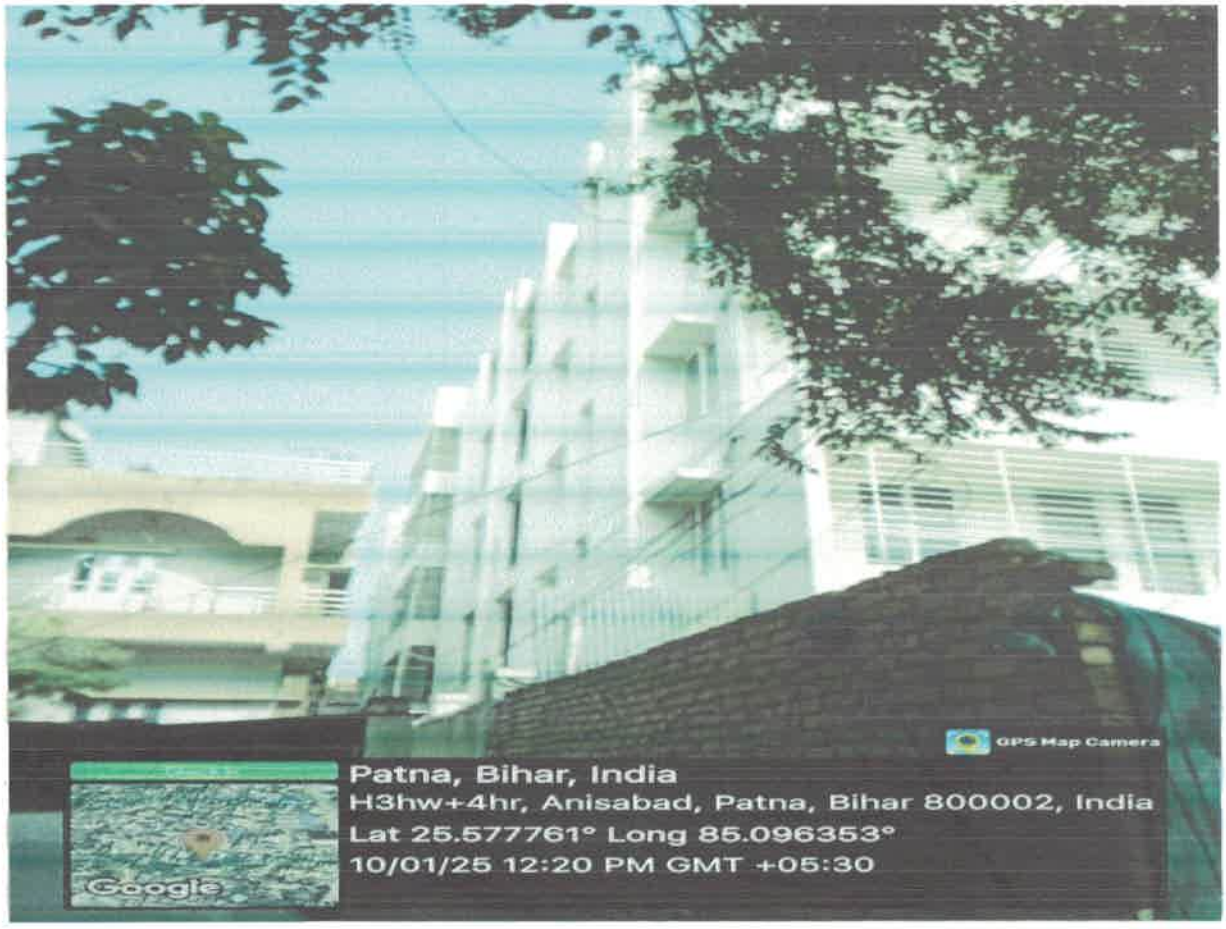



SCB ENGICON PVT. LTD.

DIRECTOR



X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	2078102000005814
2.	Estimated Cost of the Project including land cost at the start of the Project	9,01,00,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	4,15,00,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	18,50,000=00
6.	Actual Cost Incurred during the Quarter	22,25,352=96
7.	Net amount at end of the Quarter	4,262=30
8.	Total expenditure on Project **till date**	1,74,25,753=04
9.	Cumulative fund collected till the end of Quarter in question	1,89,45,202=00
10.	Cumulative expenditure done till the end of Quarter in question	1,74,25,753=04

SCB ENGICON PVT. LTD.
Rajeev Ranjan
DIRECTOR

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART
Weather the project in progress is as per time schedule or lagging behind?

XIV UNITS ALLOCATION DETAILS		
Total Number of sanctioned apartments 1 BHK- 2 BHK, -08 3 BHK-16 4 BHK- Shop- Bungalow - Plot etc	Details of allotment made so far with Flat number/ Bungalow - Plot etc FLAT. NO. 302 3BHK 402 3BHK	Cancellation of flat allotment, If any with Flat number/ Bungalow – Plot etc
XV. BROCHURE /Prospectus		

SCB ENGICON PVT. LTD.

Rajeev Rajan

DIRECTOR

XVI Grievance Redressal Officer

Name : RAJEEV RANJAN

Contact No : 8294631701

Email id : rajeevranjansepl@gmail.com

Address : AT NEAR-PETROL PUMP, NEW BYPASS,ALKAPURI,PATNA

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

SCB ENGICON PVT. LTD.

Rajeev Ran

DIRECTOR

Signature of Promoter

Name: Rajeev Ranjan

Date:

FORM No. 1
[See Regulation 3]

ARCHITECT'S CERTIFICATE

(To be submitted at the time of Registration of Ongoing Project and for withdrawal of Money from Designated Account)

Date 10/01/25

To,
The S.C.B Engicon Pvt Ltd. (Name & Address of Promoter),
Director - Rajeev Ranjan
RERA NO — BRERAP02626-2/75/R-1402/2022

Subject: Certificate of Percentage of Completion of Construction Work of---------- No. of Building(s)/---------- Wing(s) of the---------- Phase of the Project [Bihar RERA Registration Number] situated on the Plot bearing C.N. No/CTS No./Survey No./ Final Plot No. 321, 350 demarcated by its boundaries (latitude and longitude of the end points) ---------- to the North ---------- to the South ----------to the East ---------- to the West of Division ---------- village Harnichak Block Phulwari Sharif District Patna PIN ---------- admeasuring 949.03 sq.mts. area being developed by [Promoter's Name] S.C.B. Engicon Pvt. Ltd.

Sir,
I/ We Pawan Kumar have undertaken assignment as Architect /Licensed Surveyor of certifying Percentage of Completion of Construction Work of the ---------- Building(s)/----------Wing(s) of the ---------- Phase of the Project, situated on the plot bearing C.N. No/CTS No./Survey No./Final Plot No. 321, 350 - of Division ---------- Village Harnichak Block Phulwari Sharif District Patna PIN ---------- admeasuring 949.03 sq.mts.area being developed by [Promoter's Name] SCB Engicon Pvt Ltd.

1. Following technical professionals are appointed by Owner / Promoter:—

(i) M/s/Shri/Smt. Pawan Kumar as L.S. / Architect;
(ii) M/s /Shri / Smt. Amrendra Kumar as Structural Consultant
(iii) M/s /Shri / Smt. Manish Kumar as MEP Consultant
(iv) M/s /Shri / Smt. Ranjeet Kumar as Site Supervisor

Based on Site Inspection, with respect to each of the Building/Wing of the aforesaid Real Estate Project, I certify that as on the date of this certificate, the Percentage of Work done for each of the building/Wing of the Real Estate Project as registered vide number under _____ Bihar RERA is as per table A herein below. The percentage of the work executed with respect to each of the activity of the entire phase is detailed in Table B.

Ar. Pawan Kumar
UDHD Reg. No.- CA/2008/43276

Table-A

Building/ Wing number ..... (to be prepared separately for each building / wing of the project)

S. No.	Task/Activity	Percentage of Actual Work Done	Projected date of completion (DD/MM/YYYY)
1.	Excavation(if any)	100%.	
2.	Basements(if any)	N/A	
3.	Podiums(if any)	N/A	
4.	Plinth	100%.	
5.	Stilt Floor	100%.	
6.	Slabs of Super Structure	100%.	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100%.	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	100%.	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100%.	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	100%.	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/splint protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other	100%.	

Yours Faithfully,

Ar. Pawan Kumar

UDHD Reg. No.- CA/2008/43276

Signature & Name (IN BLOCK LETTERS) of L.S/ Architect

(Registration No./License No. .....)

TABLE B

Internal and External Development Works in respect of the entire Registered Phase.

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Projected date of completion (dd/mm/yyyy)
1.	Internal Roads &Footpaths	yes	100%.	
2.	Water Supply	yes	100%.	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	yes	100%.	
4.	Storm Water Drains	yes	100%.	
5.	Landscaping & Tree Planting	yes	100%.	
6.	Street Lighting	NO	N/A	
7.	Community Buildings	NO	N/A	
8.	Treatment and Disposal of Sewage and Sullage Water	NO	N/A	
9.	Solid Waste Management & Disposal	NO	N/A	
10.	Water Conservation/Rain Water Harvesting	yes	100%.	
11.	Energy Management	NO	N/A	
12.	Fire Protection and Fire Safety Requirements	yes	100%.	
13.	Electric Meter Room	yes	100%.	
14.	Any Other Amenities	NO	N/A	

Ar. Pawan Kumar
UDHD Reg. No.- CA/2008/43276

R.G.S & ASSOCIATES
Chartered Accountants

komalagrawal.ca@gmail.com
agrawal.komal@hotmail.com
Mob. No. : 9006668233

Annexure A
List of Extra/Additional Items executed with Cost
(which were not part of the original Estimate of Total Cost)

FORM No. 3

[See Regulation 3]
CHARTERED ACCOUNTANT'S CERTIFICATE
(FOR REGISTRATION OF A PROJECT AND SUBSEQUENT WITHDRAWAL OF MONEY)
Cost of Real Estate Project : Ram Nagina Enclave
Bihar RERA Registration Number:
BRERAP02626-2/75/R-142222

Sr. No.	Particulars	Amount (₹)
1.i	**Land Cost :**	**Estimated Incurred**
	a. Acquisition Cost of Land or Development Rights, lease Premium, lease rent, interest cost incurred or payable on Land Cost and legal cost.	
	b. Amount of Premium payable to obtain development rights, FSI, additional FSI, fungible area, and any other incentive under DCR from Local Authority or State Government or any Statutory Authority.	
	c. Acquisition cost of TDR (if any)	
	d. Amounts payable to State Government or competent authority or any other statutory authority of the State or Central Government, towards stamp duty, transfer charges, registration fees etc; and	- 8,72,020=00
	e. Land Premium payable as per annual statement of rates (ASR) for redevelopment of land owned by public authorities.	
	f. Under Rehabilitation Scheme:	
	(i) Estimated construction cost of rehab building including site development and infrastructure for the same as certified by Engineer.	
	(ii) Actual Cost of construction of rehab building incurred as per the books of accounts as verified by the CA.	
	Note :(for total cost of construction incurred, Minimum of (i) or (ii) is to be considered).	
	(iii) Cost towards clearance of land of all or any encumbrances including cost of removal of legal/illegal occupants, cost for providing	

Pallavi Apartment 5th Floor
Flat No.-502, Nala Road, Patna - 800 003

temporary transit accommodation or rent in lieu of Transit Accommodation, overhead cost,

(iv) Cost of ASR linked premium, fees, charges and security deposits or maintenance deposit, or any amount whatsoever payable to any authorities towards and in project of rehabilitation.

Sub-Total of Land Cost 8,72,020/-

Sr.No.	Particulars	Amount (₹) Estimated	Incurred
ii	**Development Cost/ Cost of Construction :**		
	a. (i) Estimated Cost of Construction as certified by Engineer.	4,15,00,000/-	
	(ii) Actual Cost of construction incurred as per the books of accounts as verified by the CA.		4,50,00,000/-
	Note : (for adding to total cost of construction incurred, Minimum of (i) or (ii) is to be considered).		
	(iii) On-site expenditure for development of entire project excluding cost of construction as per (i) or (ii) above, i.e. salaries, consultants fees, site overheads, development works, cost of services (including water, electricity, sewerage, drainage, layout roads etc.), cost of machineries and equipment including its hire and maintenance costs, consumables etc. All costs directly incurred to complete the (i) construction of the entire phase of the project registered.	26,27,980/-	
	b. Payment of Taxes, cess, fees, charges, premiums, interest etc. to any Statutory Authority.		
	c. Principal sum and interest payable to financial institutions, scheduled banks, non-banking financial institution (NBFC) or money lenders on construction funding or money borrowed for construction;		
	Sub-Total of Development Cost		4,50,00,000/-

2.	Total Estimated Cost of the Real Estate Project [1(i) + 1(ii)] of Estimated Column.	4,15,00,000/-
3	Total Cost Incurred of the Real Estate Project [1(i) + 1(ii)] of Incurred Column.	4,50,00,000/-
4	% completion of Construction Work (as per Project Architect's Certificate)	100.1.
5	Proportion of the Cost incurred on Land Cost and Construction Cost to the Total Estimated Cost. (3/2)	35,00,000/-
6	Amount Which can be withdrawn from the Designated Account. **Total Estimated Cost * Proportion of cost incurred (Sr. number 2 * Sr. number 5)**	
7	Less: Amount withdrawn till date of this certificate as per the Books of Accounts and Bank Statement.	
8	Net Amount which can be withdrawn from the Designated Bank Account under this certificate.	

This certificate is being issued for RERA compliance for the Company [Promoter's Name] and is based on the records and documents produced before me and explanations provided to me by the management of the Company.

Yours Faithfully,
For RGS and Associates

Komal Agrawal

RGS & ASSOCIATES * PATNA * Chartered Accountants *

Partner

Signature of Chartered Accountant,

(Membership Number - 063579)

Name : KOMAL AGRAWAL

(ADDITIONAL INFORMATION FOR ONGOING PROJECTS)

Sr. No.	Particulars	Amount (₹) Estimate Incurred
1.	Estimated Balance Cost to Complete the Real Estate Project (Difference of Total Estimated Project cost less Cost incurred) (calculated as per the Form IV)	
2.	Balance amount of receivables from sold apartments (as per Annexure A to this certificate(as certified by Chartered Accountant as verified from the records and books of Accounts)	
3.	(i) Balance Unsold area (to be certified by Management and to be verified by CA from the records and books of accounts) (ii) Estimated amount of sales proceeds in respect of unsold apartments (calculated as per ASR multiplied to unsold area as on the date of certificate, to be calculated and certified by CA)as per Annexure A to this certificate	
4.	Estimated receivables of ongoing project. Sum of 2 + 3 (ii)	
5.	Amount to be deposited in Designated Account – 70% or 100% If 4 is greater than 1, then 70 % of the balance receivables of ongoing project will be deposited in designated Account If 4 is lesser than 1, then 100% of the of the balance receivables of ongoing project will be deposited in designated Account	

This certificate is being issued for RERA compliance for the Company [Promoter's Name] and is based on the records and documents produced before me and explanations provided to me by the management of the Company.

Yours Faithfully,
For RGS and Associates



Partner

Signature of Chartered Accountant,

(Membership Number - 063579)

Name : KOMAL AGRAWAL

Annexure A

Statement for calculation of Receivables from the Sales of the Ongoing Real Estate Project

Sold Inventory

Sr. No.	Flat No.	Carpet Area (in sq.mts.)	Unit Consideration as per Agreement/Letter of Allotment	Received Amount	Balance Receivable
(1)	(2)	(3)	(4)	(5)	(6)

(Unsold Inventory Valuation)
Ready Reckoner Rate as on the date of Certificate of the Residential/Commercial premises Rs. _____ per sq.mts.

Sr.No.	Flat No.	Carpet Area (in sq.mts.)	Unit Consideration as per Read Reckoner
01	02	03	04

FORM No. 2
[See Regulation 3]

ENGINEER'S CERTIFICATE

(To be submitted at the time of Registration of Ongoing Project and for withdrawal of Money from Designated Account- Project wise)

Date : 10/01/25

To,
The SCB Engicon Pvt. Ltd (Name & Address of Promoter),
Director - Rajeev Ranjan
Rera No. - BRERAP02626-2/75/R-1402/2022

Subject : Certificate of Cost Incurred for Development of [Project Name]_____ for Construction of _____ building(s)/_____Wing(s) of the _____Phase (Bihar RERA Registration Number) situated on the Plot bearing Khesra No/ Khata No./Thana No./ Tauzi No../C.N.No./CTSNo./SurveyNo./Final Plot No. 321, 350 demarcated by its boundaries (latitude and longitude of the end points) _____to the North_____to the South _____to the East _____to the West of Division _____ Village Hasnichak Block Phulwari Sharif District _____ PIN _____admeasuring 949.03 sq.mts. area being developed by [Promoter] SCB Engicon Pvt. Ltd

Ref: Bihar RERA Registration Number BRERAP02626-2/75/R-1402/2022

Sir,

I/ We Amrendra Kumar have undertaken assignment of certifying Estimated Cost for the Subject Real Estate Project proposed to be registered under Bihar RERA, being _____Building(s)/ _____ Wing(s) of the _____ Phase situated on the plot bearing C.N. No./CTS No./Survey No./ Final Plot No. 321, 350 of Division _____ Village Hasnichak Taluka _____ District Patna PIN _____admeasuring 949.03 sq.mts. area being developed by [Owner/Promoter]

1. Following technical professionals are appointed by Owner / Promoter :—

(i) M/s /Shri/Smt Pawan Kumar as L.S. / Architect ;
(ii) M/s /Shri/Smt Amrendra Kumar as Structural Consultant
(iii) M/s /Shri/Smt Manish Kumar as MEP Consultant
(iv) M/s /Shri/Smt Ranjeet Kumar as Quantity Surveyor *

2. We have estimated the cost of the completion to obtain Occupancy Certificate / Completion Certificate, of the Civil, MEP and Allied works, of the Building(s) of the project. Our estimated cost calculations are based on the Drawings/plans made available to us for the project under reference by the Developer and Consultants and the Schedule of items and quantity for the entire work as calculated by _____ Quantity Surveyor* appointed by Developer/Engineer, and the assumption of

the cost of material, labour and other inputs made by developer, and the site inspection carried out by us.

3. We estimate Total Estimated Cost of completion of the building(s) of the aforesaid project under reference as Rs. _____(Total of Table A and B). The estimated Total Cost of project is with reference to the Civil, MEP and allied works required to be completed for the purpose of obtaining Occupancy Certificate / Completion Certificate for the building(s) from the _____ being the Planning Authority under whose jurisdiction the aforesaid project is being implemented.

4. The Estimated Cost Incurred till date is calculated at Rs. _____(Total of Table A and B). The amount of Estimated Cost incurred is calculated on the base of amount of Total Estimated Cost.

5. The Balance cost of Completion of the Civil, MEP and Allied works of the Building(s) of the subject project to obtain Occupancy Certificate / Completion Certificate from_____ (planning Authority) is estimated at Rs. _____(Total of Table A and B).

6. I certify that the Cost of the Civil, MEP and allied work for the aforesaid Project as completed on the date of this certificate is as given in Table A and B below :

TABLE A

Building /Wing bearing Number_____ or called _____
(to be prepared separately for each Building /Wing of the Real Estate Project)

Sr. No.	Particulars	Amounts
1	Total Estimated cost of the building/wing as on _____ date of Registration is	Rs. 4.15 Cr.
2	Cost incurred as on _____ (based on the Estimated cost)	Rs. 4.5 Cr.
3	Work done in Percentage (as Percentage of the estimated cost)	% 100 %
4	Balance Cost to be Incurred (Based on Estimated Cost)	Rs. 0 /-
5	Cost Incurred on Additional /Extra Items as on _____not included in the Estimated Cost (Annexure A)	Rs. 0.35 Cr.

TABLE B

(To be prepared for the entire registered phase of the Real Estate Project)

Sr. No.	Particulars	Amounts
1	Total Estimated cost of the Internal and External Development Works including amenities and Facilities in the layout as on _____ date of Registration is	10 Lakh Rs.
2	Cost incurred as on _____ (based on the Estimated cost).	Rs. 10 LAKH
3	Work done in Percentage (as Percentage of the estimated cost).	100/. %
4	Balance Cost to be Incurred (Based on Estimated Cost).	Rs. 0
5	Cost Incurred on Additional /Extra Items as on _____ not included in the Estimated Cost (Annexure A).	Rs. NO

Yours Faithfully,

Signature of Engineer.

Er. Amrendra Kumar
(Structural Engineer)
Reg. No. BR/UDHD/SE/230129

* Note :

1. The scope of work is to complete entire Real Estate Project as per drawings approved from time to time so as to obtain Occupancy Certificate / Completion Certificate.
2. (*) Quantity survey can be done by office of Engineer or can be done by an independent Quantity Surveyor, whose certificate of quantity calculated can be relied upon by the Engineer. In case of independent Quantity Surveyor being appointed by Developer, the name has to be mentioned at the place marked (*) and in case quantity are being calculated by office of Engineer, the name of the person in the office of Engineer, who is responsible for the quantity calculated should be mentioned at the place marked (*).
3. The estimated cost includes all labour, material, equipment and machinery required to carry out entire work.
4. As this is an estimated cost, any deviation in quantity required for development of the Real Estate Project will result in amendment of the cost incurred / to be incurred.
5. All components of work with specifications are indicative and not exhaustive
