QUARTERLY PROGRESS REPORT FOR RERA BIHAR

Apr - Jun, 2021

ABSTRACT

This report documents and describes the updates on project work progress, with updates on status of financials, bookings in the project along with status of the approvals for the quarter.

PROJECT NAME

SAI SAMPAN AMITA USHA PALACE

PROMOTER NAME

SAISAMPAN GRIHSHOBHA PVT. LTD.

RERA REGISTRATION NO.

BRERAP63441-1/900/R-621/2019

Report Drafted by Limpid Construction Consulting LLP

PROJECT QUARTERLY PROGRESS STATUS

Quarter: Apr - Jun, 2021

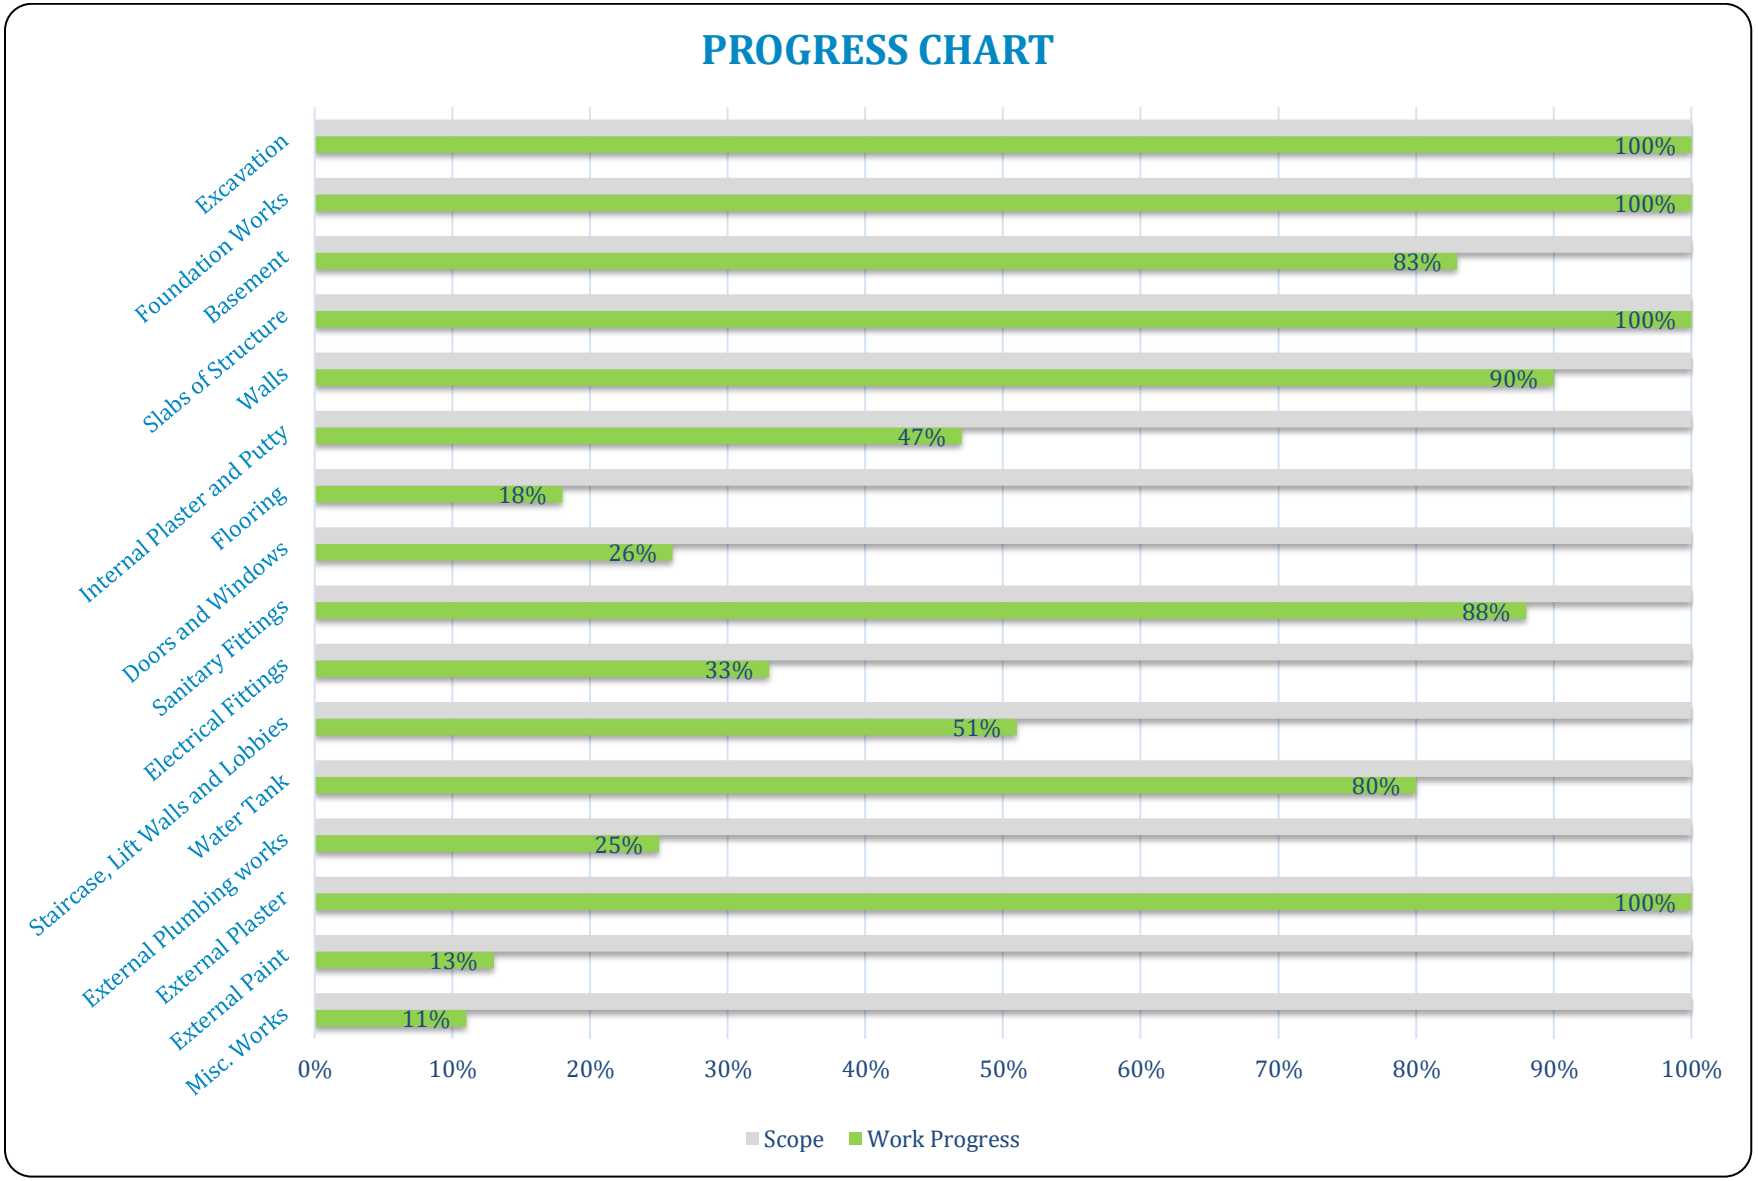
Project Description: *A residential building project consisting of B+G+6 floors having 44 no. of flats.*

Progress Update of each Block/Wing separately

S. No.	Task/Activity	Applicable (Yes/No)	Percentage of Work Done	Remarks
1	Excavation	Yes	100%	Overall excavation works complete.
2	Foundation Works	Yes	100%	Overall Foundation Works Completed.
3	Basement	Yes	83%	Basement Retaining wall &ramp construction completed. Soling, PCC, and finishing works also completed.
4	Slabs of structure	Yes	100%	Overall Slab Casting Completed.
5	Walls	Yes	90%	Brickwork under progress in full swing and near about to completion.
6	Internal Plaster& Putty	Yes	47%	Internal plastering and Putty work under progress in full swing.
7	Flooring inside units and common areas	Yes	18%	Flooring work inside units under progress in full swing.
8	Doors and Window to each of unit and common areas	Yes	26%	Door frame and balcony handrail fixing under progress and window work pending.
9	Sanitary fittings within the unit including water proofing and plumbing	Yes	88%	SWR, CPVC, waterproofing, Koba work complete and Indian WC Installation under progress in full swing.
10	Electrical fitting within the unit	Yes	33%	Conduit Jhiri, Pipe laying, MS box laying under progress.
11	Staircase, lift walls and lobbies at each floor	Yes	51%	Lift structure, Looby Structure work complete &

Progress Update of each Block/Wing separately

S. No.	Task/Activity	Applicable (Yes/No)	Percentage of Work Done	Remarks
				Staircase structure complete upto Terrace.
12	Water tank	Yes	80%	Water tank Construction under progress.
13	External Plumbing works and completion of terrace with waterproofing of the building if specified.	Yes	25%	External plumbing work under progress.
14	External Plaster	Yes	100%	Overall external plastering work complete.
15	External Paint	Yes	13%	Back elevation putty work complete and front elevation under progress.
16	Installation of lifts water pumps, firefighting fittings as NOC, Electricals fittings to the common areas, electro mechanic equipment, finishing to the entrance lobby, plinth protection, paving of areas, compound walls and other requirements as may be required to obtain completion/occupancy certificate. (Misc. Works)	Yes	11%	Submersible pump has been installed.


PROGRESS CHART
Excavation
Foundation Works
Basement
Slabs of Structure
Walls
Internal Plaster and Putty
Flooring
Doors and Windows
Sanitary Fittings
Electrical Fittings
Staircase, Lift Walls and Lobbies
Water Tank
External Plumbing works
External Plaster
External Paint
Misc. Works
100%
100%
83%
100%
90%
47%
18%
26%
88%
33%
51%
80%
25%
100%
13%
11%
0%
10%
20%
30%
40%
50%
60%
70%
80%
90%
100%
Scope
Work Progress

Progress Updatefor Common Areas, Facilities and Amenities in the Project

S. No.	Description	Applicable (Yes/No)	Percentage of Work Done	Remarks
1	Compound Walls	Yes	50%	Compound wall construction 70% complete, finishing works yet to start.
3	Water supply	Yes	50%	Boring works complete and supply pipes installation balance.

Update on number and types of flats/plots booked during the quarter

S.No	Unit Type	Total No. of Units in builder's Share	No. of Flats / Plot Booked				No. of Garages/ Covered Parking Booked			
			Opening Balance	Booked in the quarter	Cancelled in the quarter	Closing Balance	Opening Balance	Booked in the quarter	Cancelled in the quarter	Closing Balance
1	2 BHK	6	6	0	0	6	6	0	0	6
2	3 BHK	16	16	0	0	16	16	0	0	16

Status of financials in the project up to 30th June, 2021

S.No.	Description	Amount (in Rs.)
1	Amounts received from allottees against booking of units(for builder's share) (excl GST)	6,78,30,230.03/-
2	Expenditure done towards completion of project	5,43,40,521.00/-
3	Balance in Designated Bank A/c as on this quarter end	8,31,244.62/-

Note- Audited financials might vary. These values do not reflect the audited figures

Status of Approvals

A. Approval Received

S. No.	Description	Date of Receipt
1	Provisional Fire Clearance	10.01.19
3	Sanctioning of Building Plan	15.02.19
4	RERA Registration	14.05.19

B. Approval Applied

S. No.	Description	Expected Date
NA	NA	NA

C. Approvals to be applied

S. No.	Description	Expected Date of application
NA	NA	NA

D. Modifications amendments or revisions, if any, issued by competent authority with regard to any sanctioned plans, layout plans, specifications, license, permit or approval for the project - NA

Project Site Photographs



