FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024

I. PARTICULARS OF PROMOTERS

Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U70109BR2021PTC054969	Name of Firm	GENX BUILDCON PRIVATE LIMITED
Firm Address :	602, 6th Floor, GENX ICON, MANGALAM COLONY MORE, NEAR RPS MORE, BAILEY ROAD, PATNA		
Total Experience of promoter in Real Estate sector	07 Years		
Total Experience in Real Estate after Implementation of RERA	06 Months		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT

Project Registration Number	BRERAP85440-1/96/R-1742/2024	Name of Project/Phase of Registered Project	GENX BUDDHA
Name of Promoter	GENX BUILDCON PRIVATE LIMITED	Project Address	GAYA-BODH GAYA ROAD, HARIO NEAR AIMS, GAYA , MAUJA - HARIO PLOT NO -152 DISTRICT – GAYA
Name of Co-promoter	N/A		
Project Registration is valid up to	26-01-2029		
Starting date of Project or Phase of the Project			
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	26-01-2029		

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type	Carpet Area	Total Number of	Total Number of Apartments in	Total Number of Apartments in

GENX BUILDCON PVT. LTD.

Rakesh Ranjan

DIRECTOR

	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow - 6. Plot etc.			sanctioned apartments 25 Flat 01 Shop	Promoter's share - 13 Flat 1. Booked / Allotted - NIL 2. Sold-	Landowner's share - 12 Flat +01 Shop 3. Booked/ Allotted - NIL
					Percentage of booking NIL	Percentage of booking NIL

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.
Association of allottees name
Details of allottees - Name, Address, Email id (if any), contact number. These details may not be available to common people

Name	Address	contact number	Email id (If any)

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted -	
		2. Sold -	

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	State Fire Officer		10.01.2024	
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	Airport Authority		10.10.23	
5.	Other Approval(s), if any, required for the Project.	N/A			

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. _____(To beaded for each Building / Wing)

GENX BUILDCON PVT. LTD.
Rakesh Ranjan.
DIRECTOR

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	0%	
2.	Basements (if any)		
3.	Podiums (if any)		
4.	Plinth	0%	
5.	Stilt Floor	0%	
6.	Slabs of Super Structure	0%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	0%	

GENX BUILDCON PVT. LTD.

Rakesh Ranjan

DIRECTOR

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths		0%	
2.	Water Supply		0%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)		0%	
4.	Storm Water Drains			
5.	Landscaping & Tree Planting		0%	
6.	Street Lighting		0%	
7.	Community Buildings			
8.	Treatment and Disposal of Sewage and Sullage Water		0%	
9.	Solid Waste Management & Disposal		0%	
10.	Water Conservation / Rain Water Harvesting		0%	
11.	Energy Management		0%	
12.	Fire Protection and Fire Safety Requirements		0%	
13.	Closed Parking		0%	
14.	Open Parking			
15.	Electrical Meter Room, Sub-Station, Receiving Station		0%	
16.	Others (Option to Add More)			

GENX BUILDCON PVT. LTD.

Ratish Ranjan

DIRECTOR

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT				
		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT			
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	
	3.	Side Elevation	
(B)		Photograph of each floor	

GENX BUILDCON PVT. LTD.
Rakesh Ranjan.
DIRECTOR



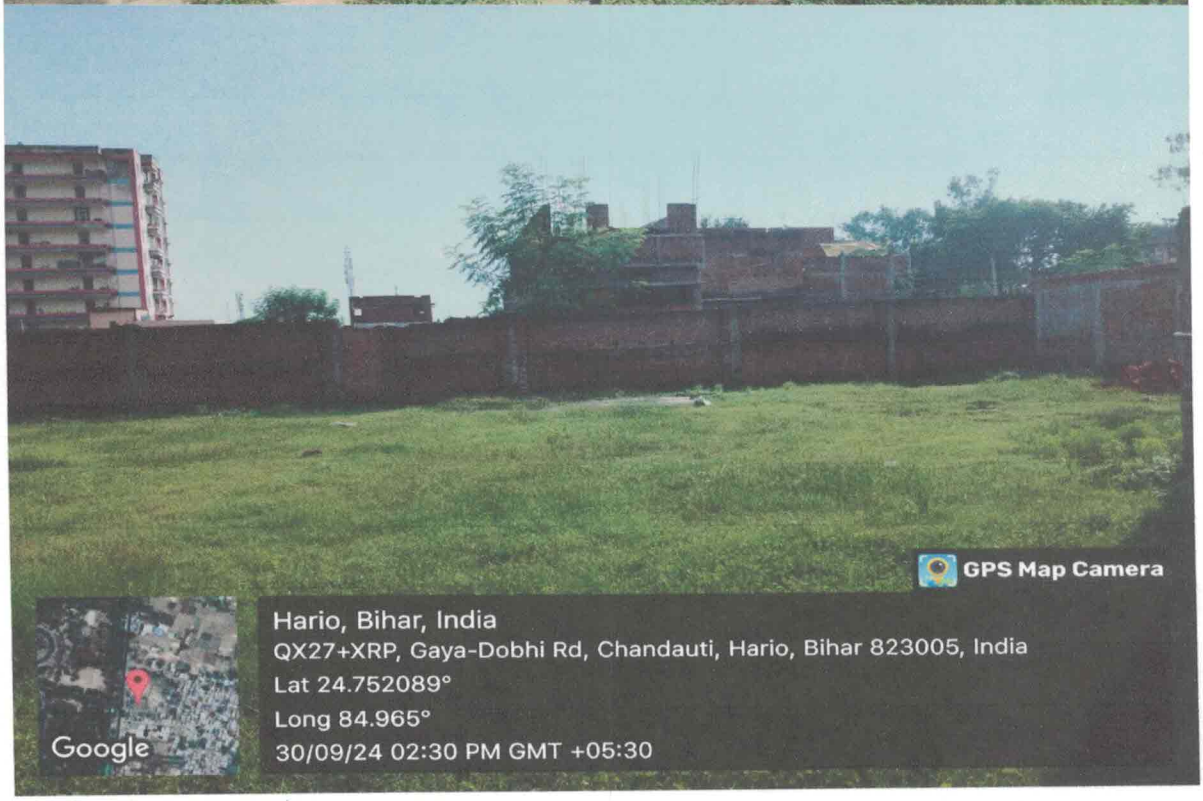

X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	333905001899
2.	Estimated Cost of the Project including land cost at the start of the Project	6,70,19,136=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	6,15,32,136=00

GENX BUILDCON PVT. LTD.
Rakesh Ranjan.
DIRECTOR

4.	Any Variation in Development Cost which is declared at the start of the Project .	NO
5.	Amount received during the Quarter	NIL
6.	Actual Cost Incurred during the Quarter	NIL
7.	Net amount at end of the Quarter	NIL
8.	Total expenditure on Project **till date**	NIL
9.	Cumulative fund collected till the end of Quarter in question	NIL
10.	Cumulative expenditure done till the end of Quarter in question	NIL

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	N/A
2.	Name of Parties	N/A
3.	No of Execution Cases against this project Case No. Name of Parties	N/A
4.	No of Suo - Moto cases against this project Case No. Name of Parties	N/A
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	N/A
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	N/A
2.	Agreement for Sale	N/A
3.	No. of possessions given to allottees	
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

XIV UNITS ALLOCATION DETAILS

GENX BUILDCON PVT. LTD.

Rakesh Ranjan.

DIRECTOR

Total Number of sanctioned apartments 1 BHK - 2 BHK, - 3 BHK 4 BHK - Shop- Bungalow - Plot etc	Details of allotment made so far with Flat number/ Bungalow - Plot etc No Booking	Cancellation of flat allotment, If any with Flat number/ Bungalow – Plot etc N/A
XV. BROCHURE /Prospectus		
XVI Grievance Redressal Officer **Name :** KUNAL KUMAR **Contact No :**9939255166 **Email id :** genxbuildcon2024@gmail.com **Address :** 602, 6th Floor, GENX ICON, MANGALAM COLONY MORE, NEAR RPS MORE, BAILEY ROAD, PATNA		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

GENX BUILDCON PVT. LTD.
Rakesh Ranjan.
DIRECTOR

Signature of Promoter

Name:

Date:
