FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending December of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U70109BR2019PTC044035	Name of Firm	SHRISHTY CITY DEVELOPERS PRIVATE LIMITED
Firm Address :	C/O- BIRENDRA KUMAR, MURLICHAK, KHAJPURA, PATNA		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA	03 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP95456-1/103/R-1415/2022	Name of Project/Phase of Registered Project	SHRISHTY GOLD AVENUE
Name of Promoter	SHRISHTY CITY DEVELOPERS PRIVATE LIMITED	Project Address	OPPOSITE CERAMIC JUNCTION, 70 FEET BPCL ROAD, DASRATHA, PATNA 800002
Name of Co-promoter	N/A		
Project Registration is valid up to	20/05/2027		
Starting date of Project or Phase of the Project	21/06/2022		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	19/04/2025		

SHRISHTY CITY DEVELOPERS PVT. LTD.

Dipesh Diwakar

DIRECTOR

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - FLAT-33	Total Number of Apartments in Landowner's share - FLAT-32
BLOCK-A & BLOCK-B	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.	35 30	27705.00 24765.00	BLOCK-A-35 BLOCK-B-30	1. Booked / Allotted – BLOCK-A-07 BLOCK-04 2. Sold-NIL	3. Booked/ Allotted-NIL Sold -NIL
					Percentage of booking 33.33%	Percentage of booking 0%

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
BLOCK-A & BLOCK-B	65	1. Booked/Allotted -	11
		2. Sold -	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	DIRECTOR-CUM-STATE FIRE OFFICER, BIHAR, PATNA		05-03-2022	
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

SHRISHTY CITY DEVELOPERS PVT. LTD.

Dipesh Diwakar

DIRECTOR

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. PMAA/PRN/PAKARI VISHUNPUR/BEUR/BLOCKA&B-G+5/11/2022

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3) BLOCK-A	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	NO	
3.	Podiums (if any)	NO	
4.	Plinth	100%	
5.	Stilt Floor	100%	
6.	Slabs of Super Structure	20%	30/09/2025
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0% 0% 0% 0%	25/08/2026 25/09/2026 25/09/2026 25/10/2026
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0% 0%	30/11/2026 30/11/2026
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	10% 10% 0%	30/11/2026 30/11/2026 30/12/2026
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0% 0% 0% 0%	30/10/2026 30/10/2026 30/09/2026 28/02/2026

SHRISHTY CITY DEVELOPERS PVT. LTD.

Dipesh Diwakar

DIRECTOR

11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	0% 100% 0% 0% 0% NIL	30/12/2026 30/10/2026 30/09/2026 30/12/2026

1. Plan Case No.PMAA/PRN/PAKARI VISHUNPUR/BEUR/BLOCKA&B-G+5/11/2022

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3) BLOCK-B	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	NO	
3.	Podiums (if any)	NO	
4.	Plinth	100%	
5.	Stilt Floor	100%	
6.	Slabs of Super Structure	100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	80% 80% 0% 0%	30/05/2025 30/07/2025 30/0/2026 30/01/2026
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	30% 30%	30/05/2026 30/05/2026

SHRISHTY CITY DEVELOPERS PVT. LTD.

Dipesh Diwakar

DIRECTOR

9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100% 100% 100%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	50% 80% 10% 0%	30/11/2025 30/11/2025 30/05/2026 30/05/2025
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	0% 100% 0% 20% 0% 0%	30/05/2025 30/11/2026 30/11/2025 30/12/2026

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	30/03/2027
2.	Water Supply	YES	20%	30/01/2027
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	30/12/2026

SHRISHTY CITY DEVELOPERS PVT. LTD.

Dipesh Diwakar

DIRECTOR

4.	Storm Water Drains	YES	0%	30/12/2026
5.	Landscaping & Tree Planting	YES	0%	30/04/2027
6.	Street Lighting	YES	0%	30/03/2027
7.	Community Buildings	NO	N/A	
8.	Treatment and Disposal of Sewage and Sullage Water	YES	0%	30/12/2026
9.	Solid Waste Management & Disposal	YES	0%	30/01/2027
10.	Water Conservation / Rain Water Harvesting	YES	0%	30/03/2027
11.	Energy Management	YES	0%	30/03/2027
12.	Fire Protection and Fire Safety Requirements	YES	0%	30/11/2026
13.	Closed Parking	YES	0%	28/02/2027
14.	Open Parking	NO	N/A	
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	30/04/2027
16.	Others (Option to Add More)	NO		

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			


SHRISHTY CITY DEVELOPERS PVT. LTD.

Dipesh Diwakar


DIRECTOR


5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX.	GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT		
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

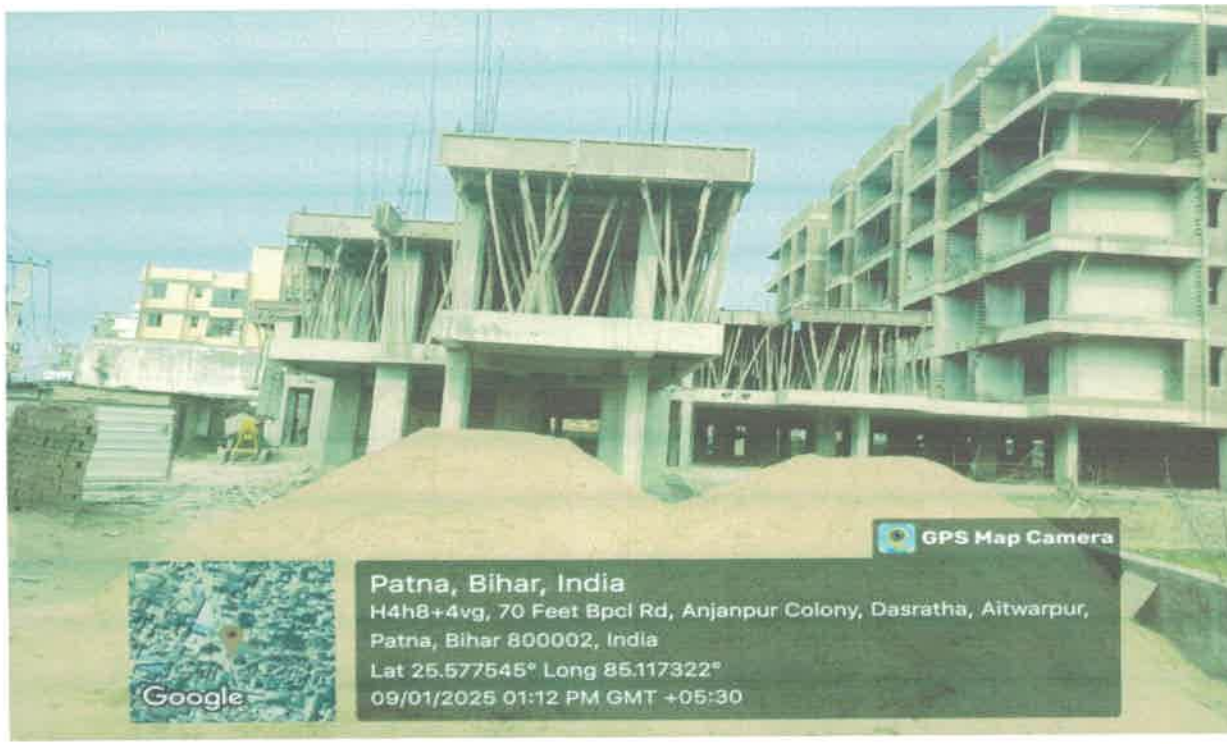

SHRISHTY CITY DEVELOPERS PVT. LTD.
Dipesh Diwakar
DIRECTOR

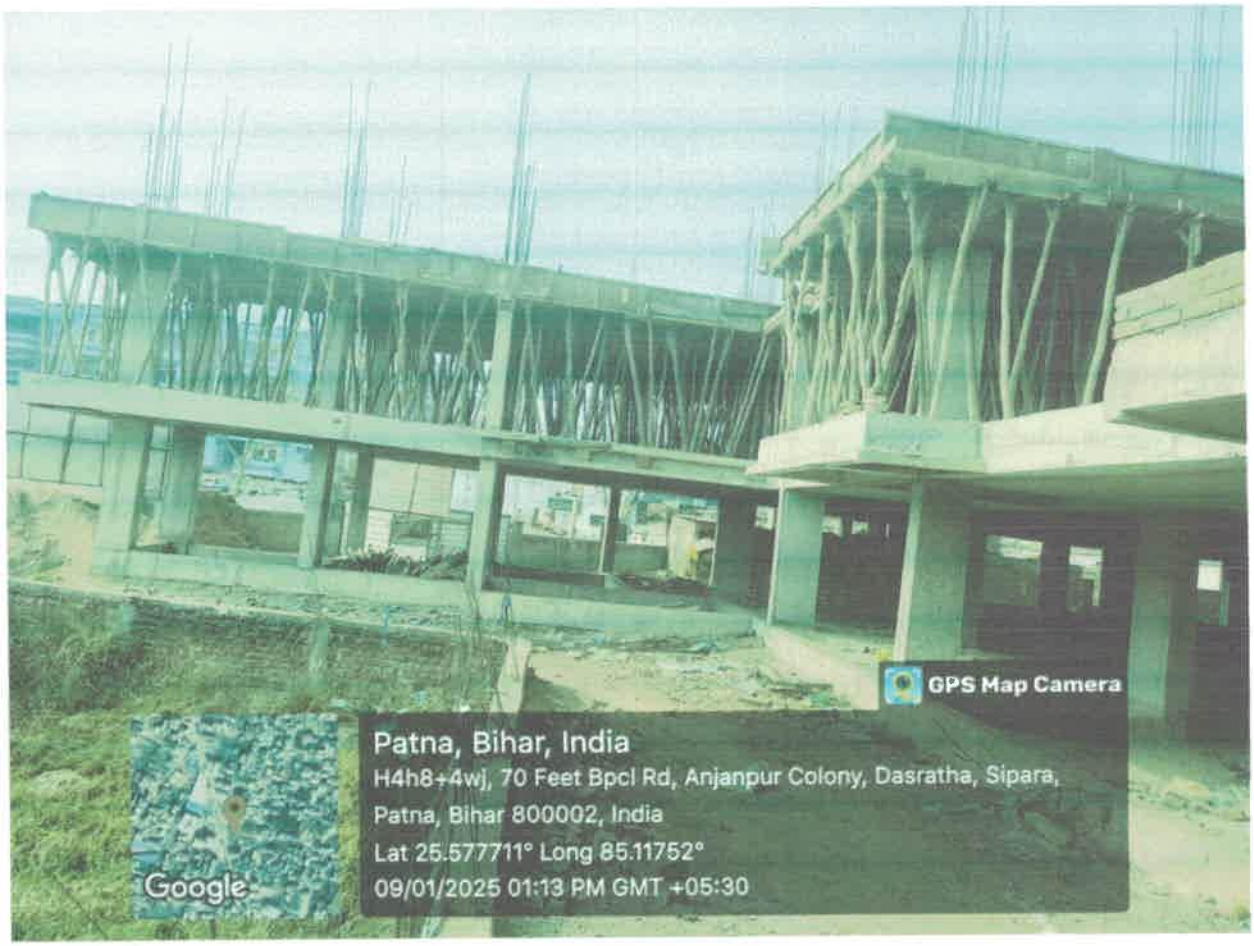

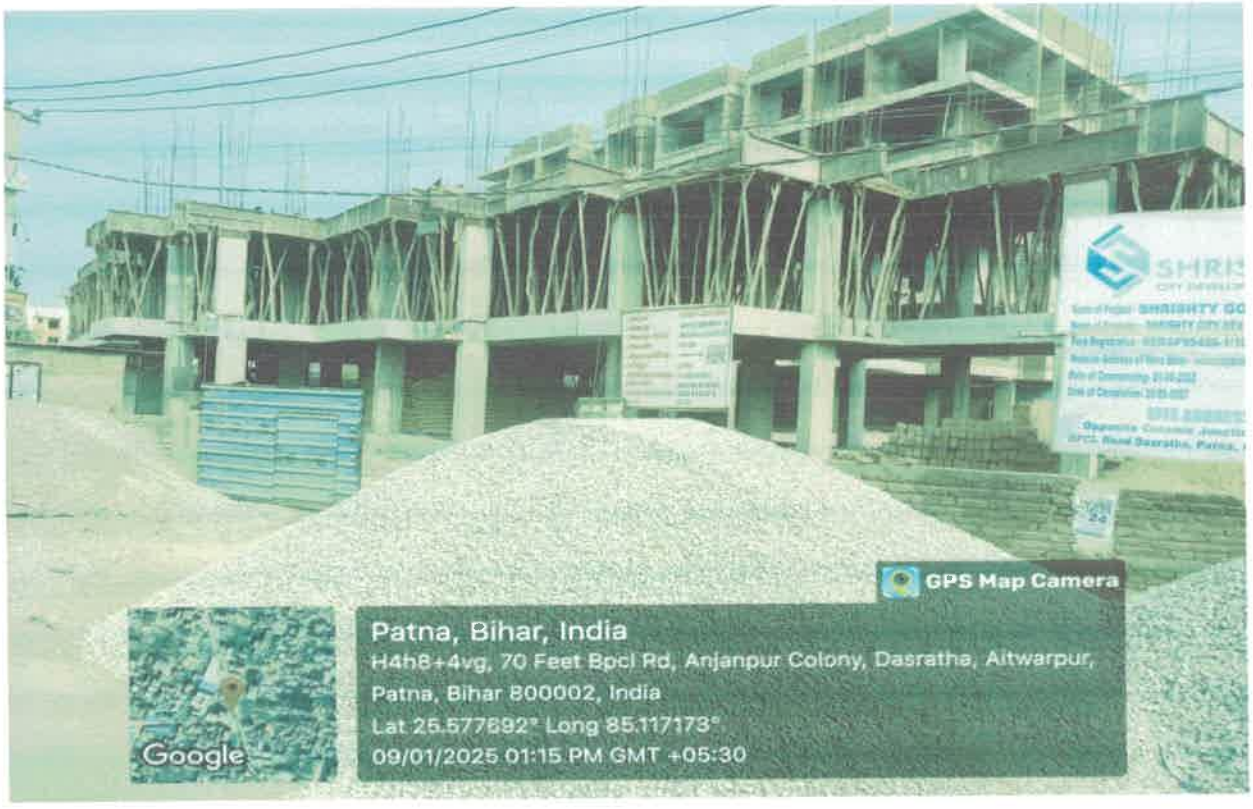

SHRISHTY CITY DEVELOPERS PVT. LTD.
Dipesh Diwakar
DIRECTOR



X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	2017102000004015
2.	Estimated Cost of the Project including land cost at the start of the Project	18,00,00,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	10,00,00,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	20,73,401=40
6.	Actual Cost Incurred during the Quarter	22,81,005=61
7.	Net amount at end of the Quarter	40,243=47
8.	Total expenditure on Project **till date**	1,82,56,982=15
9.	Cumulative fund collected till the end of Quarter in question	1,73,12,003=00
10.	Cumulative expenditure done till the end of Quarter in question	1,82,56,982=15

SHRISHTY CITY DEVELOPERS PVT. LTD.

Dipesh Diwakar

DIRECTOR

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS

A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

XIV UNITS ALLOCATION DETAILS

Total Number of sanctioned apartments
1 BHK-
2 BHK -35
3 BHK-30
4 BHK-
Shop-
Bungalow -
Plot etc

Details of allotment made so far with Flat number/ Bungalow - Plot etc

FLAT-NO.	FLAT TYPE
BLOCK-A-106	2 BHK
BLOCK-A-303	3 BHK
BLOCK-A-304	3 BHK
BLOCK-A-305	3 BHK
BLOCK-A-306	2 BHK
BLOCK-A-307	3 BHK
BLOCK-B-204	3 BHK
BLOCK-B-205	3 BHK
BLOCK-B-403	3 BHK
BLOCK-B-405	3 BHK

Cancellation of flat allotment, If any with Flat number/ Bungalow – Plot etc

RAJNI BALA 3BHK

SHRISHTY CITY DEVELOPERS PVT. LTD.
Dipesh Diwakar
DIRECTOR

XV. BROCHURE /Prospectus
XVI Grievance Redressal Officer **Name :** DIPESH DIWAKAR **Contact No :** 9934373000 **Email id :** info@shrishtycity.com **Address :** C/O- BIRENDRA KUMAR, MURLICHAK, KHAJPURA, PATNA

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

SHRISHTY CITY DEVELOPERS PVT. LTD.

Dipesh Diwakar

DIRECTOR

Signature of Promoter

Name:

Date:
