FORM-7

[REGULATION-9]

Quarterly Progress Report for quarter ending 31st December of 2024 (Year)

I. PARTICULARS OF PROMOTERS	
Promoter's Registration Number/CIN No.	Deed No. – 600 Dated – 15-09-2021
Name of the Promoter's Entity	Sanrachna Buildcon
Address of the Promoter's Entity :	305, Naman Ashray Apartment, Sahdeo Mahto Marg, Boring Road, S K Puri, Patna, Bihar, 800001
Total Experience of promoter in Real Estate Sector	1 Years
Total Experience in Real Estate After commencement of RERA	1 Years
No of Project done Before commencement of RERA	No Any
No of Project done After commencement of RERA	1. Sanrachna ONYX

II. PARTICULARS OF PROJECT	
Project Registration Number	BRERAP40516-1/107/R-1752/2024
Name of Project	Sanrachna ONYX
Name of Promoter	Sanrachna Buildcon
Project Address	Plot No. C.S- 1251 Part, Khata No.- 160, Mauza- Digha, Tauzi No.- 15270, Present P.S Name- Digha, Survey P.S and Pargana- Phulwari, Town and District- Patna, Bihar, Block- Patna Sadar Mauja - दीघा District – Patna Plot No -1251 Part
Project Registration is valid up to	02-05-2028
Starting date of Project	10-06-2024
Type of Project	Residential/Group Housing
Name of the Competent Authority which sanctioned the project map	Patna Municipal Corporation
Period of validity of map by the Competent Authority	FIVE YEARS FROM THE DATE OF PASSING OF MAP

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building/Block Number	Apartment Type	Carpet Area (In Sqft)	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share –20		Total Number of Apartments in Landowner's share –22	
				Booked	AFS Executed	Booked	AFS Executed
Sanrachna ONYX	3 BHK	950.00	20				
Sanrachna ONYX	2 BHK	713.00	10				
Sanrachna ONYX	2 BHK	704.00	10				
Sanrachna ONYX	1 BHK	421.00	2				
Total				0	0	0	0
				00%of total units	00%of total units	00%of total units	00%of total units

IV. DETAILS OF ASSOCIATION OF ALLOTTEES :

Mandatory in case the booking percentage exceeds 50% of the total sanctioned flats/plots/buildings/commercial space

Association of Allottee not be made because, booking percentage not exceeds 50% yet.

V. CANCELLATION OF FLAT ALLOTMENT, IF ANY WITH FLAT NUMBER/BUNGALOW /PLOT NO./OFFICE SPACE/SHOP/ETC.

(A) Cancelled by Allotees	(B) Cancelled by Promoters
No Any	**No Any**

VI. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES/ PARKING SPACE

Building Wise/ Block Number	Total Number of Sanctioned Garages/ Parking Space	Total Number of Garages/Parking Space: 1. Booked/Allotted -
Sanrachna ONYX	42	0

VII. DETAILS OF BUILDING APPROVALS

Already filed along with Registration Application

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Validity Upto		Attach Copy
1.	Environment Clearance				

2.	Fire N.O.C.				
4.	Airport Authority of India NOC				
5.	Water Supply Permission				
6.	Other Approval(s), if any, required for the Project.				

VIII. PROGRESS OF THE PROJECT – INTERNAL INFRASTRUCTURE DEVELOPMENT

In case of more than one Block/Building/Apartments/Plots/Bungalow, the details have to be filled for each Block separately

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	**100%**	**Completed**
2.	Basements (if any)	**90%**	**10-02-2025**
3.	Podiums (if any)	**NA**	
4.	Plinth	**100%**	**Completed**
5.	Stilt Floor	**10%**	**10-03-2025**
6.	Slabs of Super Structure	**0%**	**15-02-2026**
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	**0%**	**15-02-2026**
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	**0%**	**10-12-2026**
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	**10%**	**10-03-2027**
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	**0%**	**10-12-2026**
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per prescribed norms.	**10%**	**05-01-2027**
12.	N.O.C, Electrical fittings, Mechanical Equipment, compliance to conditions of environment as per prescribed norms	**0%**	**05-03-2027**
13.	Finishing to entrance lobby/s plinth protection, paving of areas appurtenant to	**0%**	**05-03-2027**

	Building/Wing, Compound Wall and all other requirements as may be required to complete project as per Specifications in Agreement of Sale. Any other activities.		
14.	Overall Percentage of Actual Work Done and final completion date	**26.66%**	**05-03-2027**

IX. EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS - PROGRESS RELATED TO AMENITIES AND COMMON AREA				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	No	**NA**	
2.	Water Supply	Yes	50%	**05-03-2027**
3.	Sewerage (Chamber, Line, Septic Tank, STP)	Yes	0%	**05-03-2027**
4.	Storm Water Drains	No		
5.	Landscaping & Tree Planting	No		
6.	Street Lighting	No		
7.	Community Buildings	No		
8.	Treatment and Disposal of Sewage and Sullage Water	No		
9.	Solid Waste Management & Disposal	No		
10.	Water Conservation / RainWater Harvesting	No		
11.	Energy Management	No		
12.	Fire Protection and FireSafety Requirements	Yes	**0%**	**05-03-2027**
13.	Closed Parking	Yes	50%	**05-03-2027**
14.	Open Parking	No		
15.	Electrical Meter Room, Sub-Station, Receiving Station	No		
16.	Others (Option to AddMore)	No		

17.	Overall Percentage of Actual Work Done and final completion date	Yes	25%	**05-03-2027**

X. EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT
Not Applicable because our project is Residential/Group Housing.

XI. Financial Progress of the Project

S.No.	Particulars	Amount (in Rs.)
1	Project Account No.	040405011431
2	Estimated Cost of the Project including land cost at the start of the Project(In lakh)	880.00/-
3	Estimated Development Cost of the Project at the start of the Project. (Excluding Land Cost) (In lakh)	361.60/-
4	Any Variation in Development Cost which is declared at the start of the Project.	No Any
5	Amount received during the Quarter	00.00/-
6	Actual Cost Incurred during the Quarter	45,00,000.00/-
7	Net amount at end of the Quarter	00.00/-
8	Total expenditure on Project **till date**	45,00,000.00/-
9	Cumulative fund collected till the end of Quarter in question	00.00/-
10	Cumulative expenditure done till the end of Quarter in question	45,00,000.00/-
11	Percentage of Expenditure incurred of the total Estimated development cost of the project.	12.44%

XII. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED/DETAILS OF LOAN TAKEN BY PROMOTERS AGAINST THE PROJECT, If any
No Any


XIII. GEO TAGGED PHOTOGRAPHS (EACH BLOCK/BUILDING/APARTMENTS/PLOTS/BUNGALOW) OF THE PROJECT The photograph must have date.

(A)	S. No.	Particulars
	1.	**Photographs showing Front Elevation.-** Attached Below

	2.	**Photographs showing Rear Elevation.-** Attached Below
	3.	**Photographs showing Side Elevation (Both sides)** Attached Below
	4.	**Photograph of each floor showing the progress of interior works**
	5.	**Photograph of Common Areas (Staircase, Lift Area, Terrace, Parking, etc.)**
(B)		**Photograph of the display board set up at the project site providing requisite information along with the QR code of the project allotted by the Authority**

XIV. MISCELLANEOUS		
A	List of Legal Cases (if any) On Project / Promoter	
1.	(a) Case No. (b) Name of Parties Order Passed, if Yes , Whether complied (Yes/No)	NA
2.	No. of Execution Cases against this project (a) Case No. (b) Name of Parties Order Passed, if Yes , Whether complied (Yes/No)	NA
3.	No. of Suo - Moto cases against this project (a) Case No. (b) Name of Parties Order Passed, if Yes , Whether complied (Yes/No)	NA
4.	No. of Certificate cases /PDR cases against this project (a) Case No. (b) Name of Parties	NA

XV. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART
a. Whether the project is in progress as per time schedule or lagging behind? Yes b. If yes, whether it would be completed on the completion date fixed as per RC. Yes If No, then Reason for delay: NA

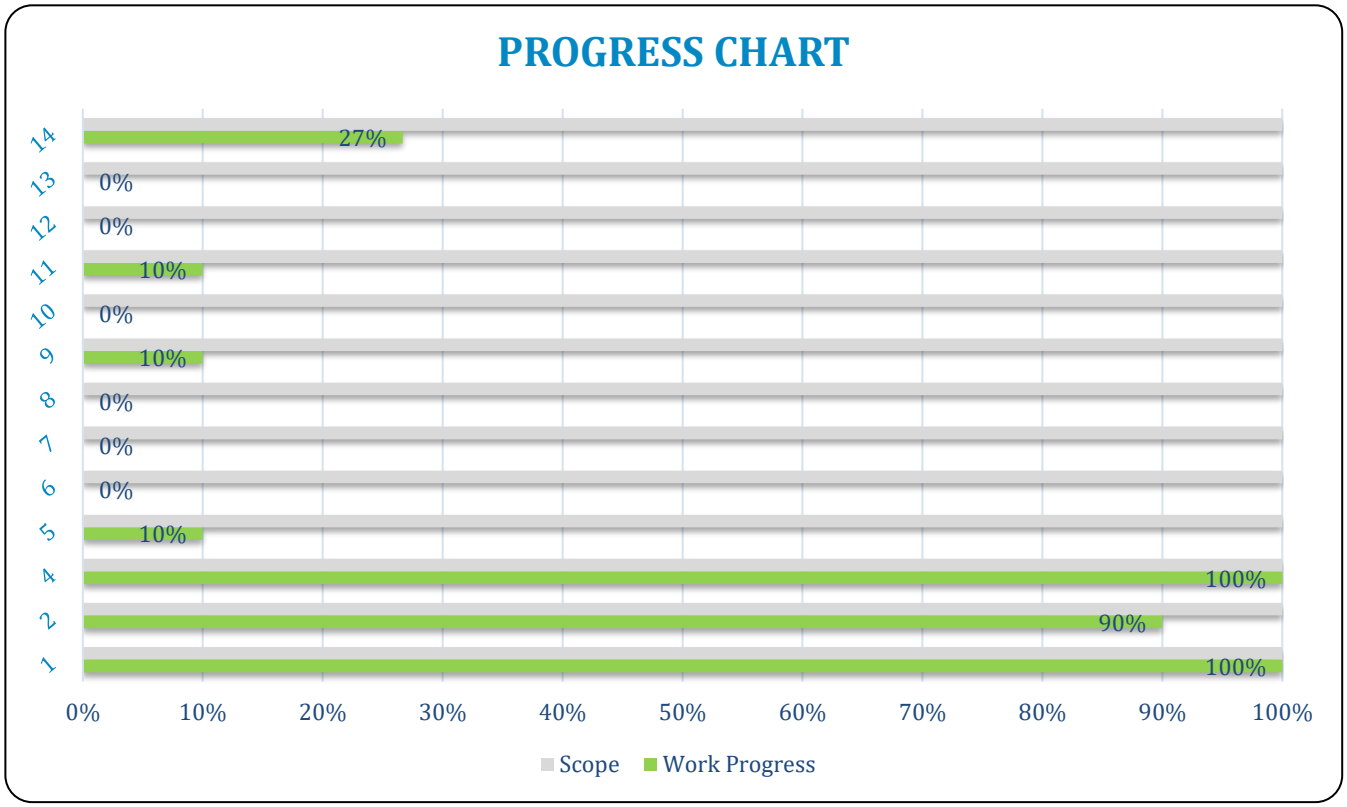

XVI. BROCHURE /Prospectus- Attached

XVII. Grievance Redressal Officer

Name :- Manoj Kumar Singh and Sushil Kumar Singh

Contact No :- 9973675009, 9934305202

Email id :- buildconsanrachna@gmail.com

Address :- 305, Naman Ashray Apartment, Sahdeo Mahto Marg, Boring Road, S K Puri, Patna, Bihar, 800001

Project Site Photographs


GPS Map Camera
खास महल दीघा दियरा, बिहार, भारत
J3mh+j6x, जगत विहार कॉलोनी, रुकनपुरा, खास महल दीघा दियरा, पटना, बिहार 800011, भारत
Lat 25.634191° Long 85.078074°
01/01/25 01:32 PM GMT +05:30
Google


GPS Map Camera
पटना, बिहार, भारत
J3ph+24f, अचार्या किशोरे कुनाल पथ, जगत विहार कॉलोनी, रुकनपुरा, पटना,
पानापुर तौफिर, बिहार 800025, भारत
Lat 25.634702° Long 85.078156°
01/01/25 01:34 PM GMT +05:30
Google


GPS Map Camera
पटना, बिहार, भारत
J3ph+24f, अचार्या किशोरे कुनाल पथ, जगत विहार कॉलोनी, रुकनपुरा, पटना,
पानापुर तौफिर, बिहार 800025, भारत
Lat 25.634713° Long 85.078166°
01/01/25 01:34 PM GMT +05:30
Google


GPS Map Camera
पटना, बिहार, भारत
J3mh+p62, अभ्युदय मार्ग, शांति वैन, यादव कॉलोनी, रुकनपुरा, पटना, खास महल
दीघा दियरा, बिहार 800011, भारत
Lat 25.6343° Long 85.078092°
01/01/25 01:33 PM GMT +05:30
Google


GPS Map Camera
पटना, बिहार, भारत
J3mh+p62, अभ्युदय मार्ग, शांति वैन, यादव कॉलोनी, रुकनपुरा, पटना, खास महल
दीघा दियरा, बिहार 800011, भारत
Lat 25.634454° Long 85.078125°
01/01/25 01:33 PM GMT +05:30
Google



Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Signature of Promoter
Sanrachna Homes Pvt. Ltd.

Director
Date: 15-01-2025
