FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending MARCH 2025

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U43299BR2023PTC062666	Name of Firm	SATYASAROJ CONSTRUCTIONS PRIVATE LIMITED
Firm Address :	C/O SRI AKHILES PD. SINHA, KHAS MAHAL, CHIRAIYATAR, KARBIGAHIYA, PATNA BIHAR, K-SECTOR, SAMPATCHAK, PATNA - 800020, BIHAR		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA	01 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP90103-1/117/R-1732/2024	Name of Project/Phase of Registered Project	SHIVPUJAN ENCLAVE APARTMENT
Name of Promoter	SATYASAROJ CONSTRUCTIONS PRIVATE LIMITED	Project Address	DHANWAN, MAUZA-KHARANTINTI, P.S. – BODH GAYA, DISTRICT-GAYA, BIHAR
Name of Co-promoter	N/A		
Project Registration is valid up to	07-04-2029		
Starting date of Project or Phase of the Project	22-07-2024		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	07-04-2029		

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - FLAT-16	Total Number of Apartments in Landowner's share - FLAT-16
	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.	08 24		FLAT-32	1. Booked / Allotted -NIL 2. Sold-NIL	3. Booked/ Allotted-NIL Sold -NIL
					Percentage of booking 0%	Percentage of booking 0%

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted -	NIL
	32	2. Sold -	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	DIRECTOR-CUM-STATE FIRE OFFICER, BIHAR, PATNA		01-01-2024	
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	AAI		28-08-2023	
5.	Other Approval(s), if any, required for the Project.	N/A			

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. _____(To beaded for each Building / Wing)

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	0%	
2.	Basements (if any)		
3.	Podiums (if any)		
4.	Plinth	0%	
5.	Stilt Floor	0%	
6.	Slabs of Super Structure	0%	20/12/2025
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0% 0% 0% 0%	15/08/2027 15/08/2027 10/04/2028 15/05/2028
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0% 0%	15/09/2028 15/09/2028
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0% 0% 0%	15/12/2028 15/12/2028 15/12/2028
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0% 0% 0% 0%	15/08/2028 15/08/2028 15/08/2028 15/08/2028
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be	0% 0% 0% 0% 0% 0%	15/12/2028 15/12/2028 15/12/2028 15/12/2028 15/12/2028 15/12/2028

	required to complete project as per Specifications in Agreement of Sale. Any other activities	0%	

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	10/02/2029
2.	Water Supply	YES	0%	15/03/2029
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	
4.	Storm Water Drains	YES	0%	
5.	Landscaping & Tree Planting	YES	0%	15/03/2029
6.	Street Lighting	YES	0%	
7.	Community Buildings	N/A		
8.	Treatment and Disposal of Sewage and Sullage Water	YES	0%	
9.	Solid Waste Management & Disposal	YES	0%	15/03/2029
10.	Water Conservation / Rain Water Harvesting	YES	0%	15/03/2029
11.	Energy Management	YES	0%	
12.	Fire Protection and Fire Safety Requirements	YES	0%	
13.	Closed Parking	YES	0%	15/03/2029

14.	Open Parking	N/A		
15.	Electrical Meter Room, Sub-Station, Receiving Station	N/A		
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	Sr. No.		
	1.	Front Elevation	ATTACH
	2.	Rear Elevation	ATTACH
	3.	Side Elevation	ATTACH
(B)		Photograph of each floor	


GPS Map Camera
Google
Kharanti, Bihar, India
Pxm7+m39, Kharanti, Bihar 823004, India
Lat 24.733801° Long 84.962267°
12/04/2025 04:52 PM GMT +05:30

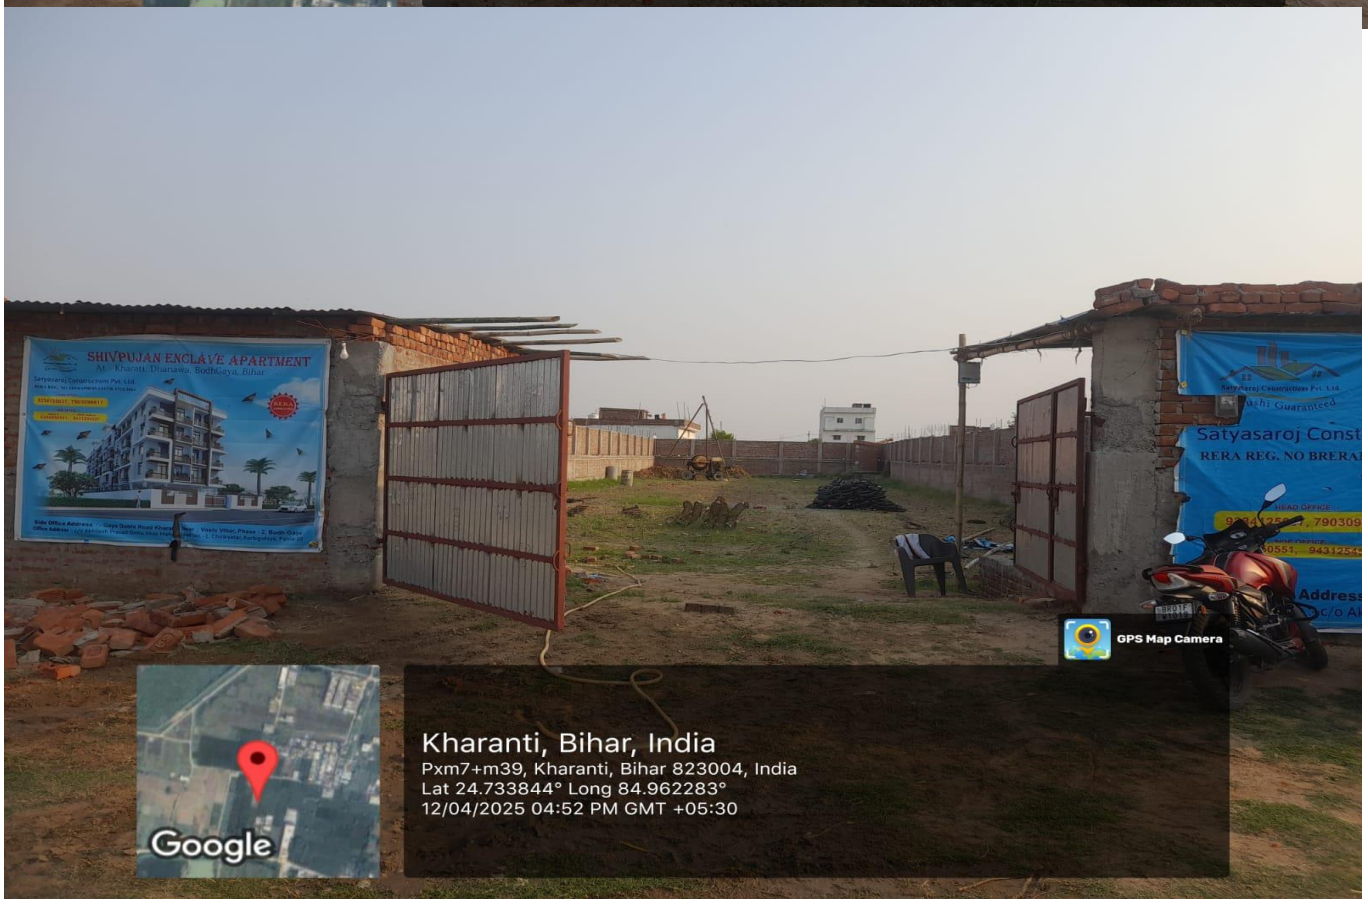
SHIVPUJAN ENCLAVE APARTMENT
GPS Map Camera
Google
Kharanti, Bihar, India
Pxm7+m39, Kharanti, Bihar 823004, India
Lat 24.733844° Long 84.962283°
12/04/2025 04:52 PM GMT +05:30

X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	7807812304
2.	Estimated Cost of the Project including land cost at the start of the Project	5,60,00,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	5,40,00,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	00=00
6.	Actual Cost Incurred during the Quarter	00=00
7.	Net amount at end of the Quarter	00=00
8.	Total expenditure on Project **till date**	00=00
9.	Cumulative fund collected till the end of Quarter in question	00=00
10.	Cumulative expenditure done till the end of Quarter in question	00=00
XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED		

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO

B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

XIV UNITS ALLOCATION DETAILS		
Total Number of sanctioned apartments 1 BHK- 2 BHK -08 3 BHK-24 4 BHK- Shop- Bungalow - Plot etc	Details of allotment made so far with Flat number/ Bungalow - Plot etc NO BOOKING	Cancellation of flat allotment, If any with Flat number/ Bungalow – Plot etc
XV. BROCHURE /Prospectus		
XVI Grievance Redressal Officer **Name :** SATYANARAYAN SINGH **Contact No :** 9473386357 **Email id :** satyanarayansinghanand@gmail.com **Address :** S/O- SRI AKHILESH PD SINHA, KHAS MAHAL, CHIRAINYATAR, KARBIGAHIYA, PATNA		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.



Signature of Promoter

Name:

Date:
