FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	PARTNERSHIP DEED NO. 323/2017	Name of Firm	KATYAYANI HOMES
Firm Address :	1ST FLOOR B.D MARKET, KANKARBAGH MAIN ROAD, PATNA 20		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA			
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP12539-1/1262/R-1170/2021	Name of Project/Phase of Registered Project	GOKUL DHAM RESIDENCY
Name of Promoter	KATYAYANI HOMES	Project Address	JANTA ROAD CHITKOHRA, PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	10/10/2024		
Starting date of Project or Phase of the Project	20/07/2021		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	3 YEARS + 9 Month Covid 19		

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - FLAT-21	Total Number of Apartments in Landowner's share - FLAT-19
	1. 1 BHK				1. Booked / Allotted -09	3. Booked/ Allotted-NIL
	2. 2 BHK, -	12	8379.33			
	3. 3 BHK	28	28742.76	40	2. Sold-NIL	Sold-NIL
	4. Shop					
	5. Bungalow					
	6. Plot etc.				Percentage of booking 38%	Percentage of booking 0%

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted -	09
	40	2. Sold -	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

pvth

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. P/Chitkohe-PRN-B+G+2/327/2018 To beaded for each Building / Wing)

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	100%	
3.	Podiums (if any)	100%	
4.	Plinth	100%	
5.	Stilt Floor	100%	
6.	Slabs of Super Structure	100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100% 100% 20%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	50%	31-12-2024
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	80% 100%	31-12-2024
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	70% 70% 70% 50%	31-12-2024 31-12-2024 31-12-2024 31-12-2024

11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	100%	

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES		
2.	Water Supply	YES	100%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	70%	31-12-2024
4.	Storm Water Drains	YES	30%	
5.	Landscaping & Tree Planting	YES	0%	
6.	Street Lighting	YES	0%	
7.	Community Buildings	NO		
8.	Treatment and Disposal of Sewage and Sullage Water	NO		

9.	Solid Waste Management & Disposal	YES	50%	
10.	Water Conservation / Rain Water Harvesting	YES	20%	31-12-2024
11.	Energy Management	YES	0%	
12.	Fire Protection and Fire Safety Requirements	YES	10%	31-12-2024
13.	Closed Parking	YES	60%	31-12-2024
14.	Open Parking			
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			

9.	Energy Management			

IX.	GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT		
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

X.	FINANCIAL PROGRESS OF THE PROJECT	
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	920020064869699
2.	Estimated Cost of the Project including land cost at the start of the Project	13,60,00,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	8,00,00,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	14,36,400=00
6.	Actual Cost Incurred during the Quarter	14,00,307=00
7.	Net amount at end of the Quarter	1,22,008=00
8.	Total expenditure on Project **till date**	3,20,19,626=00
9.	Cumulative fund collected till the end of Quarter in question	1,18,78,219=00
10.	Cumulative expenditure done till the end of Quarter in question	3,20,19,626=00

XI.	DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII.	MISCELLANEOUS

A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	02
3.	No. of possessions given to allottees	NIL

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

XIV UNITS ALLOCATION DETAILS

Total Number of sanctioned apartments
1 BHK-
2 BHK -12
3 BHK-28
4 BHK-
Shop-
Bungalow -
Plot etc

Details of allotment made so far with Flat number/ Bungalow - Plot etc

FLAT NO.	FLAT TYPE
104	3 BHK
105	3 BHK
106	3 BHK
107	3 BHK
110	3 BHK
111	3 BHK
208	3 BHK
209	3 BHK
211	3 BHK

Cancellation of flat allotment, If any with Flat number/ Bungalow – Plot etc

XV. BROCHURE /Prospectus

XVI Grievance Redressal Officer

Name : RAVI SHANKAR PRASAD SINGH

Contact No : 7979876197

Email id : Katyayanihomespatna01@rediffmail.com

Address : 1ST FLOOR B.D MARKET, KANKARBAGH MAIN ROAD, PATNA 20

Undertaking:


I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Signature of Promoter

Name:

Date:

Gokuldham Residency

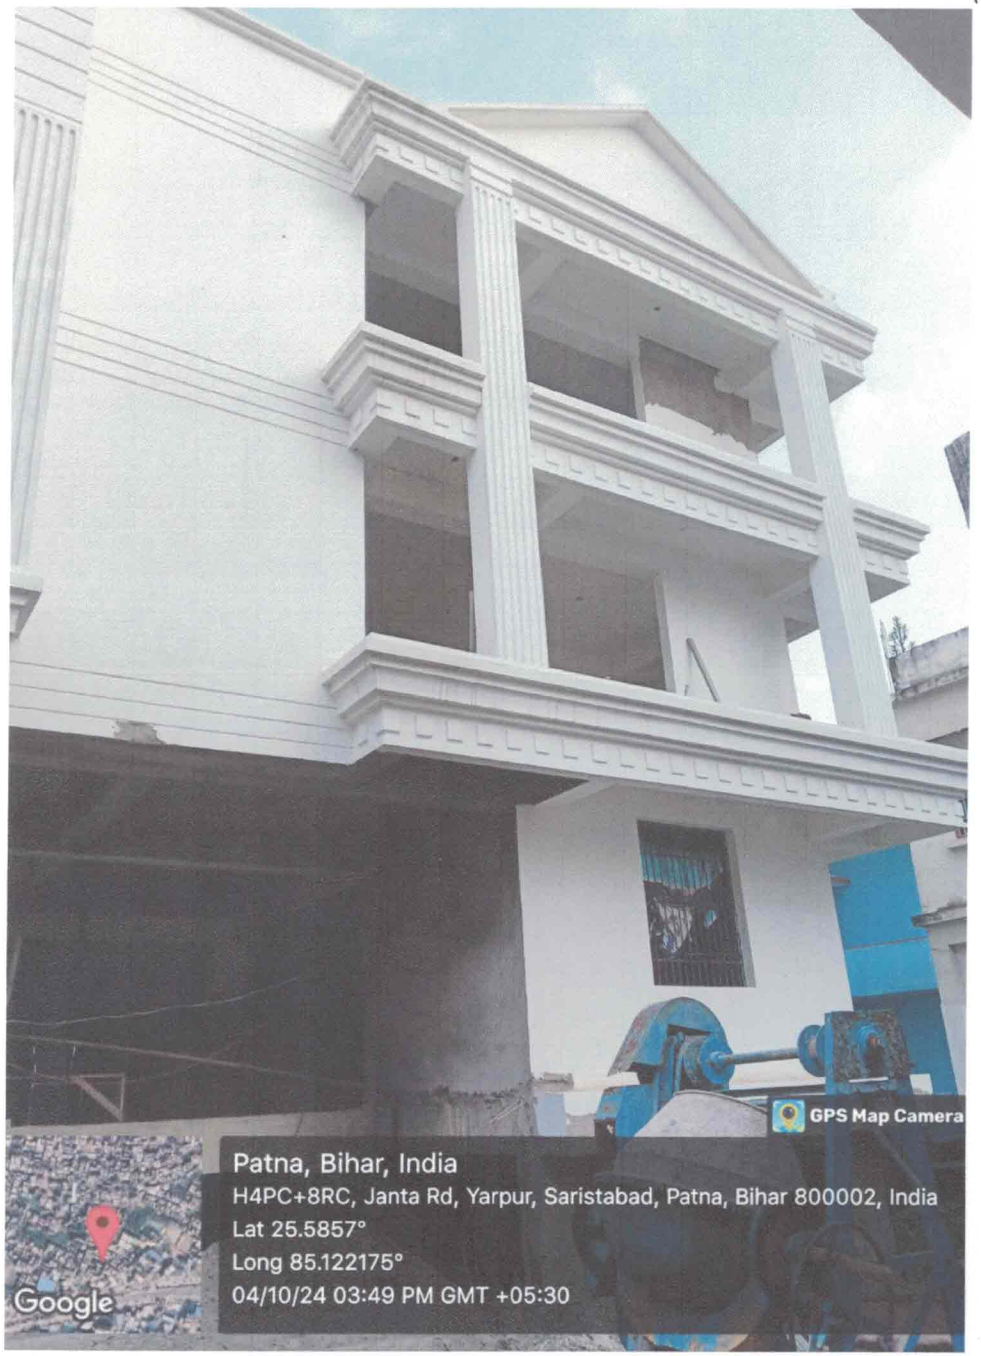




GPS Map Camera
Patna, Bihar, India
H4PC+8RC, Janta Rd, Yarpur, Saristabad, Patna, Bihar 800002, India
Lat 25.585733°
Long 85.122223°
04/10/24 03:50 PM GMT +05:30
Google
