FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	PATNERSHIP DEED DATE-15-11-20216	Name of Firm	SRI SAI DEVELOPER
Firm Address :	SHIV MANDIR ROAD, NEAR IRRIGATION COLONY, DIPUGARHA, HAZARIBAGH, JHARKHAND		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA	02 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP93448-1/154/R-1461/2022	Name of Project/Phase of Registered Project	SRI SAI RESIDENCY
Name of Promoter	SRI SAI DEVELOPER	Project Address	RAMJAYPAL NAGAR, NEAR GANGA CITY, DANAPUR, PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	15/08/2026		
Starting date of Project or Phase of the Project	08/09/2022		
Type of Project or Phase of the Project	1. Residential		
Period of validity of map by the Competent Authority	3 YEARS		

SRI SAI DEVELOPER

PARTNER

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share -	Total Number of Apartments in Landowner's share -
	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow - 6. Plot etc.	10 06		FLAT-16	1. Booked / Allotted -06 2. Sold-NIL	3. Booked/ Allotted-NIL Sold -NIL
					Percentage of booking	Percentage of booking 0%

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.			
Association of allottees name			
Details of allottees - Name, Address, Email id (if any), contact number. These details may not be available to common people			
Name	Address	contact number	Email id (If any)

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
	16	1. Booked/Allotted -	06
		2. Sold -	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	N/A			
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

SRI SAI DEVELOPER

PARTNER

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. 58/22-23

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	100%	
3.	Podiums (if any)	NIL	
4.	Plinth	100%	
5.	Stilt Floor	NIL	
6.	Slabs of Super Structure	95%	03-02-2025
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100% 70% 60% 50%	 03-02-2025 03-02-2025 02-03-2025
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	70% 65%	03-03-2025 03-03-2025
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100% 70% 70%	03-11-2025 03-05-2025 20-02-2025
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	40% 50% 90% 50%	20-03-2025 02-02-2025 20-03-2025 02-02-2025

SRI SAI DEVELOPER

PARTNER

8.	Treatment and Disposal of Sewage and Sullage Water	YES	100%	
9.	Solid Waste Management & Disposal	YES		
10.	Water Conservation / Rain Water Harvesting	YES	0%	
11.	Energy Management	YES	0%	
12.	Fire Protection and Fire Safety Requirements	NO		
13.	Closed Parking	YES	100%	
14.	Open Parking			
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	25%	
16.	Others (Option to Add More)	NO		

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			

SRI SAI DEVELOPER

PARTNER

8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX.	GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT		
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

X.	FINANCIAL PROGRESS OF THE PROJECT	
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	7577002900000029
2.	Estimated Cost of the Project including land cost at the start of the Project	5,00,00,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	00=00
6.	Actual Cost Incurred during the Quarter	00=00
7.	Net amount at end of the Quarter	70,000=00
8.	Total expenditure on Project **till date**	3,95,10,000=00
9.	Cumulative fund collected till the end of Quarter in question	1,50,39,370=00
10.	Cumulative expenditure done till the end of Quarter in question	4.05,00,000=00

XI.	DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

SRI SAI DEVELOPER

PARTNER

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

XIV UNITS ALLOCATION DETAILS

Total Number of sanctioned apartments	Details of allotment made so far with Flat number/ Bungalow - Plot etc		Cancellation of flat allotment, If any with Flat number/ Bungalow – Plot etc
1 BHK- 2 BHK -10 3 BHK-06 4 BHK- Shop- Bungalow - Plot etc	FLAT NO.	FLAT TYPE	
	103	2 BHK	
	104	2 BHK	
	301	3 BHK	
	302	3 BHK	
	G 1	3 BHK	
	203	2 BHK	

XV. BROCHURE /Prospectus

SRI SAI DEVELOPER

PARTNER

XVI Grievance Redressal Officer

Name : RAHUL KUMAR

Contact No : 7488623465

Email id : srisaideveloperhzb@gmail.com

Address : SHIV MANDIR ROAD, NEAR IRRIGATION COLONY, DIPUGARHA, HAZARIBAGH, JHARKHAND

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

SRI SAI DEVELOPER

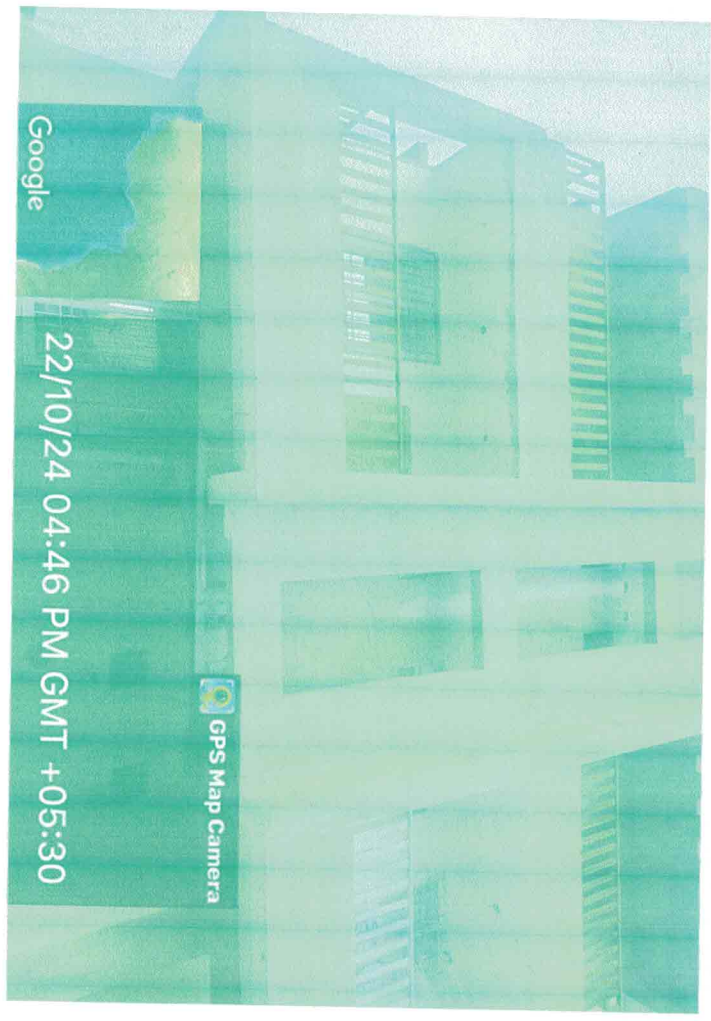
PARTNER

Signature of Promoter

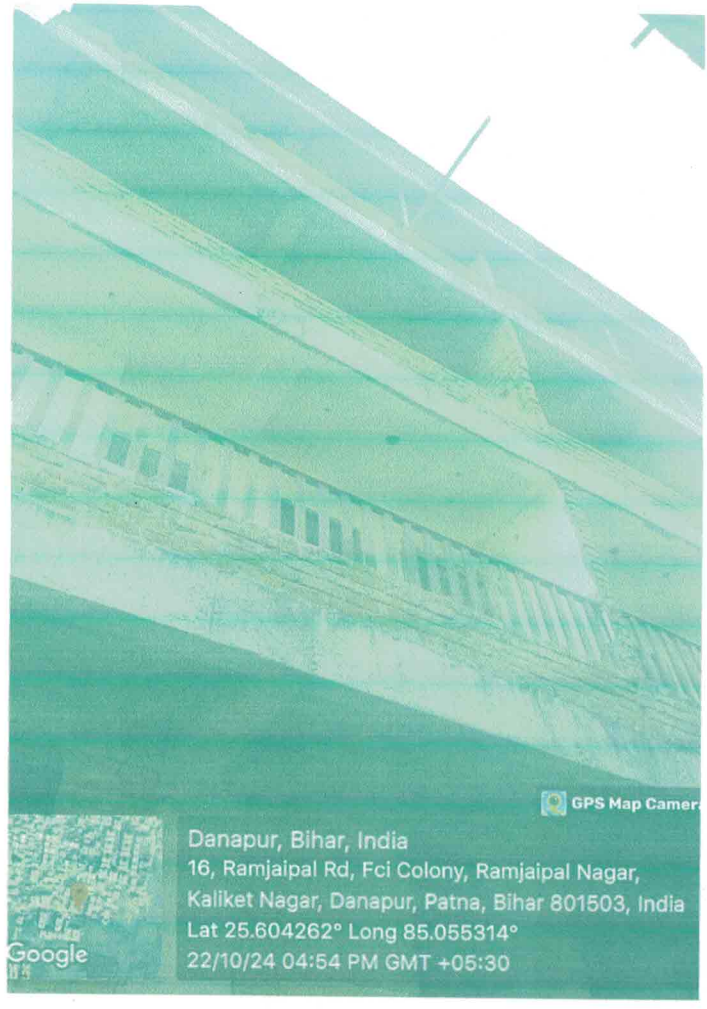
Name:

Date:


GPS Map Camera
Google
22/10/24 04:47 PM GMT +05:30


Google
22/10/24 04:46 PM GMT +05:30
GPS Map Camera


GPS Map Camera
Google
22/10/24 04:47 PM GMT +05:30


GPS Map Camera
Google
Danapur, Bihar, India
16, Ramjaipal Rd, Fci Colony, Ramjaipal Nagar,
Kaliket Nagar, Danapur, Patna, Bihar 801503, India
Lat 25.604262° Long 85.055314°
22/10/24 04:54 PM GMT +05:30
