FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending June of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U45309BR2016PTC032168	Name of Firm	RGM RESIDENCY PRIVATE LIMITED
Firm Address :	27 MAHARAJA KAMESHWAR COMPLEX, GROUND FLOOR, FRASER ROAD, PATNA 800001		
Total Experience of promoter in Real Estate sector	10 YEARS		
Total Experience in Real Estate after Implementation of RERA	04 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	13 01	
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	02	

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP75933-1/121/R-1271/2022	Name of Project/Phase of Registered Project	PUSHKARA
Name of Promoter	RGM RESIDENCY PRIVATE LIMITED	Project Address	NORTH OF TRIBHUWAN SCHOOL, VIJAY SINGH YADAV PATH,KHAGAUL ROAD, DANAPUR, PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	15/07/2024		
Starting date of Project or Phase of the Project	14/02/2022		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	From 28/07/2021 to 27/07/2024		

RGM Residency Pvt. Ltd.

Director

CamScanner

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - 12 1. Booked / Allotted -06 2. Sold-01	Total Number of Apartments in Landowner's share - 12 3. Booked/ Allotted - NIL Sold -NIL
	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.	6 18	5738.46 21004.50	24	Percentage of booking 58%	Percentage of booking %

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
	24	1. Booked/Allotted -	06
		2. Sold -	01

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.	State Fire officer-cum-Director, Patna, Bihar	31/03/2021	07/04/2021	Annexure-A
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. 39/21-22

RGM Residency Pvt. L.

Director

CamScanner

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	100%	
3.	Podiums (if any)	N/A	
4.	Plinth		
5.	Stilt Floor		
6.	Slabs of Super Structure	100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	100%	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	100%	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale.	100%	

RGM Residency Pvt. Ltd.

Director

CamScanner

	Any other activities		

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	100%	
2.	Water Supply	YES	100%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	100%	
4.	Storm Water Drains	YES	100%	
5.	Landscaping & Tree Planting	YES	100%	
6.	Street Lighting	YES	100%	
7.	Community Buildings	N/A		
8.	Treatment and Disposal of Sewage and Sullage Water	N/A		
9.	Solid Waste Management & Disposal	YES	100%	
10.	Water Conservation / Rain Water Harvesting	YES	100%	
11.	Energy Management	YES	100%	

RGM Residency Pvt. Ltd.

Director

CamScanner

12.	Fire Protection and Fire Safety Requirements	YES	100%	
13.	Closed Parking	YES	100%	
14.	Open Parking	N/A		
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	100%	
16.	Others (Option to Add More)	N/A		

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			


IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

RGM Residency Pvt. Ltd.

Director

CamScanner


(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	Attach

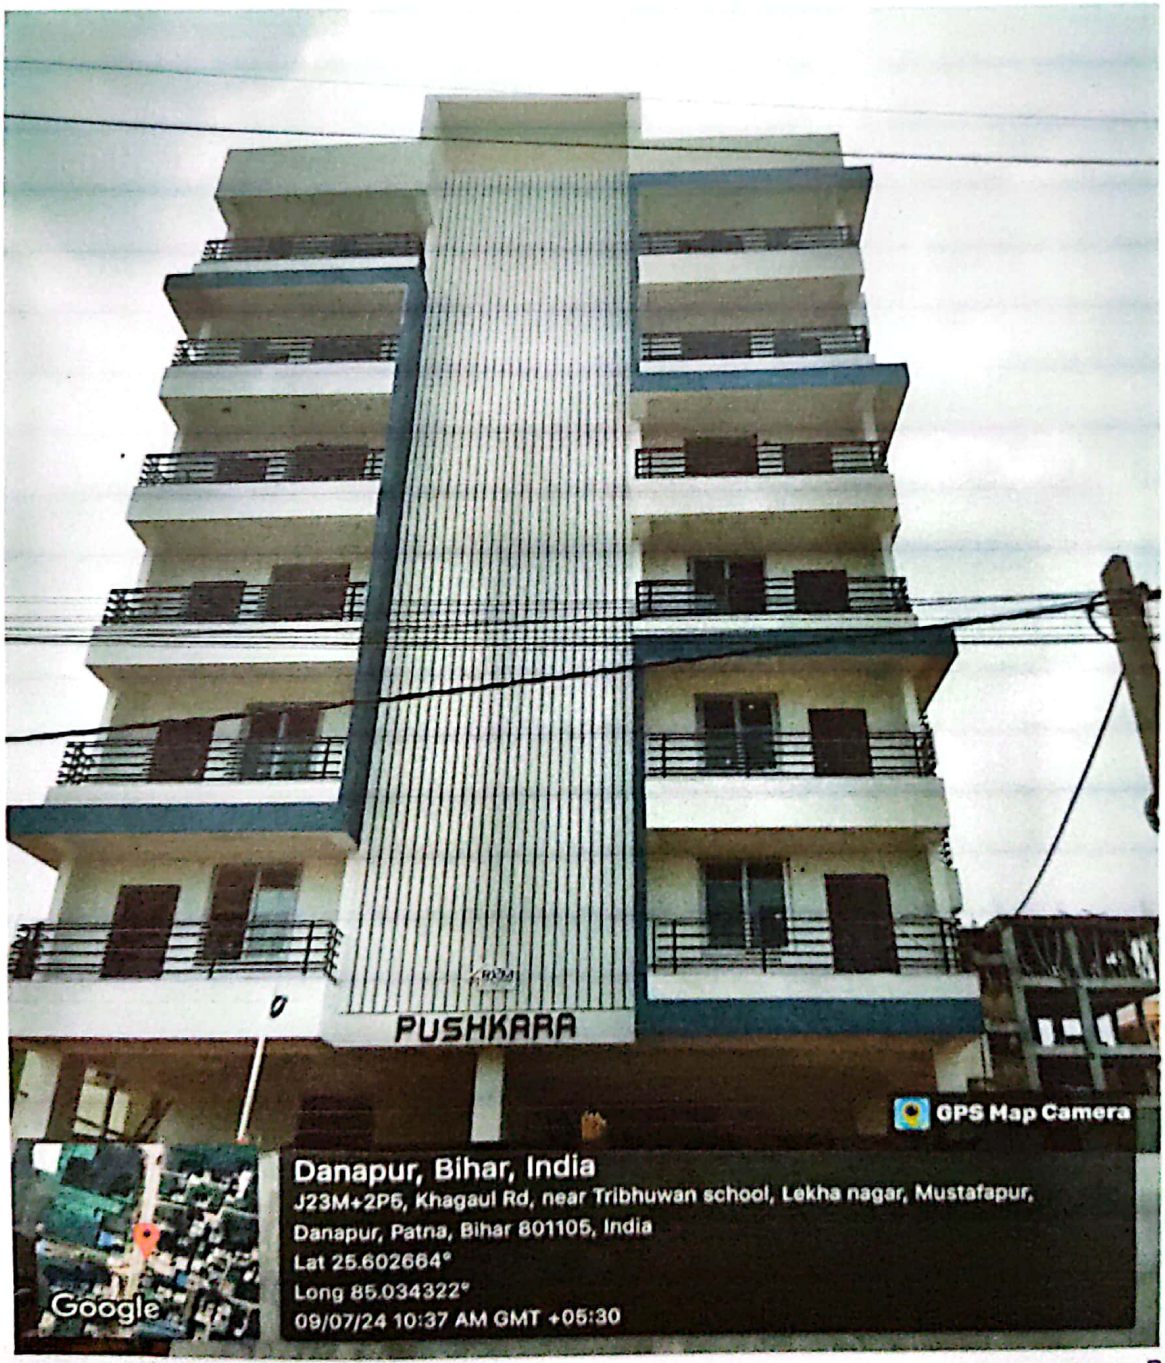


RGM Residency Pvt. Ltd.

Director

CamScanner

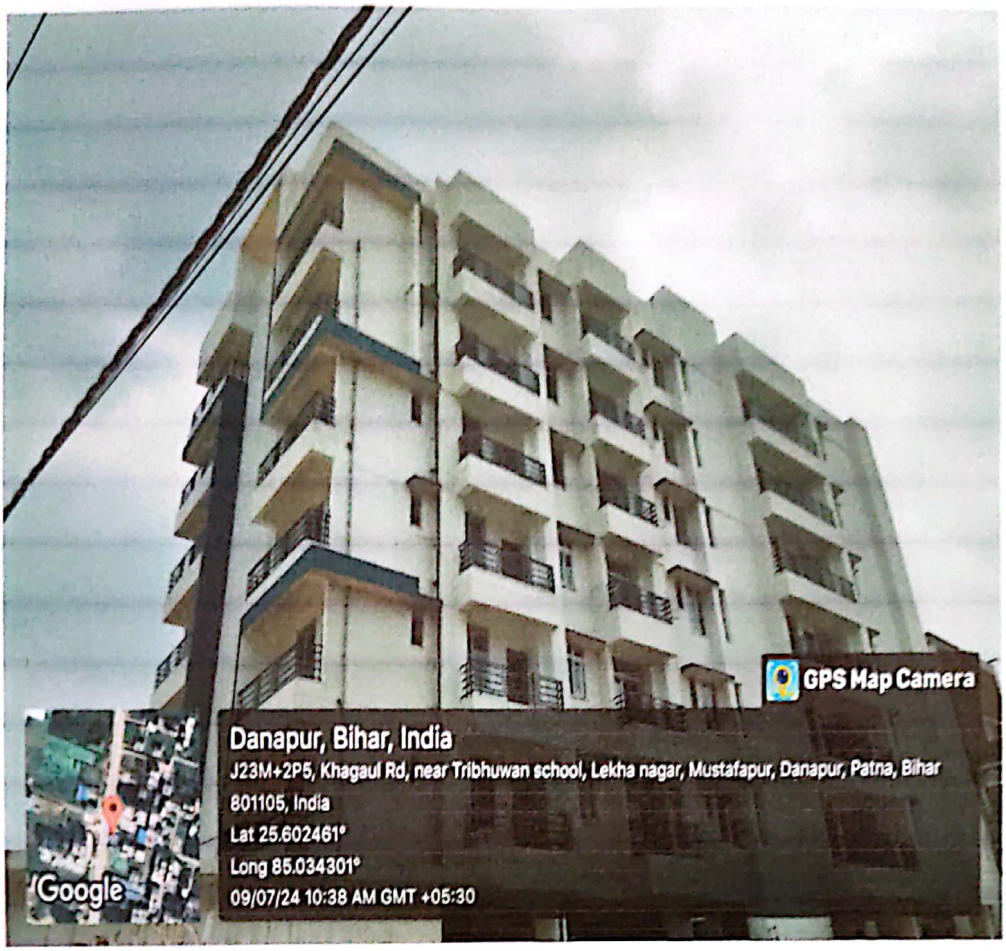


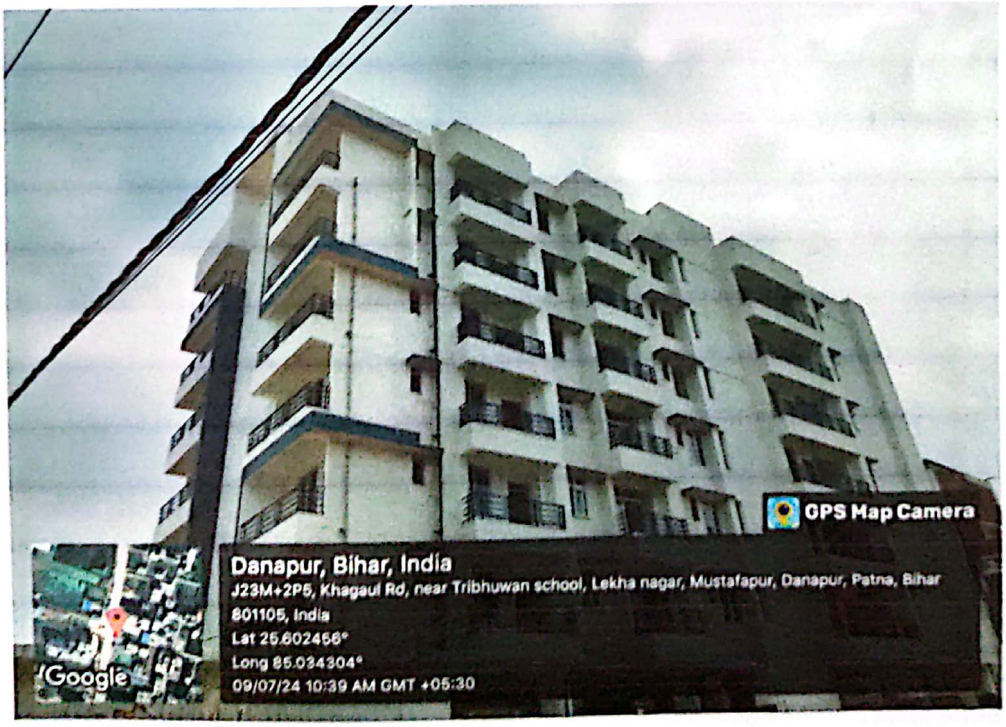


RGM Residency Pvt. Ltd.

Director

CamScanner

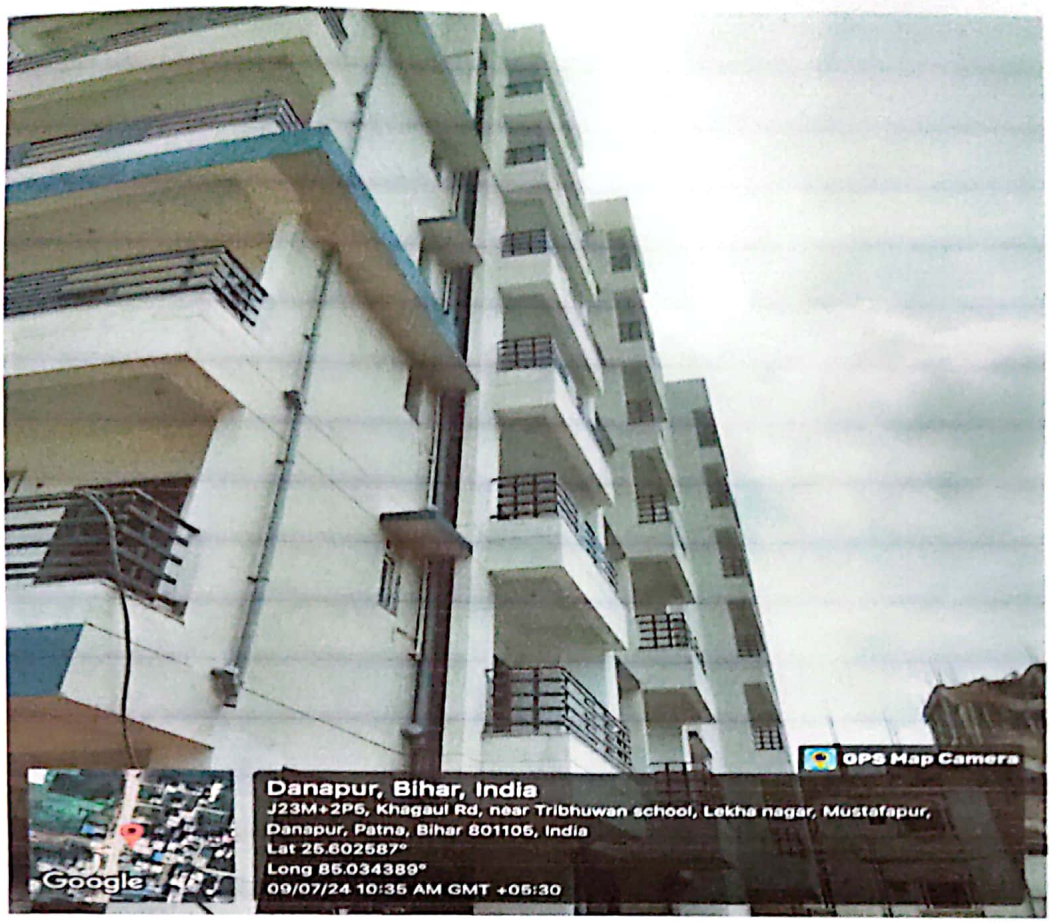

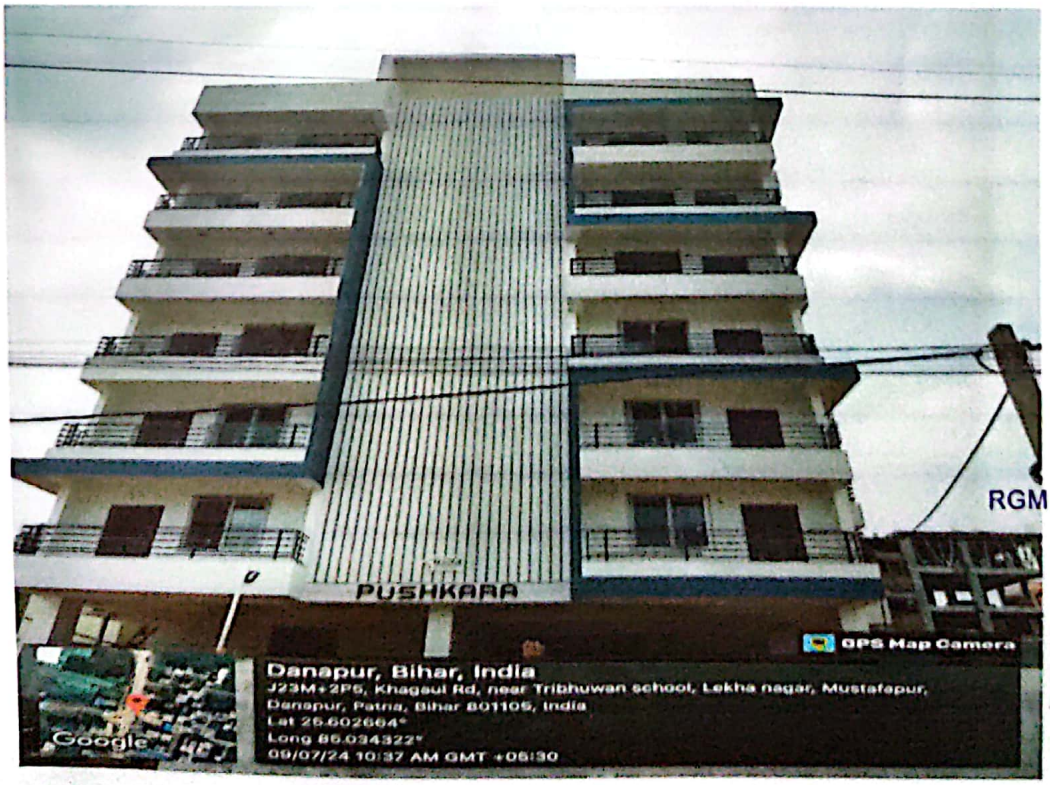

RGM Residency Pvt. Ltd.

Director

CamScanner

X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	921020024870117
2.	Estimated Cost of the Project including land cost at the start of the Project	6,80,00,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	5,40,00,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project.	N/A
5.	Amount received during the Quarter	45,23,891=00
6.	Actual Cost Incurred during the Quarter	43,06,165=50
7.	Net amount at end of the Quarter	5,73,537=35
8.	Total expenditure on Project till date	1,81,42,608=70
9.	Cumulative fund collected till the end of Quarter in question	1,26,49,891=00
10.	Cumulative expenditure done till the end of Quarter in question	1,81,42,608=70

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	N/A
2.	Name of Parties	N/A
3.	No of Execution Cases against this project Case No. Name of Parties	N/A
4.	No of Suo - Moto cases against this project Case No. Name of Parties	N/A
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	N/A

RGM Residency Pvt. Ltd.

Director

CamScanner

B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	01
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

RGM Residency Pvt. L...


Director

Signature of Promoter

Name: RAJEEV ANAND


Date:


CamScanner

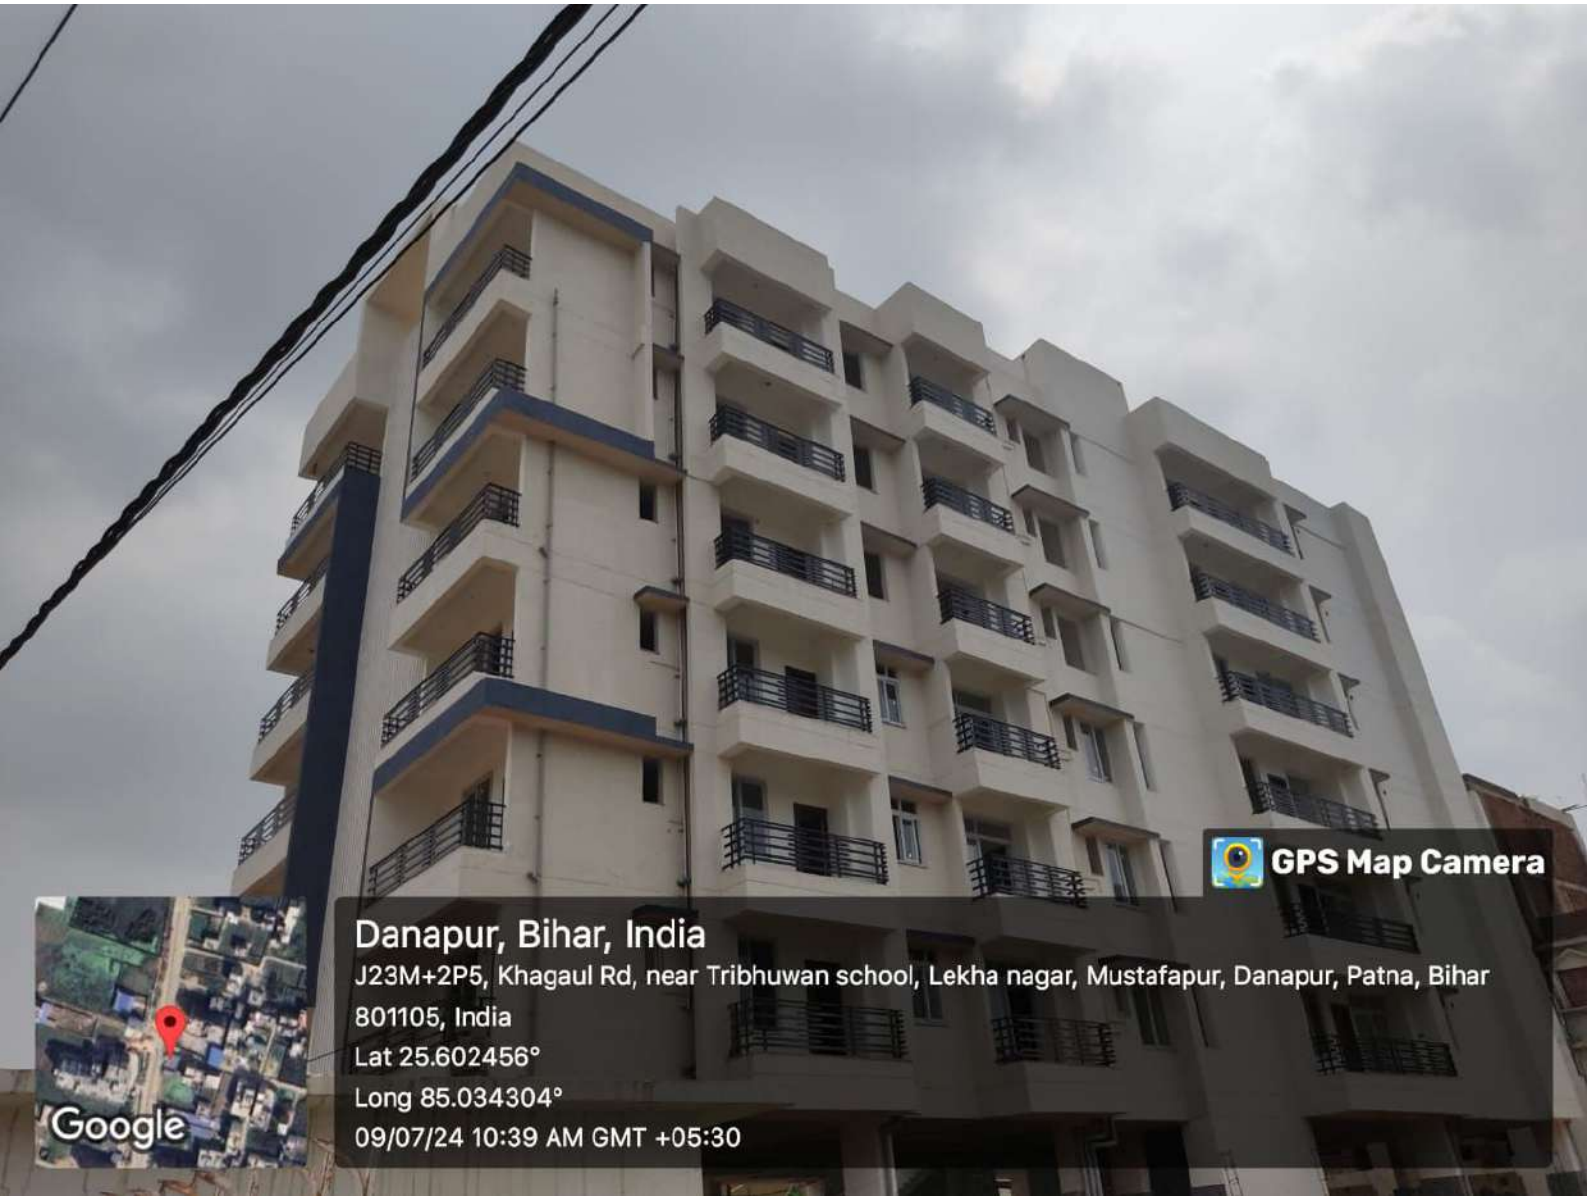
GPS Map Camera
Danapur, Bihar, India
J23M+2P5, Khagaul Rd, near Tribhuwan school, Lekha nagar, Mustafapur, Danapur, Patna, Bihar 801105, India
Lat 25.602456°
Long 85.034304°
09/07/24 10:39 AM GMT +05:30
Google


PUSHKARA
GPS Map Camera
Danapur, Bihar, India
J23M+2P5, Khagaul Rd, near Tribhuwan school, Lekha nagar, Mustafapur,
Danapur, Patna, Bihar 801105, India
Lat 25.602664°
Long 85.034322°
09/07/24 10:37 AM GMT +05:30
Google


GPS Map Camera
Patna, Bihar, India
J22M+VC5, Ashopur, Patna, Jamsaut, Bihar 801503, India
Lat 25.602203°
Long 85.034147°
09/07/24 10:30 AM GMT +05:30
Google

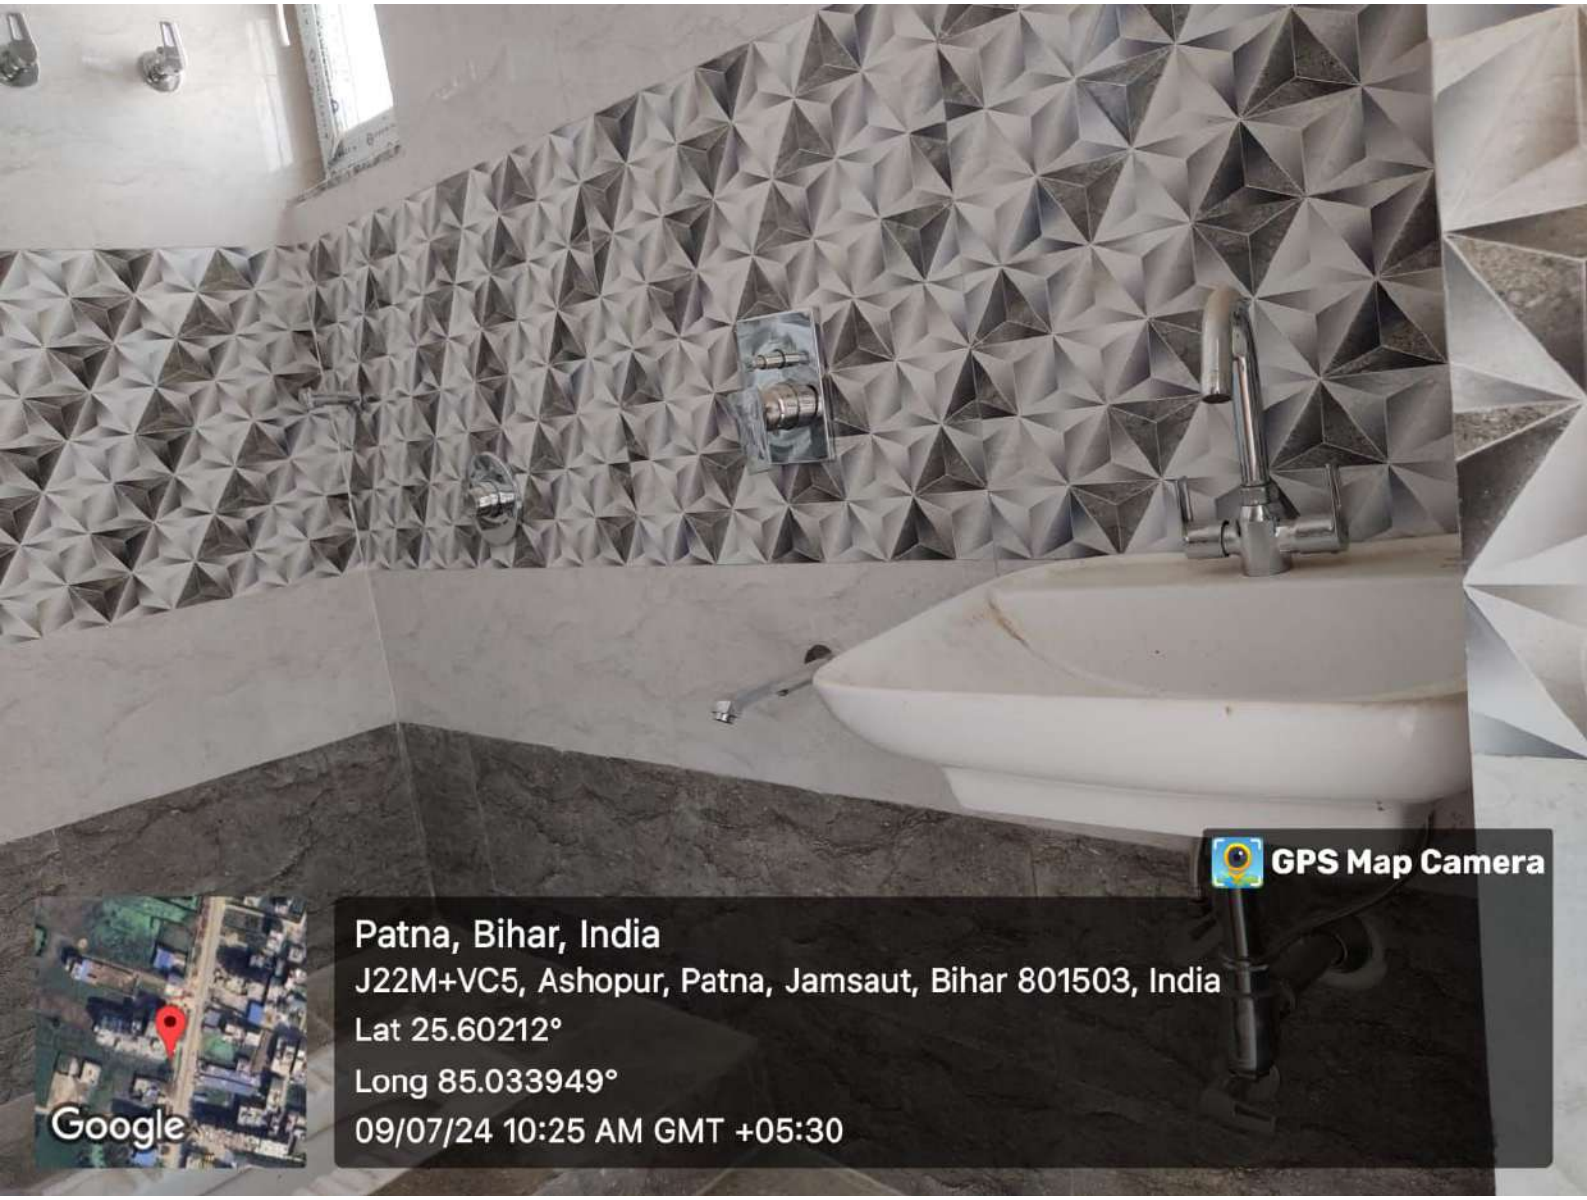
GPS Map Camera
Patna, Bihar, India
J22M+VC5, Ashopur, Patna, Jamsaut, Bihar 801503, India
Lat 25.60212°
Long 85.033949°
09/07/24 10:25 AM GMT +05:30
Google

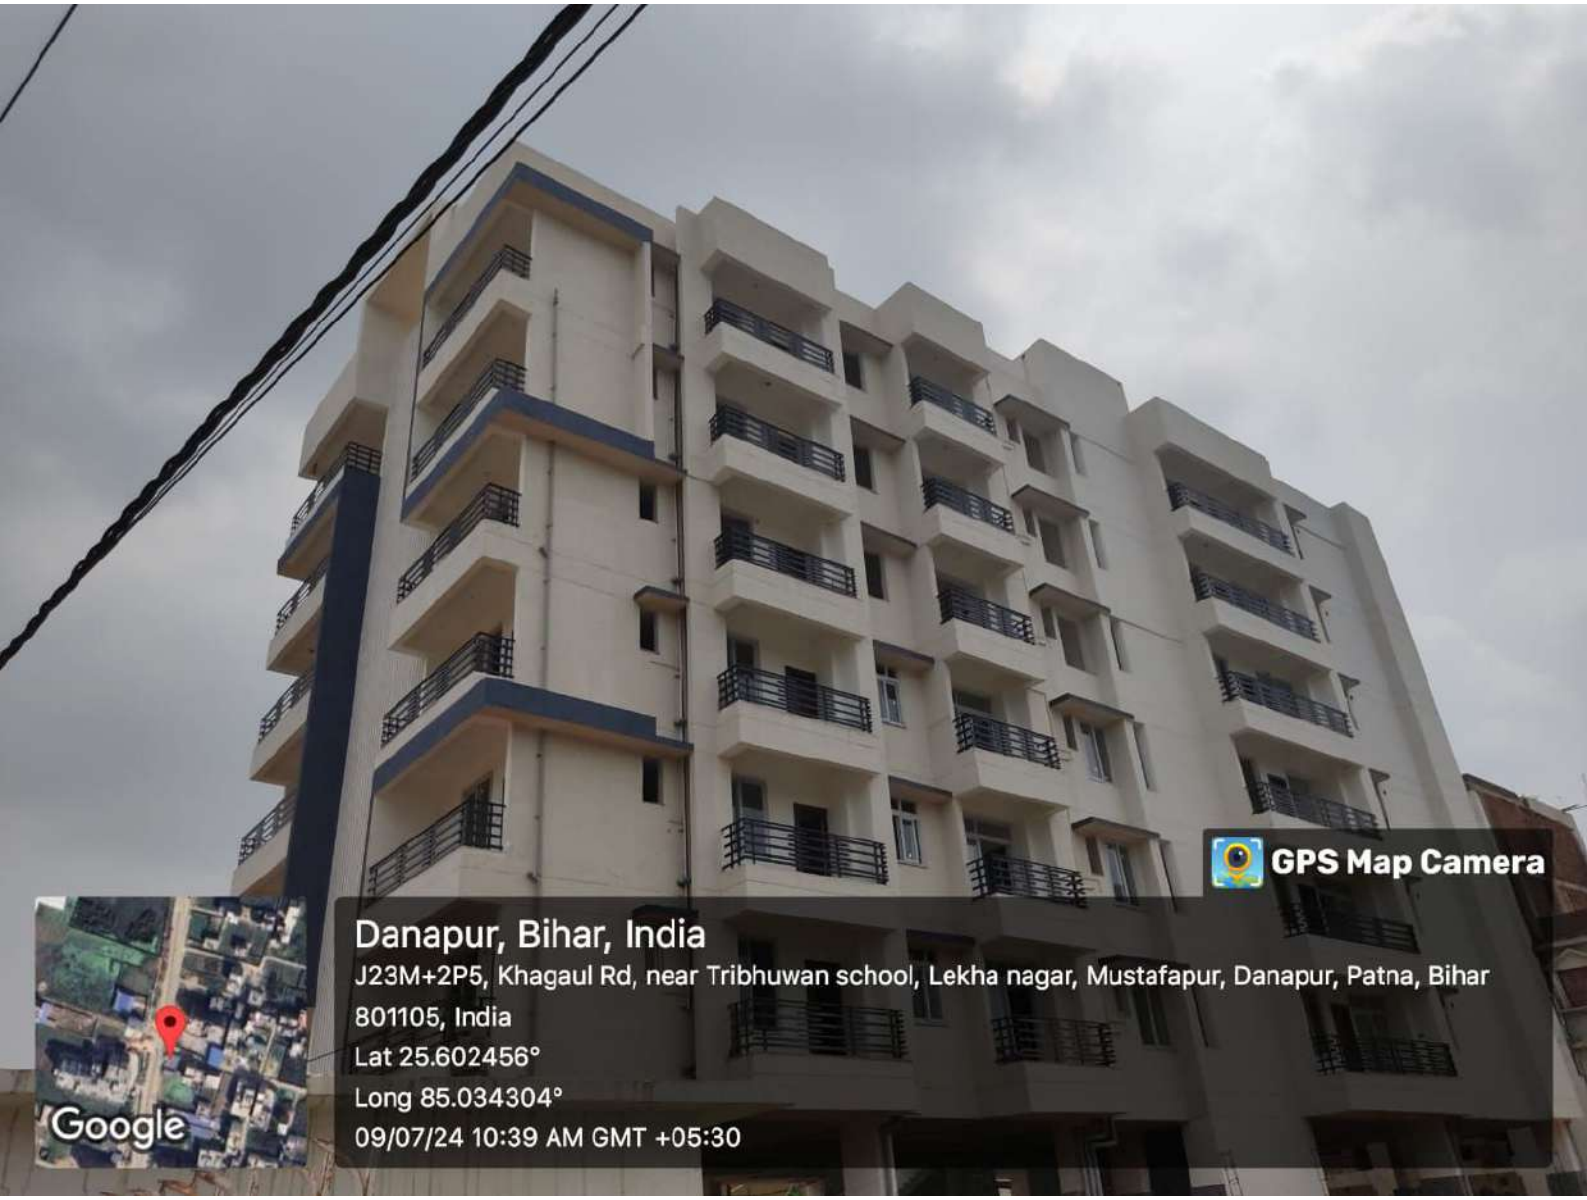
GPS Map Camera
Danapur, Bihar, India
J23M+2P5, Khagaul Rd, near Tribhuwan school, Lekha nagar, Mustafapur, Danapur, Patna, Bihar 801105, India
Lat 25.602456°
Long 85.034304°
09/07/24 10:39 AM GMT +05:30
Google
