FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending June of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U45200BR2007PTC013287	Name of Firm	YASH LAXMI ENTERPRISES PVT LTD
Firm Address :	185/ B SHRI KRISHANA PURI , SAHDEV MAHTO MARG BORING ROAD, PATNA, BIHAR, INDIA - 800001		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA			
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP0001170-01/1128/R-935/2020	Name of Project/Phase of Registered Project	SHANGRILA VILLAGE
Name of Promoter	YASH LAXMI ENTERPRISES PVT LTD	Project Address	MAUZA-GANESHPUR, ANCHAL MUSHAHRI THANA-AHIYAPUR, MUZAFFARPUR
Name of Co-promoter	N/A		
Project Registration is valid up to	31/12/2024		
Starting date of Project or Phase of the Project	29/04/2020		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	3 YEARS		

YASH LAXMI ENTERPRISES P. LTD.

M. Director

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share -	Total Number of Apartments in Landowner's share -
01 TO 05 BLOCK	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.			140	1. Booked / Allotted -06 2. Sold-NIL	3. Booked/ Allotted-NIL Sold -NIL
					Percentage of booking	Percentage of booking

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
01 TO 05 BLOCK	Open -60 and Covered -120=180	1. Booked/Allotted -	
		2. Sold -	

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. _____(To beaded for each Building / Wing)

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	1st and 2nd Block -100%	

YASH LAXMI ENTERPRISES P. LTD.

M. Director

2.	Basements (if any)	NO	
3.	Podiums (if any)	1st Block-100%	
4.	Plinth	1st Block-100%	
5.	Stilt Floor	1st, 2nd, 3rd and 4th floor only 1st Block - 100% and 2nd Block-1st and 2nd floor.	
6.	Slabs of Super Structure	60%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	30%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	16%	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	0%	

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

YASH LAXMI ENTERPRISES P. LTD.

M. Director

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yy y) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES		
2.	Water Supply	YES	12%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	
4.	Storm Water Drains	YES	0%	
5.	Landscaping & Tree Planting	YES	0%	
6.	Street Lighting	YES	0%	
7.	Community Buildings	YES	0%	
8.	Treatment and Disposal of Sewage and Sullage Water	YES	0%	
9.	Solid Waste Management & Disposal	YES	0%	
10.	Water Conservation / Rain Water Harvesting	YES	0%	
11.	Energy Management	YES	0%	
12.	Fire Protection and Fire Safety Requirements	YES	0%	
13.	Closed Parking	YES	0%	
14.	Open Parking	YES	0%	
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

YASH LAXMI ENTERPRISES P. LTD.

M. Director

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX.	GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT		
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

X. FINANCIAL PROGRESS OF THE PROJECT

YASH LAXMI ENTERPRISES P. LTD.

M. Director

S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	3787024366
2.	Estimated Cost of the Project including land cost at the start of the Project	27,50,00,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	15,40,000=00
6.	Actual Cost Incurred during the Quarter	17,60,925=00
7.	Net amount at end of the Quarter	
8.	Total expenditure on Project **till date**	3,30,32,949=00
9.	Cumulative fund collected till the end of Quarter in question	
10.	Cumulative expenditure done till the end of Quarter in question	

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL

YASH LAXMI ENTERPRISES P. LTD.

M. Director

3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

YASH LAXMI ENTERPRISES P. LTD.

M. Director

Signature of Promoter

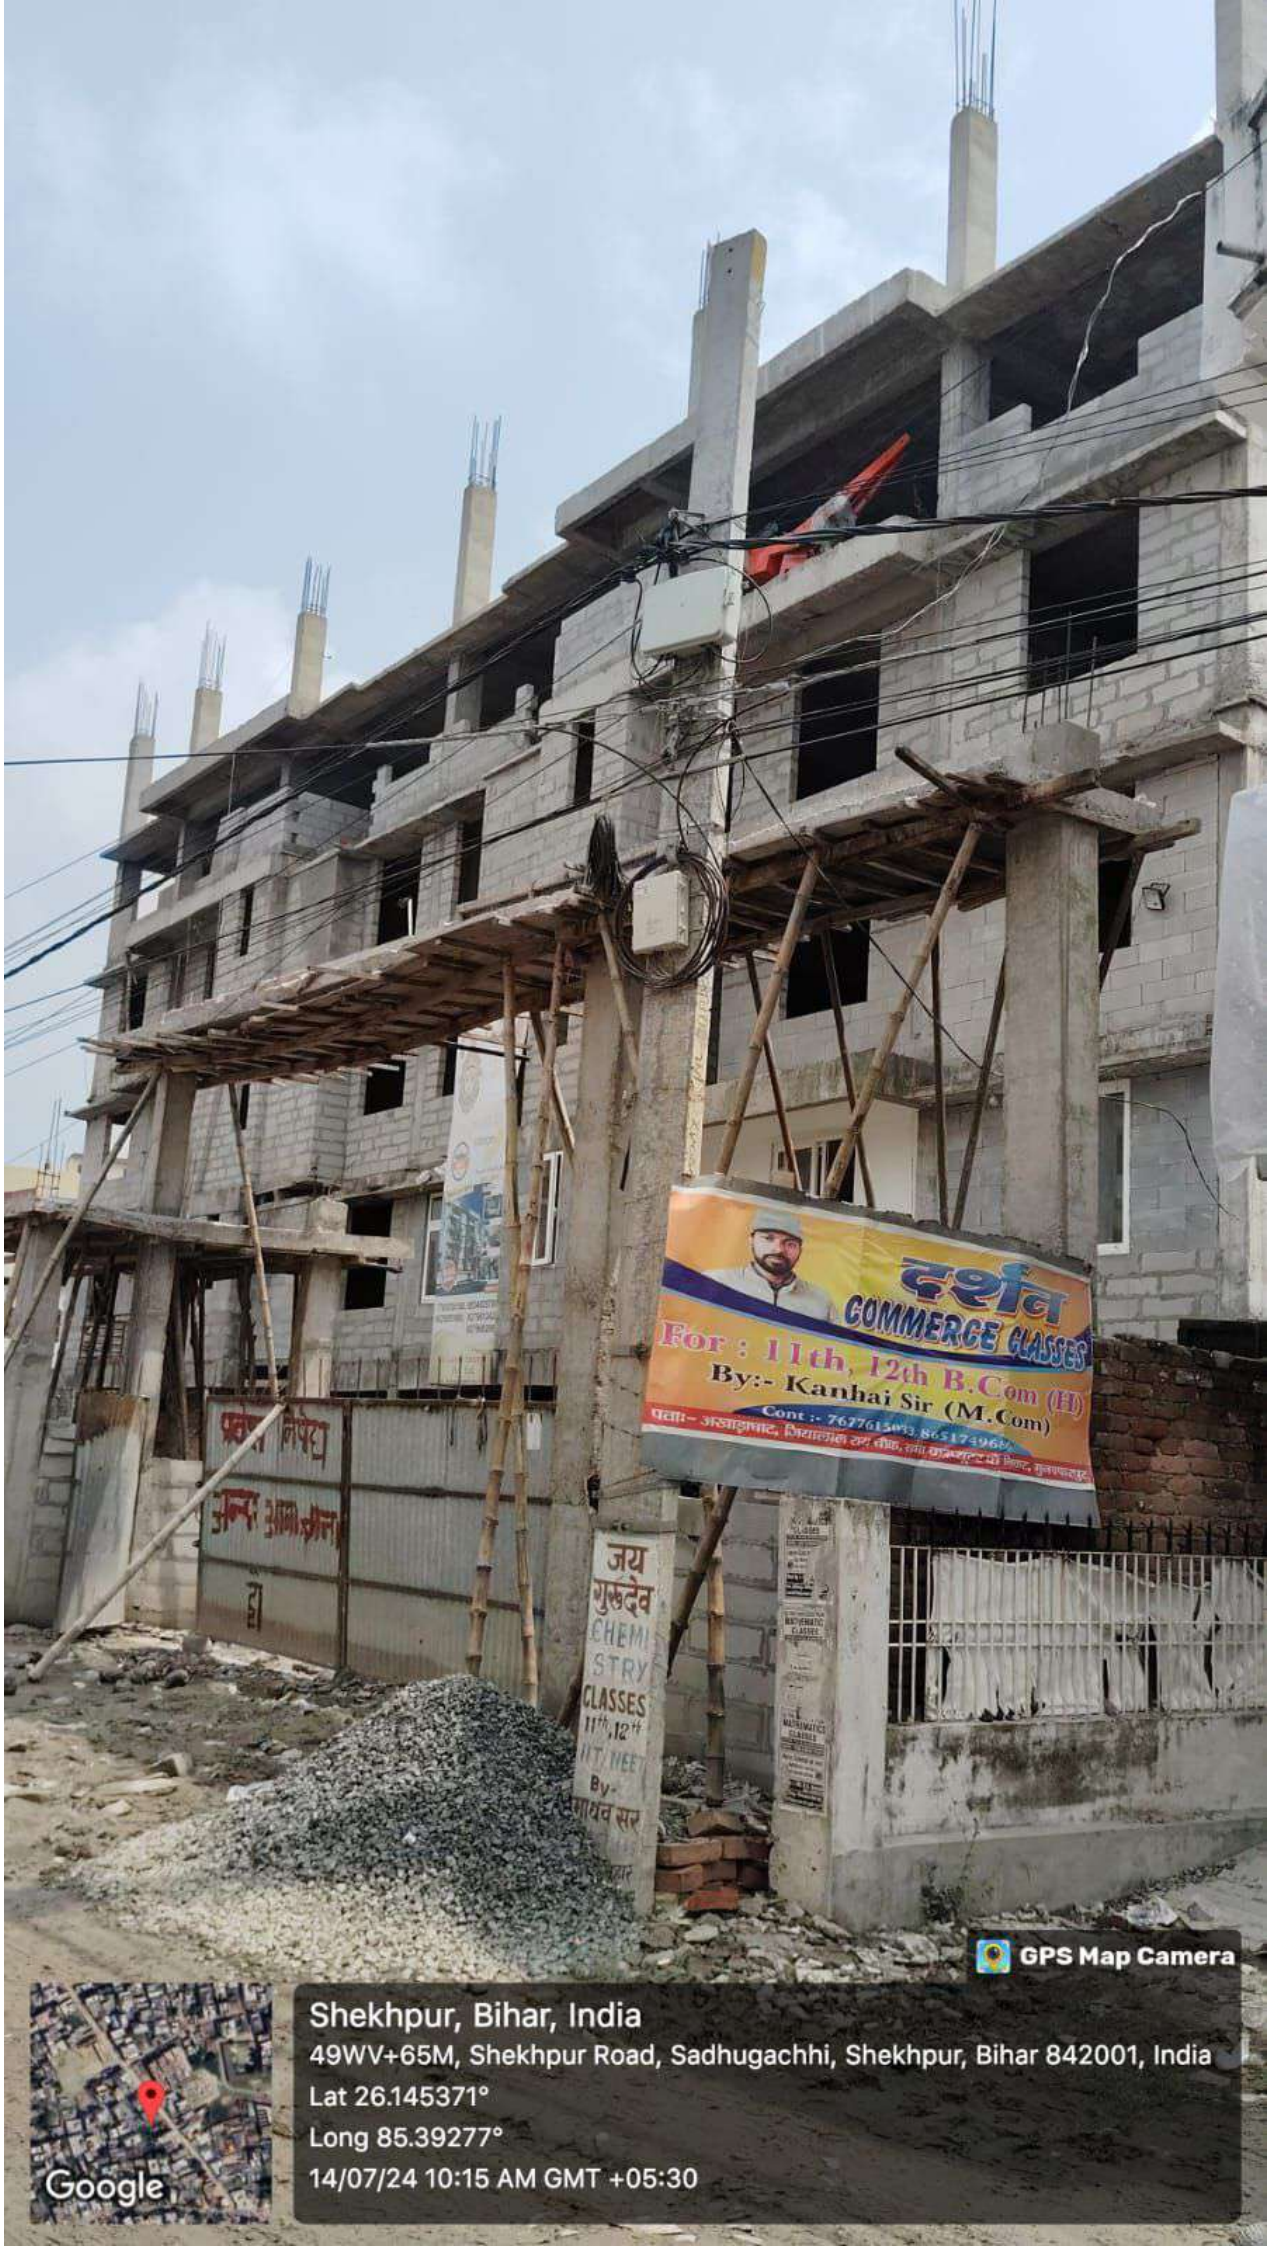
Name:

Date:


Festival Offer
GPS Map Camera
Muzaffarpur, Bihar, India
49WR+6XG, Shekhpur Road, Sadhugachhi, Muzaffarpur, Shekhpur, Bihar 842001, India
Lat 26.145503°
Long 85.392621°
14/07/24 10:18 AM GMT +05:30
Google


GPS Map Camera
Shekhpur, Bihar, India
49WV+65M, Shekhpur Road, Sadhugachhi, Shekhpur, Bihar 842001, India
Lat 26.145464°
Long 85.393042°
14/07/24 10:25 AM GMT +05:30
Google


GPS Map Camera
Shekhpur, Bihar, India
49WV+65M, Shekhpur Road, Sadhugachhi, Shekhpur, Bihar 842001, India
Lat 26.145522°
Long 85.392976°
14/07/24 10:27 AM GMT +05:30
Google


दर्शन
COMMERCE CLASSES
For : 11th, 12th B.Com (H)
By:- Kanhai Sir (M.Com)
जय गुरुदेव
CHEMI
STRY
CLASSES
GPS Map Camera
Shekhpur, Bihar, India
49WV+65M, Shekhpur Road, Sadhugachhi, Shekhpur, Bihar 842001, India
Lat 26.145371°
Long 85.39277°
14/07/24 10:15 AM GMT +05:30
Google
