FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending June of 2024 (year)

| I. PARTICULARS OF PROMOTERS | | | |
|---|---|---|---|
| Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies | CIN NO. U70109BR2014PTC023133 | Name of Firm | BALAJI DREAM HOUSE PRIVATE LIMITED |
| Firm Address : | B-34, MAGISTRATE COLONY, ROAD NO-4B, P.O-ASHIYANA, P.S-RAJEEV NAGAR, PATNA-800025 | | |
| Total Experience of promoter in Real Estate sector | | | |
| Total Experience in Real Estate after Implementation of RERA | | | |
| No of Project done Before Implementation of RERA | 1. Residential<br>2. Commercial<br>3. Residential- cum Commercial<br>4. Plotted project | | |
| No of Project done After Implementation of RERA | 1. Residential<br>2. Commercial<br>3. Residential- cum Commercial<br>4. Plotted project | | |

| II. PARTICULARS OF PROJECT | | | |
|---|---|---|---|
| Project Registration Number | BRERAP04311-2/76/R-1388/2022 | Name of Project/Phase of Registered Project | CHANDMUNI RESIDENCY |
| Name of Promoter | BALAJI DREAM HOUSE PRIVATE LIMITED | Project Address | MAUZA-BHELAI, THANA-UDAWAT NAGAR, THANA NO-228, KHATA NO-147, SURVEY PLOT NO-2130, 2131, DIST-ARAH. |
| Name of Co-promoter | N/A | | |
| Project Registration is valid up to | 14/12/2026 | | |
| Starting date of Project or Phase of the Project | 28/04/2022 | | |
| Type of Project or Phase of the Project | Residential | | |
| Period of validity of map by the Competent Authority | 3 YEARS | | |

Kamaiya Singh

Kamaiya Singh

## III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

| Building /Block Number | Apartment Type | | Carpet Area | Total Number of sanctioned apartments | Total Number of Apartments in Promoter's share - | Total Number of Apartments in Landowner's share - |
|---|---|---|---|---|---|---|
| | 1. 1 BHK | 4 | 2044.00 | | | |
| | 2. 2 BHK, - | 24 | 28080.00 | | 1. Booked / Allotted -01 | 3. Booked/ Allotted-NIL |
| | 3. 3 BHK | 48 | 54600.00 | 78 | | |
| | 4. Shop | | | | 2. Sold-NIL | Sold -NIL |
| | 5. Bungalow | | | | | |
| | 6. Plot etc. | | | | Percentage of booking | Percentage of booking 0% |

## IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

| Building / Block Number | Total Number of Sanctioned Garages | Total Number of Garages: | |
|---|---|---|---|
| | | 1. Booked/Allotted - | 01 |
| | 78 | 2. Sold - | NIL |

## V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

| S. No. | Name of the Approval / N.O.C./ Permission / Certificate | Issuing Authority | Applied Date | Issuance Date | Enclosed as Annexure No. |
|---|---|---|---|---|---|
| 1. | NOC for Environment | | | | |
| 2. | Fire N.O.C. | | | | |
| 3. | Water Supply Permission | | | | |
| 4. | NOC from Airport Authority of India | | | | |
| 5. | Other Approval(s), if any, required for the Project. | | | | |

## VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. AMAA/ARN/ZEROMILE ARA/G+6/01/2020

| S. No. (1) | Tasks/Activity (2) | Percentage of Actual Work Done (As on date of the Certificate) (3) | Expected Completion date in (dd/mm/yyy) Format |
|---|---|---|---|
| 1. | Excavation (if any) | N/A | |

| | | | |
|---|---|---|---|
| 2. | Basements (if any) | N/A | |
| 3. | Podiums (if any) | N/A | |
| 4. | Plinth | 100% | |
| 5. | Stilt Floor | Work in progress | |
| 6. | Slabs of Super Structure | 10% | |
| 7. | Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises. | 0% | |
| 8. | Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises | 0% | |
| 9. | Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks. | 0% | |
| 10. | External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing. | 0% | |
| 11. | Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale.<br><br>Any other activities | 0% | |

## VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

Kanhaiya Sith

| S. No. | Common Areas and Facilities | Proposed (Yes/No) | Percentage of actual Work Done (As on date of the Certificate) | Expected Completion date in (dd/mm/yyy) Format |
|---|---|---|---|---|
| (1) | (2) | (3) | (4) | (5) |
| 1. | Internal Roads & Footpaths | YES | 0% | |
| 2. | Water Supply | YES | 0% | |
| 3. | Sewerage (Chamber, Line, Septic Tank, STP) | YES | 0% | |
| 4. | Storm Water Drains | NO | | |
| 5. | Landscaping & Tree Planting | YES | 0% | |
| 6. | Street Lighting | YES | 0% | |
| 7. | Community Buildings | NO | | |
| 8. | Treatment and Disposal of Sewage and Sullage Water | NO | | |
| 9. | Solid Waste Management & Disposal | YES | 0% | |
| 10. | Water Conservation / Rain Water Harvesting | YES | 0% | |
| 11. | Energy Management | YES | 0% | |
| 12. | Fire Protection and Fire Safety Requirements | YES | 0% | |
| 13. | Closed Parking | YES | 0% | |
| 14. | Open Parking | NO | | |
| 15. | Electrical Meter Room, Sub-Station, Receiving Station | | | |
| 16. | Others (Option to Add More) | | | |

**VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT**

Kanhaiya Singh

| | | PROPOSED YES/NO. | PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate) | Expected Completion date in (dd/mm/yy) Format |
|---|---|---|---|---|
| 1. | Internal Roads and foot paths | | | |
| 2. | Water Supply | | | |
| 3. | Sewerage Chambers Septic Tank | | | |
| 4 | Drains | | | |
| 5. | Parks, Land Scaping and Tree Planting | | | |
| 6. | Street Lighting | | | |
| 7. | Disposal of sewage & sullage water | | | |
| 8. | Water conservation/Rain Water Harvesting | | | |
| 9. | Energy Management | | | |

| IX. | GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT | | |
|---|---|---|---|
| (A) | Sr. No. | | |
| | 1. | Front Elevation | Attach |
| | 2. | Rear Elevation | Attach |
| | 3. | Side Elevation | Attach |
| (B) | | Photograph of each floor | |

## X. FINANCIAL PROGRESS OF THE PROJECT

Kanhaiya Singh

| S. No.<br>(1) | Particulars<br>(2) | Amount (In Rs.)<br>(3) |
|---|---|---|
| 1. | Project Account No. | 7118153502 |
| 2. | Estimated Cost of the Project including land cost at the start of the Project | 3,00,00,000=00 |
| 3. | Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost) | 1,75,00,000=00 |
| 4. | Any Variation in Development Cost which is declared at the start of the Project . | N/A |
| 5. | Amount received during the Quarter | 4,00,000=00 |
| 6. | Actual Cost Incurred during the Quarter | 0=00 |
| 7. | Net amount at end of the Quarter | 4,00,000=00 |
| 8. | Total expenditure on Project **till date** | |
| 9. | Cumulative fund collected till the end of Quarter in question | |
| 10. | Cumulative expenditure done till the end of Quarter in question | |

| **XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED** |
|---|
| |
| |

| **XII. MISCELLANEOUS** | | |
|---|---|---|
| **A** | List of Legal Cases (if any) – On Project / Promoter | |
| 1. | Case No. | NO |
| 2. | Name of Parties | NO |
| 3. | No of Execution Cases against this project<br>Case No.<br>Name of Parties | NO |
| 4. | No of Suo - Moto cases against this project<br>Case No.<br>Name of Parties | NO |
| 5. | No of Certificate cases /PDR cases against this project<br>Case No.<br>Name of Parties | NO |
| **B** | Sale/Agreement for Sale during the Quarter | |
| 1. | Sale Deed | NIL |
| 2. | Agreement for Sale | NIL |

Kanhaiya Sigh

| | | |
|---|---|---|
| 3. | No. of possessions given to allottees | NIL |
| **XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART** | | |
| Weather the project in progress is as per time schedule or lagging behind? | | |

**Undertaking:**

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Kanhaiya Singh

Signature of Promoter

Name: KANHAIYA SINGH

Date:


GPS Map Camera
Arrah, Bihar, India
GJMW+PHJ, near Zero Mile, Sarvodaya Nagar, Jagdev Nagar, Arrah, Bihar 802301, India
Lat 25.53448°
Long 84.645848°
28/06/24 10:34 AM GMT +05:30
Google

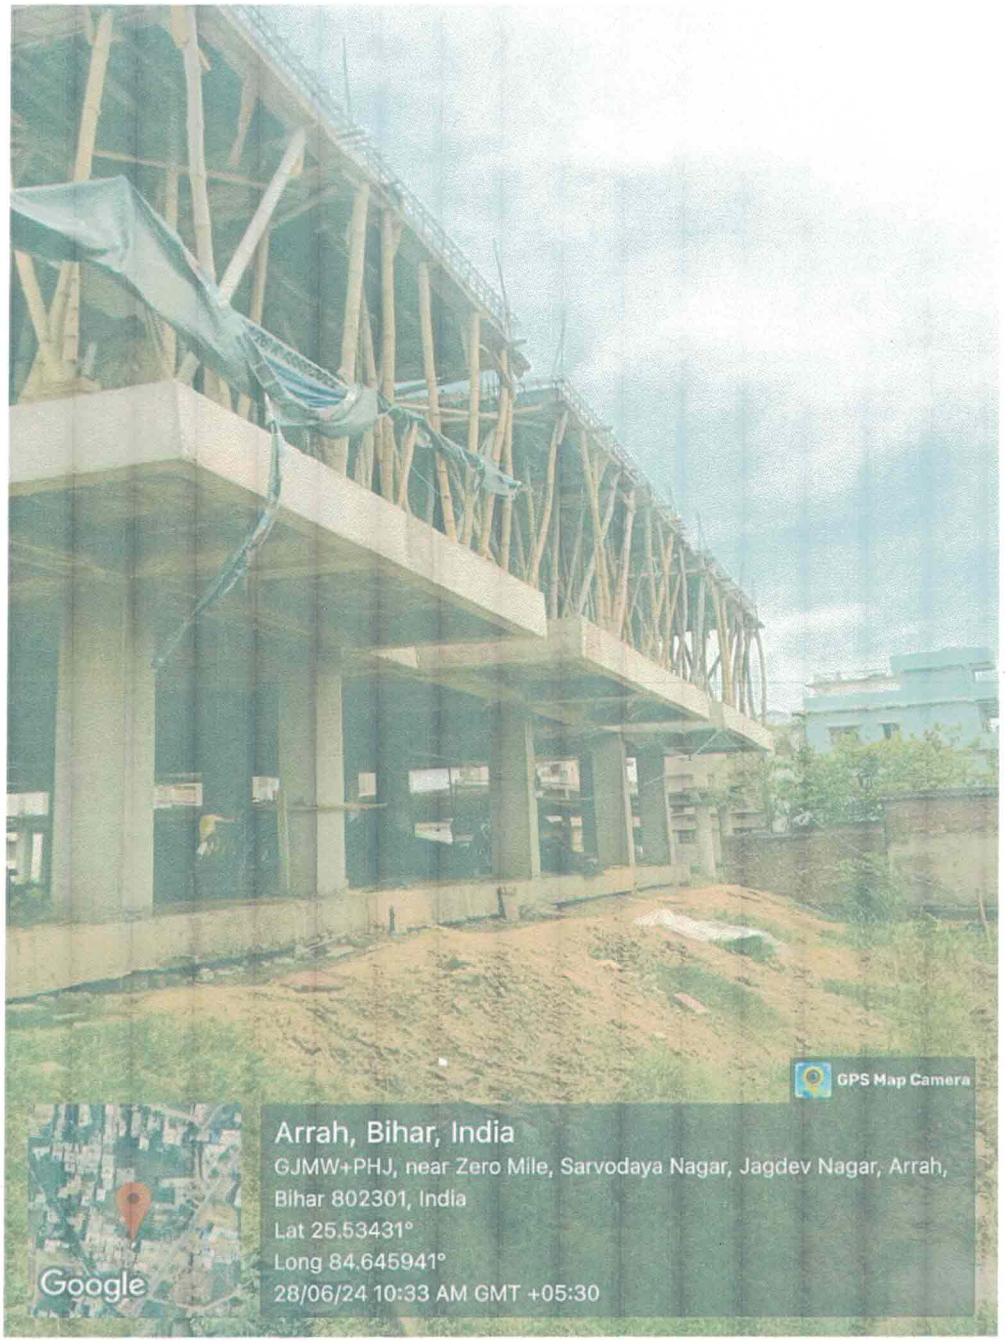
GPS Map Camera
Arrah, Bihar, India
GJMW+PHJ, near Zero Mile, Sarvodaya Nagar, Jagdev Nagar, Arrah, Bihar 802301, India
Lat 25.53431°
Long 84.645941°
28/06/24 10:33 AM GMT +05:30
Google
