FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U45209BR2018PTC038155	Name of Firm	FLORIAN CONSTRUCTION PRIVATE LIMITED
Firm Address :	C/O- MUNDRIKA PANDEY, SALIMPUR, DUMARA SHIKHPURA, NEW CAPITAL, P.O.-B.V.COLLEGE , PATNA, BIHAR, INDIA - 800014		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA	02 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP00907-1/222/R-1519/2023	Name of Project/Phase of Registered Project	SURAJ SUMAN
Name of Promoter	FLORIAN CONSTRUCTION PRIVATE LIMITED	Project Address	MITHILA COLONY, MAUZA-DIGHA, P.S. –DANAPUR, PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	25/01/2028		
Starting date of Project or Phase of the Project	23/01/2023		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	21-07-2027		

FLORIAN CONSTRUCTION PVT. LTD

Prem Kumar

DIRECTOR

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - FLAT-39	Total Number of Apartments in Landowner's share - FLAT-44
BLOCK-A, B AND C	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. 4 BHK- 5. Shop 6. Bungalow 7. Plot etc.	20 57 06		83	1. Booked / Allotted – BLOCK-C-04 BLOCK-B-02 Percentage of booking 15.38%	3. Booked/ Allotted-NIL Sold -NIL Percentage of booking 0%

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
BLOCK-A, B AND C	83	1. Booked/Allotted -	06
		2. Sold -	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	DIRECTOR CUM STATE FIRE OFFICER, BIHAR, PATNA		04-06-2022	
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

FLOR... CONSTRUCTION PVT. LTD.

DIRECTOR

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. 60/22-23

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)			Expected Completion date in (dd/mm/yyy) Format
		BLOCK-A	BLOCK-B	BLOCK-C	
1.	Excavation (if any)	0%	100%	100%	
2.	Basements (if any)	0%	100%		
3.	Podiums (if any)		100%		
4.	Plinth	0%	0%	100%	
5.	Stilt Floor				
6.	Slabs of Super Structure	0%	0%	60%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0%	0%	0%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%	0%	0%	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%	0%	0%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%	0%	0%	

FLORIAN CONSTRUCTION PVT. LTD.

Ram Kumar

DIRECTOR

11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	Motor pump install 0%	Motor pump install 0%	Motor pump install 0%	

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	
2.	Water Supply	YES	0%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	
4.	Storm Water Drains	NO		
5.	Landscaping & Tree Planting	YES	0%	

FLORIAN CONSTRUCTION PVT. LTD.

Ram Kumar

DIRECTOR

6.	Street Lighting	YES	0%	
7.	Community Buildings	NO		
8.	Treatment and Disposal of Sewage and Sullage Water	YES	0%	
9.	Solid Waste Management & Disposal	YES	0%	
10.	Water Conservation / Rain Water Harvesting	YES	0%	
11.	Energy Management	YES	0%	
12.	Fire Protection and Fire Safety Requirements	YES	0%	
13.	Closed Parking	YES	0%	
14.	Open Parking	NO		
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			


FLORIAN CONSTRUCTION PVT. LTD.

Ram Kumar

DIRECTOR

6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX.	GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT		
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

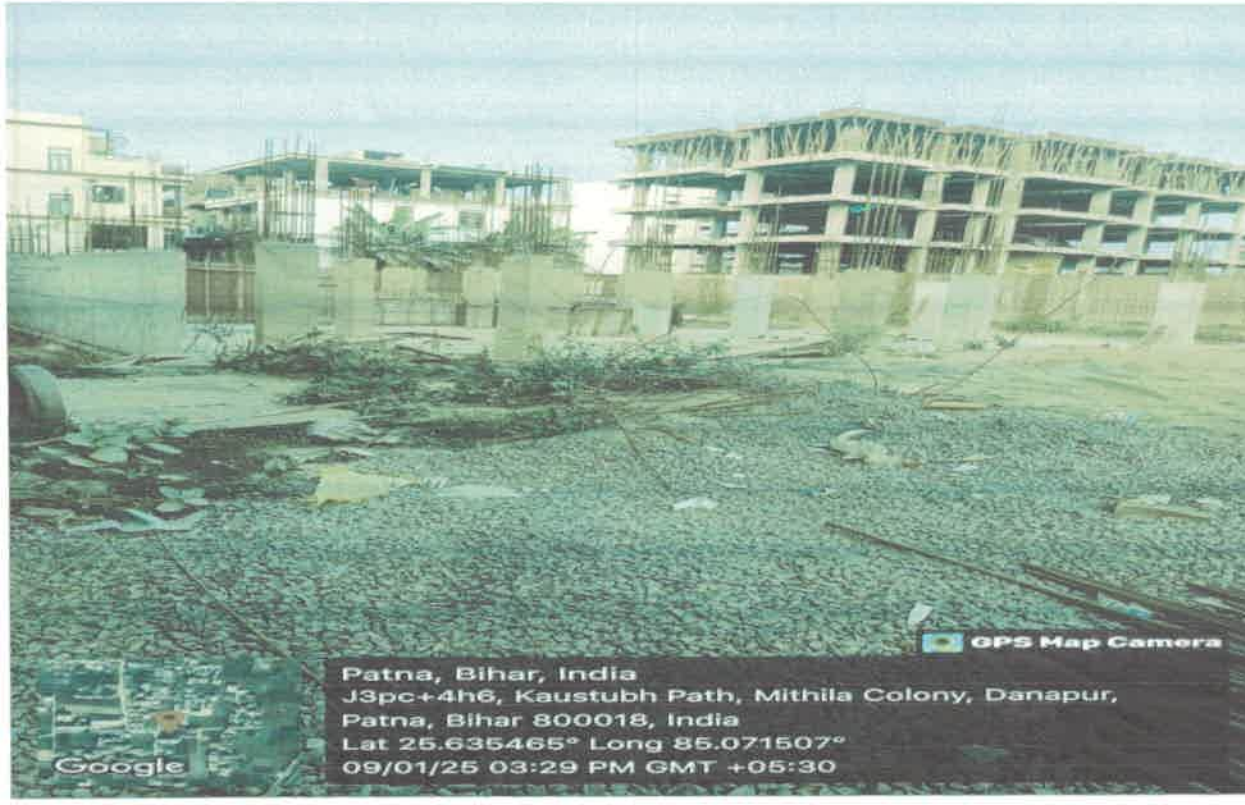

FLORIAN CONSTRUCTION PVT. LTD.

DIRECTOR





FLORIAN CONSTRUCTION PVT. LTD.

DIRECTOR

X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	41580429033
2.	Estimated Cost of the Project including land cost at the start of the Project	13,50,55,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	6,50,00,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	26,98,701.00
6.	Actual Cost Incurred during the Quarter	24,02,246=21
7.	Net amount at end of the Quarter	2,96,454=79
8.	Total expenditure on Project **till date**	2,05,07,782=41
9.	Cumulative fund collected till the end of Quarter in question	1,64,80,925=00
10.	Cumulative expenditure done till the end of Quarter in question	2,05,07,782=41

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL

2.	Agreement for Sale	06
3.	No. of possessions given to allottees	NIL

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

XIV UNITS ALLOCATION DETAILS

Total Number of sanctioned apartments	Details of allotment made so far with Flat number/ Bungalow - Plot etc		Cancellation of flat allotment, If any with Flat number/ Bungalow – Plot etc
1 BHK- 2 BHK -20 3 BHK-57 4 BHK-06 Shop- Bungalow - Plot etc	FLAT NO.	FLAT TYPE	
	BLOCK-C-303	3 BHK	
	BLOCK-C-304	3 BHK	
	BLOCK-C-305	3 BHK	
	BLOCK-C-405	3 BHK	
	BLOCK-B-301	3 BHK	
	BLOCK-B-302	3 BHK	

XV. BROCHURE /Prospectus

XVI Grievance Redressal Officer

Name : PREM KUMAR TIWARI
Contact No : 9334739262
Email id : premgg60@gmail.com
Address : C/O-MUNDRIKA PANDEY, SALIMPUR, DUMRA, SHIKHPURA, PATNA

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

FLORIAN CONSTRUCTION PVT. LTD.

Prem Kumar

Signature of Promoter DIRECTOR

Name:

Date:
