FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	LLP INDENTIFICATION NO. AAG-5805	Name of Firm	LANDMARK CONSTRUCTIONS LLP
Firm Address :	Buddha Vishweshwaraiya Industrial Training Centre Campus, Sipara, Patna-800020		
Total Experience of promoter in Real Estate sector	06 YEARS		
Total Experience in Real Estate after Implementation of RERA	06 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	NIL	
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	NIL	

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP0001920-1/1158/R-951/2020	Name of Project/Phase of Registered Project	BRIJTARA RESIDENCY
Name of Promoter	LANDMARK CONSTRUCTIONS LLP	Project Address	VISHUNPUR PAKRI, BEUR,
Name of Co-promoter	N/A		
Project Registration is valid up to	15/02/2024	(Extended upto 15-11-2024 due to COVID-19)	
Starting date of Project or Phase of the Project	05/05/2020		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the	15/02/2025		

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - Flat-12	Total Number of Apartments in Landowner's share - Flat-12
	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.	8 16	5595 15000	24	1. Booked / Allotted -03 2. Sold-NIL	3. Booked/ Allotted-NIL Sold -NIL
					Percentage of booking 25%	Percentage of booking 0%

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
	24	1. Booked/Allotted -	03
		2. Sold -	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	DIG HG & FS CUM State fire officer, Patna, Bihar	23-05-2018	12-06-2018	Annex-1
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No.PMAA/PRN/UDAIPUR/PHULWARI/G+4/124/2018

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	100%	DONE
2.	Basements (if any)	NO	N/A
3.	Podiums (if any)	NO	N/A
4.	Plinth	100%	DONE
5.	Stilt Floor	100%	DONE
6.	Slabs of Super Structure	100%	DONE
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100% 100% 65% 60%	DONE DONE 30-11-2024 30-11-2024
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	80% 50%	30-11-2024 30-11-2024
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100% 100% 80%	DONE DONE 30-11-2024
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	100% 100% 100% 100%	DONE DONE DONE DONE
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC,	30% 100% 70% 50%	30-11-2024 DONE 30-11-2024 30-11-2024 30-11-2024

	Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	50% 40%	30-11-2024 30-11-2024

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	40%	30-11-2024
2.	Water Supply	YES	80%	30-11-2024
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	80%	30-11-2024
4.	Storm Water Drains	YES	100%	DONE
5.	Landscaping & Tree Planting	YES	30%	DONE
6.	Street Lighting	YES		
7.	Community Buildings	NO	N/A	N/A
8.	Treatment and Disposal of Sewage and Sullage Water	NO	N/A	N/A
9.	Solid Waste Management & Disposal	YES		
10.	Water Conservation / Rain Water Harvesting	YES	70%	30-11-2024
11.	Energy Management	YES		


12.	Fire Protection and Fire Safety Requirements	YES	70%	30-11-2024
13.	Closed Parking	YES	100%	DONE
14.	Open Parking	NO	N/A	N/A
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	25%	30-11-2024
16.	Others (Option to Add More)	NO		

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			


IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

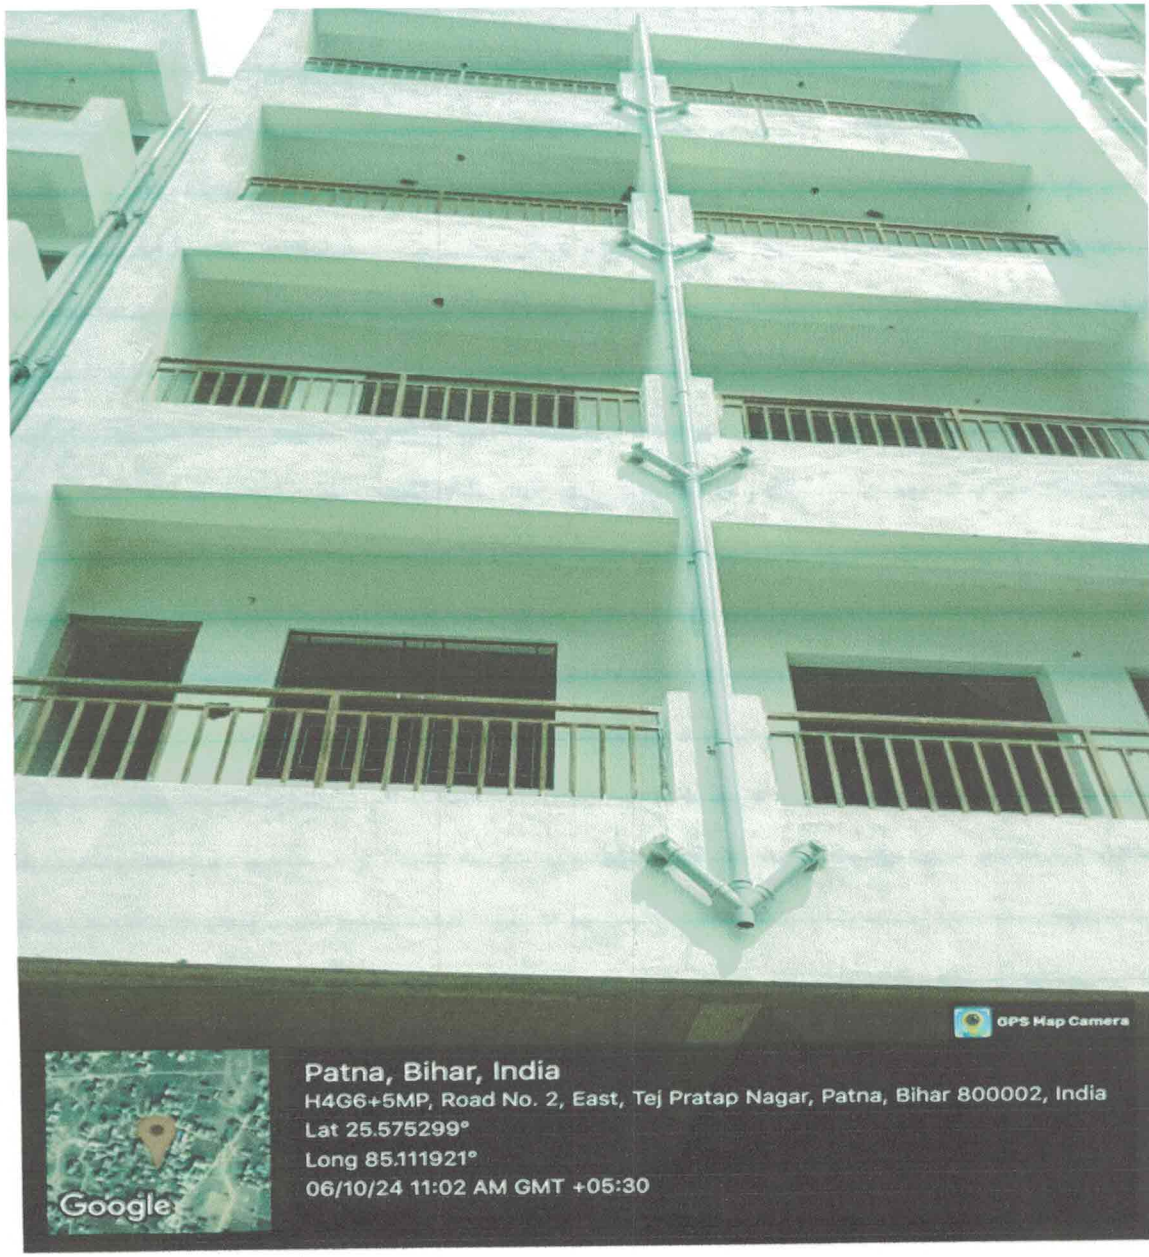

LANDMARK CONSTRUCTIONS LLP

MANAGING PARTNER

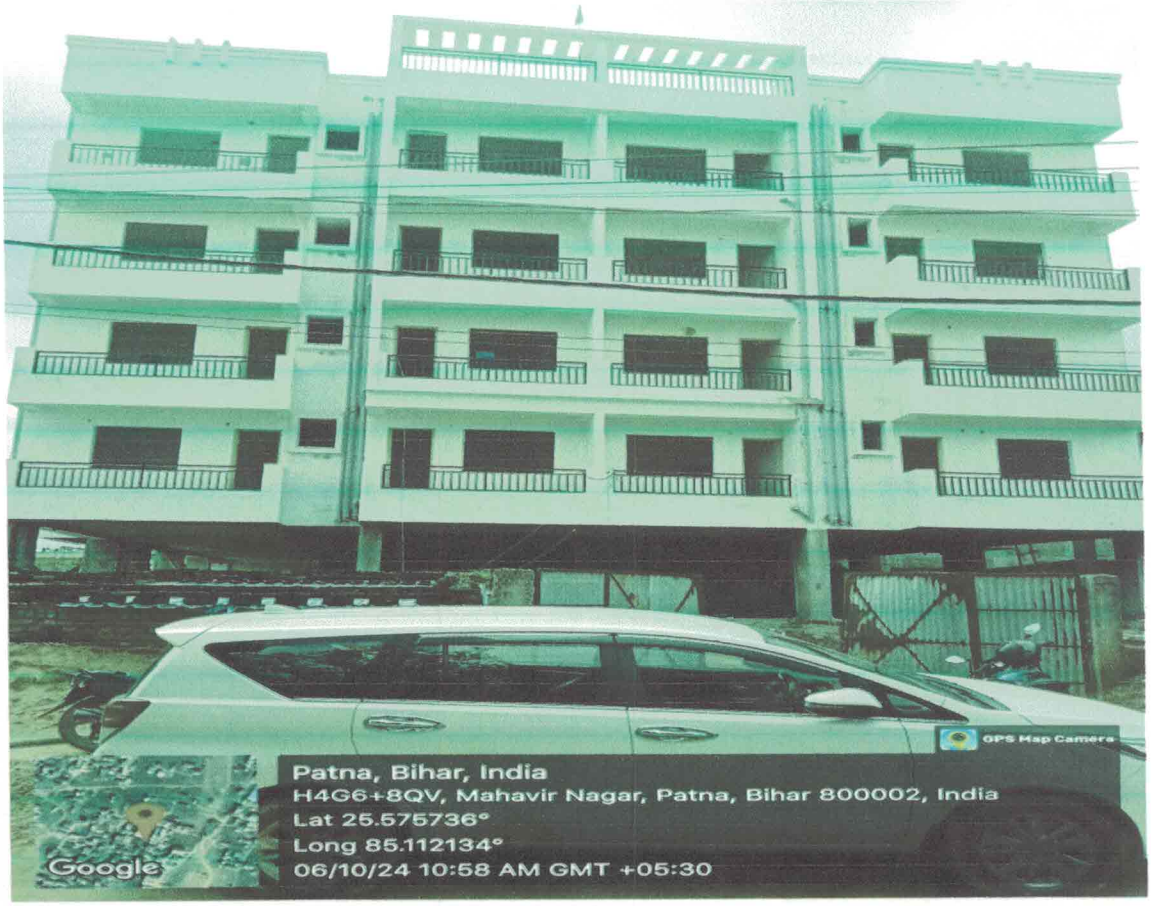



LANDMARK CONSTRUCTIONS LLP

MANAGING PARTNER



LANDMARK CONSTRUCTIONS LLP

MANAGING PARTNER

X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	300201010036899
2.	Estimated Cost of the Project including land cost at the start of the Project	7,60,00,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	5,00,00,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	NO
5.	Amount received during the Quarter	1,75,000=00
6.	Actual Cost Incurred during the Quarter	6,70,002=07
7.	Net amount at end of the Quarter	5,544=77
8.	Total expenditure on Project **till date**	79,39,924=44
9.	Cumulative fund collected till the end of Quarter in question	79,50,100=00
10.	Cumulative expenditure done till the end of Quarter in question	79,39,924=44

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	01
3.	No. of possessions given to allottees	NIL

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART
Weather the project in progress is as per time schedule or lagging behind?

XIV UNITS ALLOCATION DETAILS

Total Number of sanctioned apartments	Details of allotment made so far with Flat number/ Bungalow - Plot etc		Cancellation of flat allotment, If any with Flat number/ Bungalow – Plot etc
1 BHK- 2 BHK-08 3 BHK-16 4 BHK- Shop- Bungalow - Plot etc	FLAT NO.	FLAT TYPE	
	101	3BHK	
	106	2BHK	
	301	3BHK	

XV. BROCHURE /Prospectus

XVI Grievance Redressal Officer

Name : RAJIV RANJAN

Contact No : 9308702454

Email id : rajivclassic111@gmail.com

Address : BUDDHA VISHWASARAIYA, ITT CAMPUS, SIPARA, BEUR

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

LANDMARK CONSTRUCTIONS LLP

MANAGING PARTNER

Signature of Promoter

Name:

Date:
