FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	PARTNERSHIP DEED NO.-24/2021	Name of Firm	MITTAL INFRASPACES
Firm Address :	ALOK AGRAWAL,4 RAI GOPAL SARKAR LANE, NAYA BAZAR, BHAGALPUR		
Total Experience of promoter in Real Estate sector	08YEARS		
Total Experience in Real Estate after Implementation of RERA	07 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential-cum Commercial 4. Plotted project	NIL	
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential-cum Commercial 4. Plotted project	TWO RESIDENTIAL CUM COMMERCIAL PROJECTS	

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP81137-002/61/R-1577/2023	Name of Project/Phase of Registered Project	A.S TOWER
Name of Promoter	MITTAL INFRASPACES	Project Address	MAHESHPUR, ALIGANJ, MAUZA-BANSI ROAD, BHAGALPUR
Name of Co-promoter	N/A		
Project Registration is valid up to	16-01-2028		
Starting date of Project or Phase of the Project	15-09-2023		
Type of Project or Phase of the Project	Commercial		
Period of validity of map by the Competent Authority	16-01-2028		

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

MITTAL INFRASPACES

PARTNER

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - 10	Total Number of Apartments in Landowner's share - 09
	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow - 6. Plot etc.	19		SHOP/OFFICE -19	1. Booked / Allotted -02 2. Sold-NIL	3. Booked/ Allotted - NIL Sold -NIL
					Percentage of booking 20%	Percentage of booking 0%

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted -	
		2. Sold -	

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	DIRECTOR-CUM-STATE FIRE OFFICER, BIHAR, PATNA		22-08-2022	
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

VI. CONSTRUCTION PROGRESS OF THE PROJECT

MITTAL INFRASPACES

PARTNER

1. Plan Case No. 231/22-23			
S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	100%	
3.	Podiums (if any)		
4.	Plinth	100%	
5.	Stilt Floor		
6.	Slabs of Super Structure	16.66% 5%	10/12/2025
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	5% 0% 0% 0%	15/03/2026 10/07/2026 15/07/2027 15/09/2027
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0% 0%	15/09/2027 15/09/2027
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	17% 17% 0%	10/07/2027 15/12/2027 15/10/2027
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0% 0% 0% 0%	19/12/2027 10/03/2027 15/12/2027 12/12/2027
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing.	0% 100% 0% 0% 0% 0%	15/12/2027 10/12/2027 10/10/2027 15/12/2027 10/10/2027

MITTAL INFRASPACES

PARTNER

	Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities		

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	20%	15/12/2027
2.	Water Supply	YES	10%	10/10/2027
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	10/10/2027
4.	Storm Water Drains	YES	0%	
5.	Landscaping & Tree Planting	YES	0%	15/10/2027
6.	Street Lighting	YES	0%	10/11/27
7.	Community Buildings	NO		
8.	Treatment and Disposal of Sewage and Sullage Water	YES	0%	
9.	Solid Waste Management & Disposal	YES	0%	15/12/2027
10.	Water Conservation / Rain Water Harvesting	YES	0%	10/11/2027
11.	Energy Management	YES	0%	10/11/2027

MITTAL INFRASPACES

PARTNER

12.	Fire Protection and Fire Safety Requirements	YES	0%	15/12/2027
13.	Closed Parking	YES	0%	10/12/2027
14.	Open Parking	NO		
15.	Electrical Meter Room, Sub-Station, Receiving Station	NO		
16.	Others (Option to Add More)			


VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

MITTAL INFRASPACES

PARTNER

IX.	GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT		
(A)	Sr. No.		
	1.	Front Elevation	ATTACH
	2.	Rear Elevation	ATTACH
	3.	Side Elevation	ATTACH
(B)		Photograph of each floor	

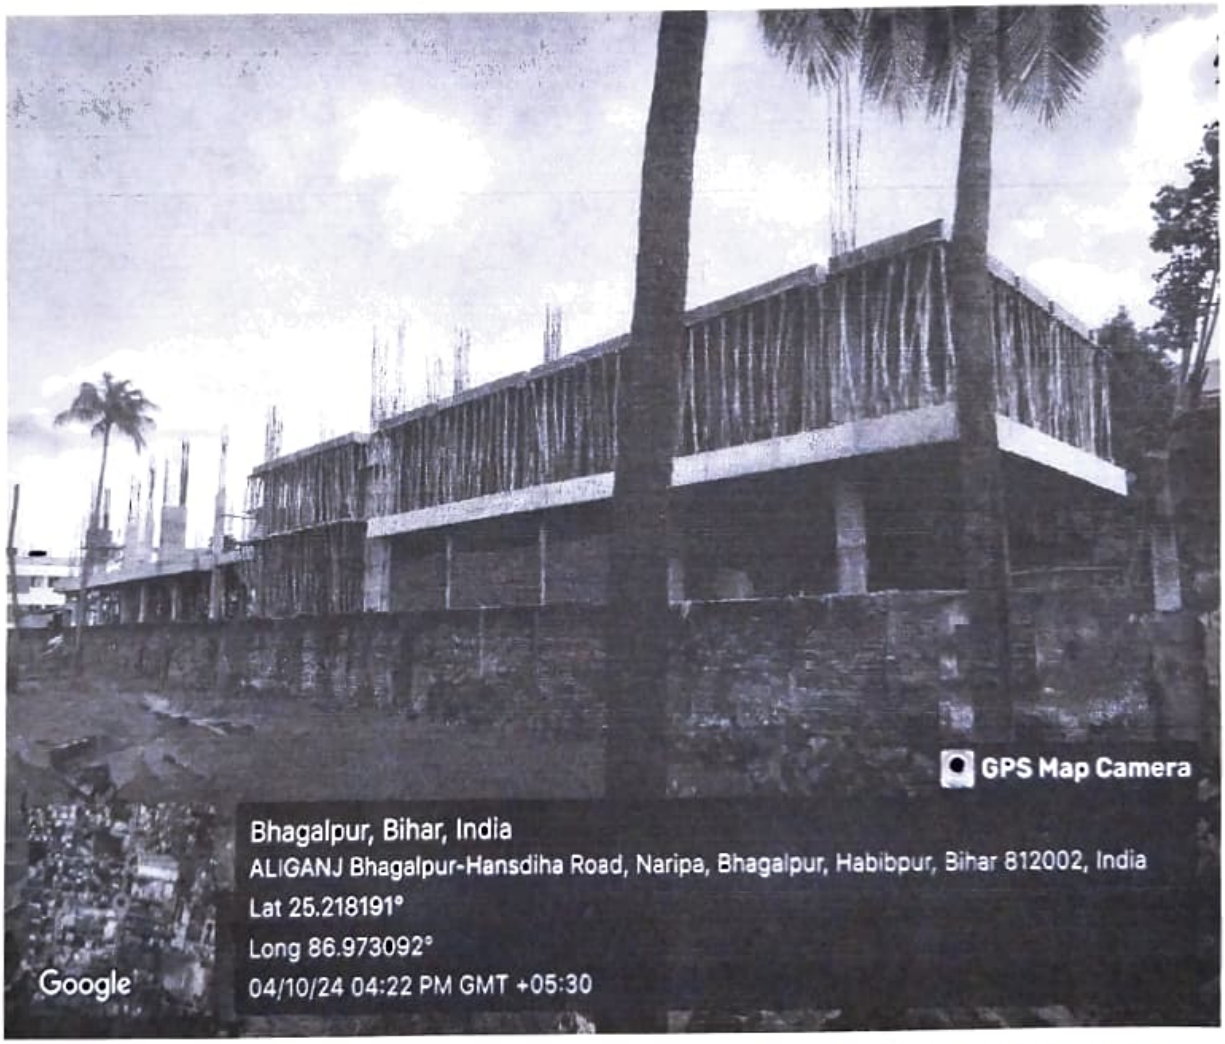

MITTAL INFRASPACES

PARTNER





MITTAL INFRASPACES

PARTNER

X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	250019121969
2.	Estimated Cost of the Project including land cost at the start of the Project	11,56,45,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	6,59,00,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	8,36,500=00
6.	Actual Cost Incurred during the Quarter	8,36,500=00
7.	Net amount at end of the Quarter	00=00
8.	Total expenditure on Project **till date**	2,17,39,760=00
9.	Cumulative fund collected till the end of Quarter in question	81,16,000=00
10.	Cumulative expenditure done till the end of Quarter in question	

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL

MITTAL INFRASPACES

PARTNER

2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

XIV UNITS ALLOCATION DETAILS

Total Number of sanctioned apartments
1 BHK-
2 BHK -
3 BHK-
4 BHK-
Shop- 19
Bungalow -
Plot etc

Details of allotment made so far with Flat number/ Bungalow - Plot etc

NO	TYPE
A2/1	SHOP
A2/2	SHOP
A2/3	SHOP
A3/1	SHOP
A3/3	SHOP

Cancellation of flat allotment, If any with Flat number/ Bungalow – Plot etc

NO	TYPE
A3/2	SHOP

XV. BROCHURE /Prospectus- online upload

XVI Grievance Redressal Officer

Name : ALOK AGRAWAL
Contact No : 9431213315
Email id : bgpmittalinfra@gmail.com
Address : ALOK AGRAWAL,4 RAI GOPAL SARKAR LANE, NAYA BAZAR, BHAGALPUR

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

MITTAL INFRASPACES
alok agrawal
PARTNER

Signature of Promoter

Name: ALOK AGRAWAL

Date: 13/10/2024
