
FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending June of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U45200BR2009PTC014820	Name of Firm	SAEBAN CONSTRUCTION PVT LTD
Firm Address :	C/O SHRI IFTAKAR AHMAD BEG,C-1 PHULWARISHARIF PATNA-801505		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA			
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP70754-003/21/R-1694/2024	Name of Project/Phase of Registered Project	K.M.GREENS
Name of Promoter	SAEBAN CONSTRUCTION PVT LTD	Project Address	MAUZA-AKBARPUR CHHATNA, P.S,. PARSA BAZAR, PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	07-07-2028		
Starting date of Project or Phase of the Project	22-05-2024		
Type of Project or Phase of the Project	1. Residential 2. Commercial 3. Residential-cum-Commercial 4, Plotted project		
Period of validity of map by the Competent Authority	07-07-2028		



III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - FLAT-40	Total Number of Apartments in Landowner's share - FLAT-40
	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.	16 64		Flat- 80	1. Booked / Allotted -NIL 2. Sold-NIL	3. Booked/ Allotted-NIL Sold -NIL
					Percentage of booking 0%	Percentage of booking 0%

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
	80	1. Booked/Allotted -	NIL
		2. Sold -	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	Director-Cum-State Fire Officer		11-07-2022	
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. PMAA/PRN/AKBARPUR CHHATANA/PARSA BAZAR/G+09/65/2021

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	0%	

2.	Basements (if any)	N/A	
3.	Podiums (if any)	0%	27-05-2025
4.	Plinth	0%	30-12-2024
5.	Stilt Floor	0%	30-03-2025
6.	Slabs of Super Structure	0%	30-12-2026
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0% 0% 0% 0%	30-08-2027 30-11-2027 27-02-2028 30-03-2028
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0% 0%	30-05-2028 30-03-2028
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0% 0% 0%	30-03-2028 30-05-2028 30-12-2027
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0% 0% 0% 0%	30-11-2027 30-10-2027 30-04-2028 30-04-2028
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	0% 0% 0% 0% 0%	30-05-2028 30-08-2024 30-05-2028 30-03-2028 30-04-2028 30-05-2028 30-06-2028

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	
2.	Water Supply	YES	0%	30-01-2028
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	30-12-2027
4.	Storm Water Drains	YES	0%	30-05-2028
5.	Landscaping & Tree Planting	YES	0%	
6.	Street Lighting	YES	0%	30-05-2028
7.	Community Buildings	NO	N/A	
8.	Treatment and Disposal of Sewage and Sullage Water	NO	N/A	
9.	Solid Waste Management & Disposal	YES	0%	30-05-2028
10.	Water Conservation / Rain Water Harvesting	YES	0%	30-05-2028
11.	Energy Management	YES	0%	27-02-2028
12.	Fire Protection and Fire Safety Requirements	YES	0%	30-05-2028
13.	Closed Parking	YES	0%	30-05-2028
14.	Open Parking			
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	30-05-2028
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT				
		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT			
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	133305003504
2.	Estimated Cost of the Project including land cost at the start of the Project	13,67,34,414=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	12,36,69,414=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	00=00
6.	Actual Cost Incurred during the Quarter	00=00
7.	Net amount at end of the Quarter	00=00
8.	Total expenditure on Project **till date**	00=00
9.	Cumulative fund collected till the end of Quarter in question	00=00
10.	Cumulative expenditure done till the end of Quarter in question	00=00

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL

2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Saehan Construction Pvt. Ltd.

Director

Signature of Promoter

Name: Shahzad Ahmad


Date:

KM Greens


GPS Map Camera
Parsa, Bihar, India
G4QC+MCV, Parsa Bazar, Punpun, Parsa, Bihar 804453, India
Lat 25.539546°
Long 85.1208°
14/08/24 04:33 PM GMT +05:30
Google


GPS Map Camera
Parsa, Bihar, India
G4QC+MCV, Parsa Bazar, Punpun, Parsa, Bihar 804453, India
Lat 25.539502°
Long 85.120859°
14/08/24 04:33 PM GMT +05:30
Google


GPS Map Camera
Parsa, Bihar, India
G4QC+MCV, Parsa Bazar, Punpun, Parsa, Bihar 804453, India
Lat 25.539548°
Long 85.120791°
14/08/24 04:33 PM GMT +05:30
Google

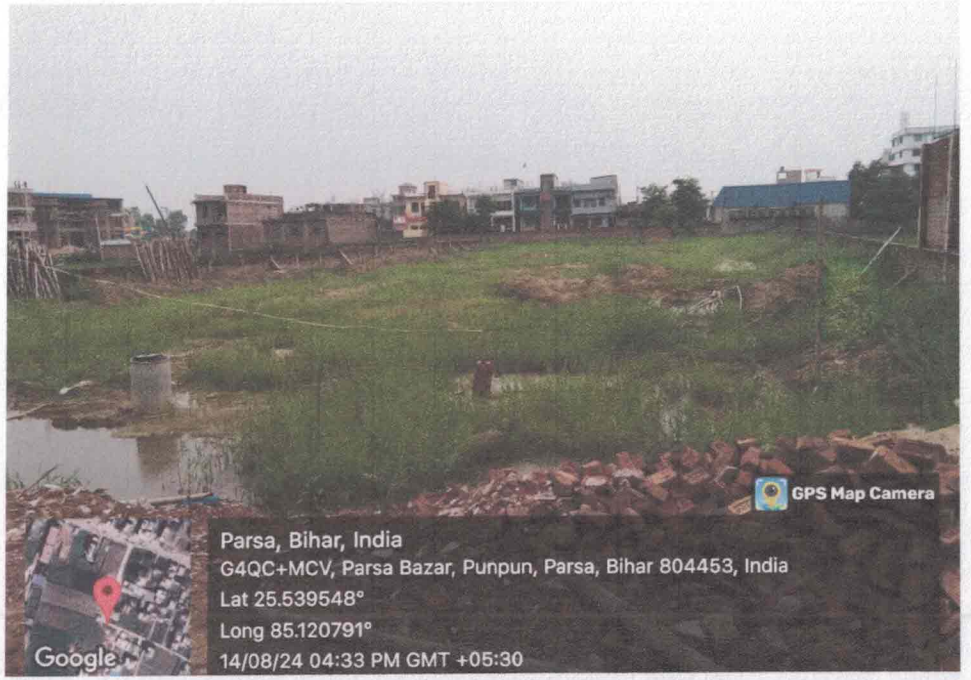
GPS Map Camera
Parsa, Bihar, India
G4QC+MCV, Parsa Bazar, Punpun, Parsa, Bihar 804453, India
Lat 25.539548°
Long 85.120791°
14/08/24 04:33 PM GMT +05:30
Google
