FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending June of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	LLPIN AAO-1133	Name of Firm	SURONDHA CONSTRUCTION LLP
Firm Address :	C/O-DHARAMJEET KUMAR, KRISHNA CHAK, GOLA ROAD, DIGHA, PATNA-801503		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA			
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP92120-1/196/R-1359/2022	Name of Project/Phase of Registered Project	J.D MANSION
Name of Promoter	SURONDHA CONSTRUCTION LLP	Project Address	MAHUABAGH, MAUZA-DHANAUT, BEHIND JHANDA MANDIR, MAHUABAGH, PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	15/02/2026		
Starting date of Project or Phase of the Project	07/04/2022		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	07/12/2024		

Surondha Construction LLP

Designated Partner

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - 09	Total Number of Apartments in Landowner's share - 10
	1. 1 BHK	1	410.00	19	1. Booked / Allotted -06 2. Sold-NIL	3. Booked/ Allotted - NIL Sold -NIL
	2. 2 BHK, -	9	5349.00			
	3. 3 BHK	9	7044.00			
	4. Shop				Percentage of booking 66%	Percentage of booking 0%
	5. Bungalow					
	6. Plot etc.					

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted -	06
	19	2. Sold -	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. P/DHANAUT-PRN-G+3/317/2021

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	N/A	

Surondha Construction LLP

Designated Partner

2.	Basements (if any)	N/A	
3.	Podiums (if any)	N/A	
4.	Plinth	100%	
5.	Stilt Floor	80%	31-12-2025
6.	Slabs of Super Structure	Four (4) 100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	Internal wall - 100% Internal Plaster -100% Flooring -80%	31-12-2024
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	Plumbing – 70% Electrical – 60%	31-12-2025
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	80%	31-12-2025
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	External Plaster - 90%	31-12-2025
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	10%	31-12-2025

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

Surondha Construction LLP

Designated Partner

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES		
2.	Water Supply	YES	40%	31-12-2025
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	31-12-2025
4.	Storm Water Drains	YES	50%	31-12-2025
5.	Landscaping & Tree Planting	YES	0%	31-12-2025
6.	Street Lighting	YES	0%	31-12-2025
7.	Community Buildings	NO		
8.	Treatment and Disposal of Sewage and Sullage Water	NO		
9.	Solid Waste Management & Disposal	YES	0%	
10.	Water Conservation / Rain Water Harvesting	YES	0%	31-01-2026
11.	Energy Management	YES	10%	31-01-2026
12.	Fire Protection and Fire Safety Requirements			
13.	Closed Parking	YES		
14.	Open Parking	NO		
15.	Electrical Meter Room, Sub-Station, Receiving Station	NO		
16.	Others (Option to Add More)			
VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT				

Surondha Construction LLP

Designated Partner


		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX.	GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT		
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	Attach

Surondha Construction LLP


Designated Partner




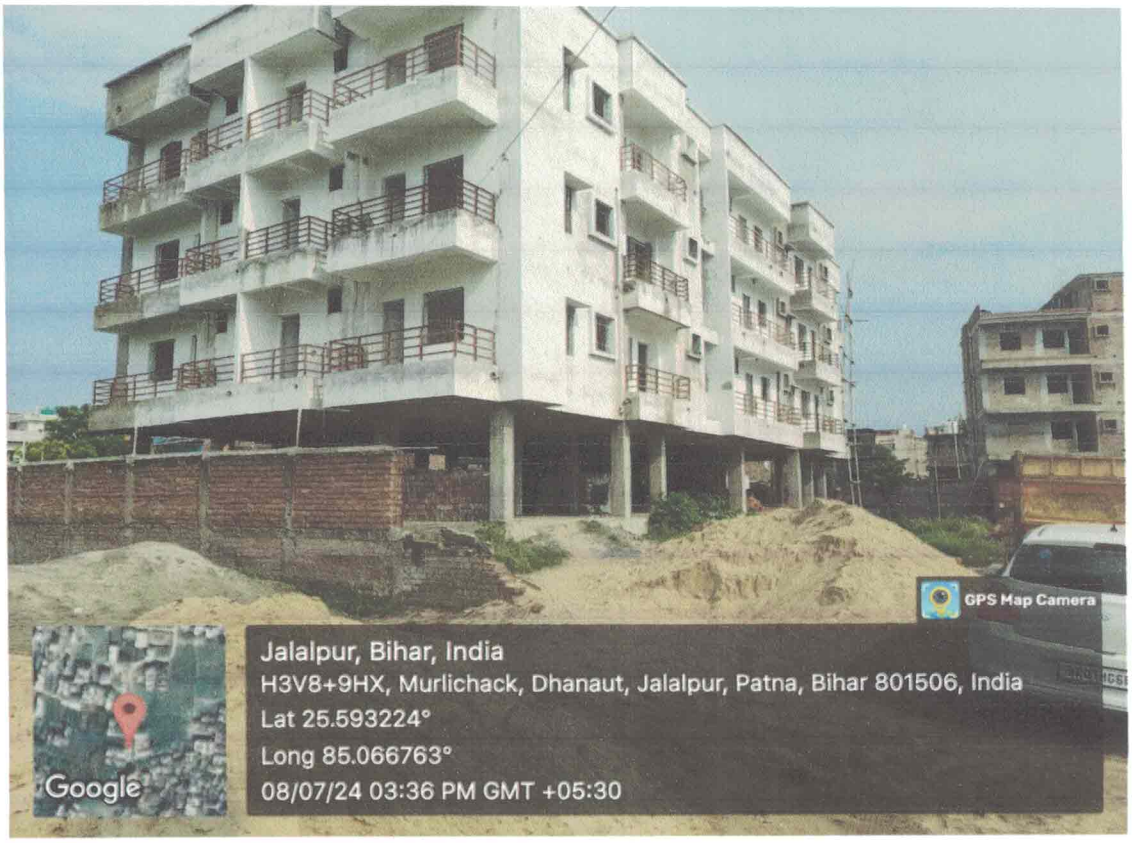

Surondha Construction LLP

Designated Partner

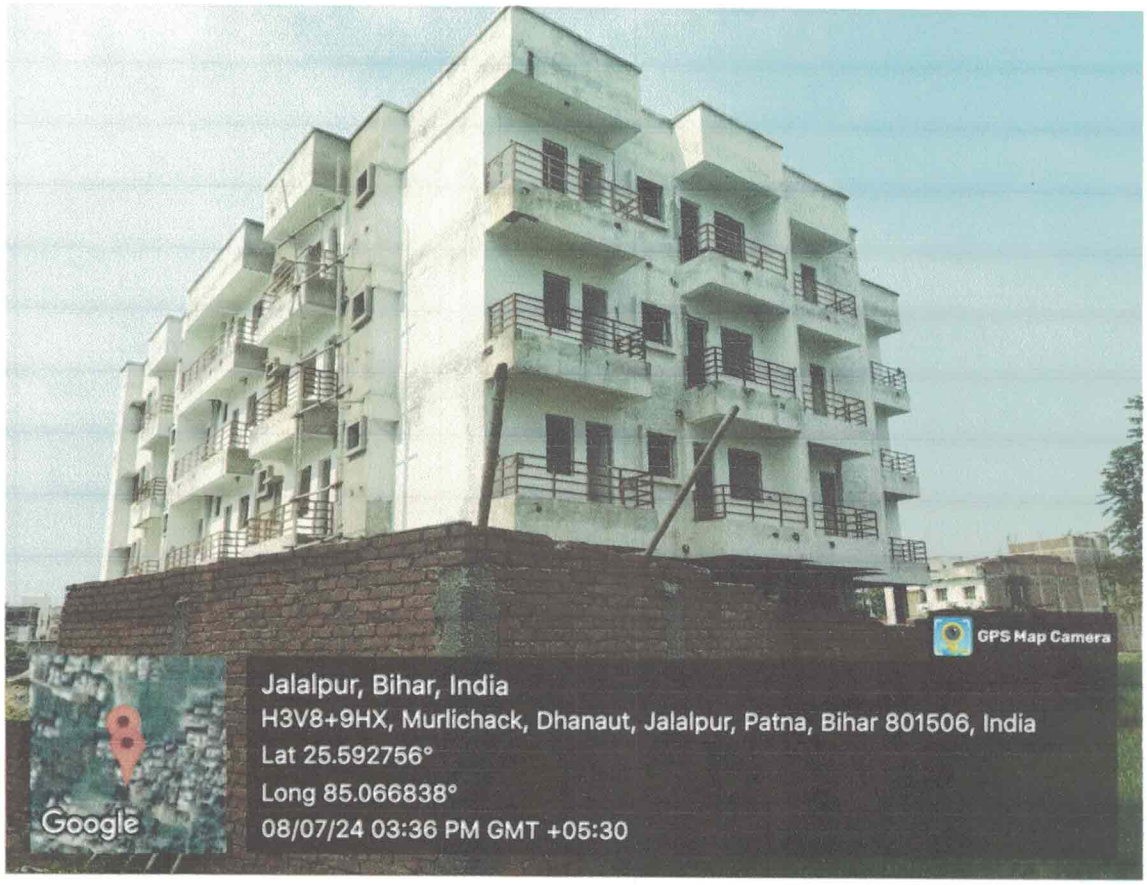

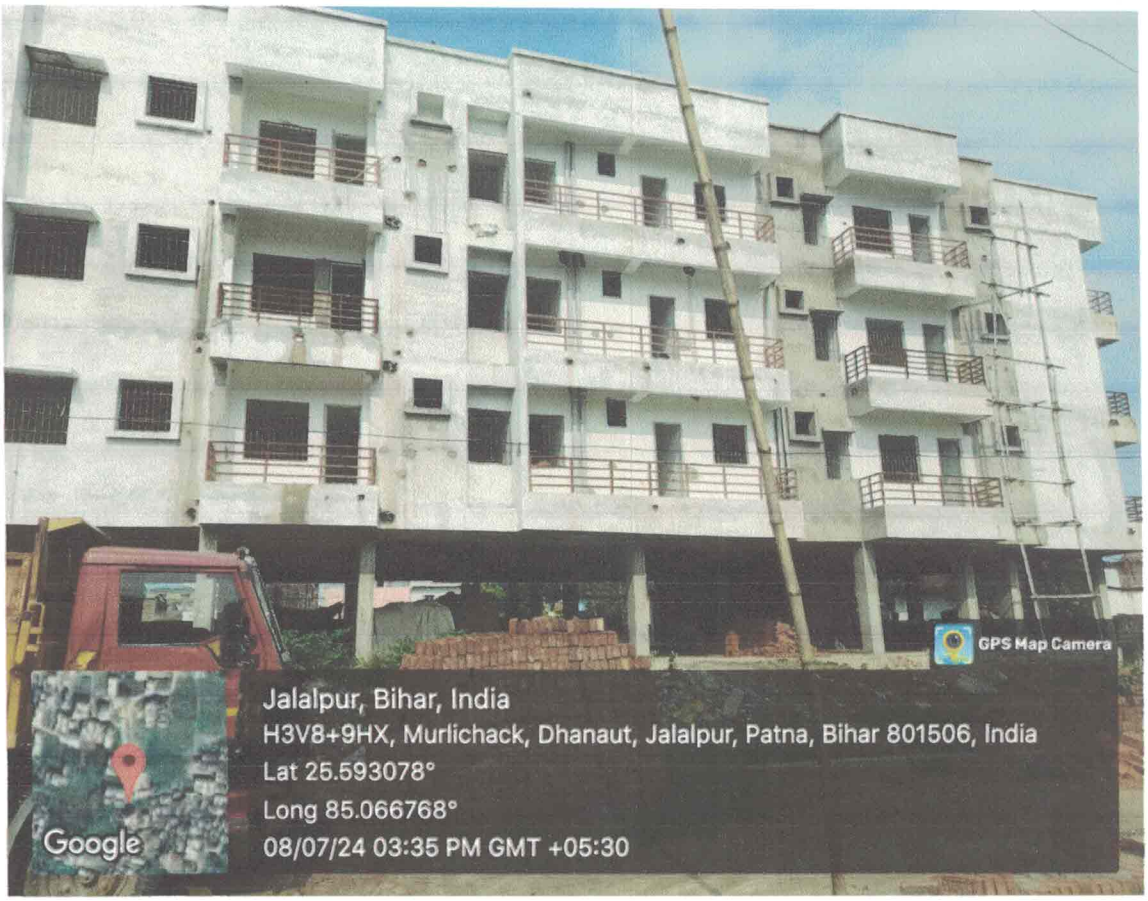

Surendra Construction LLP

Designated Partner

X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	2017102000003827
2.	Estimated Cost of the Project including land cost at the start of the Project	3,48,50,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	1,60,00,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	NO
5.	Amount received during the Quarter	27,25,000=00
6.	Actual Cost Incurred during the Quarter	32,33,432=00
7.	Net amount at end of the Quarter	
8.	Total expenditure on Project **till date**	2,57,94,059=00
9.	Cumulative fund collected till the end of Quarter in question	
10.	Cumulative expenditure done till the end of Quarter in question	

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO

Surondha Construction LLP

Designated Partner

B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	02
3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Surendra Construction LLP

Designated Partner

Signature of Promoter

Name:

Date:
