FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024 (year)

I. PARTICULARS OF PROMOTERS

Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	LLPIN AAO-1133	Name of Firm	SURONDHA CONSTRUCTION LLP
Firm Address :	C/O-DHARAMJEET KUMAR, KRISHNA CHAK, GOLA ROAD, DIGHA, PATNA-801503		
Total Experience of promoter in Real Estate sector	0 Years		
Total Experience in Real Estate after Implementation of RERA	03 Years		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT

Project Registration Number	BRERAP92120-1/196/R-1359/2022	Name of Project/Phase of Registered Project	J.D MANSION
Name of Promoter	SURONDHA CONSTRUCTION LLP	Project Address	MAHUABAGH, MAUZA-DHANAUT, BEHIND JHANDA MANDIR, MAHUABAGH, PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	15/02/2026		
Starting date of Project or Phase of the Project	07/04/2022		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	07/12/2024		

Surondha Construction LLP
Ravi Kant Kumar.
Designated Partner

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - 09	Total Number of Apartments in Landowner's share - 10
	1. 1 BHK	1	410.00	19	1. Booked / Allotted -06 2. Sold-NIL	3. Booked/ Allotted - NIL Sold -NIL
	2. 2 BHK, -	9	5349.00			
	3. 3 BHK	9	7044.00			
	4. Shop				Percentage of booking 66%	Percentage of booking 0%
	5. Bungalow					
	6. Plot etc.					

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
	19	1. Booked/Allotted -	06
		2. Sold -	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	N/A			
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	AAI		05-11-2018	
5.	Other Approval(s), if any, required for the Project.	N/A			

Surendra Construction LLP

Ravikant Kumar.

Designated Partner

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. P/DHANAUT-PRN-G+3/317/2021

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	N/A	
2.	Basements (if any)	N/A	
3.	Podiums (if any)	N/A	
4.	Plinth	100%	
5.	Stilt Floor	90%	31-12-2025
6.	Slabs of Super Structure	Four (4) 100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100% 100% 100% 20%	31-12-2025
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	70% 60%	31-12-2025 31-12-2025
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100% 90% 80%	31-12-2025 31-12-2025
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	70% 90% 80% 80%	31-12-2025 31-12-2025 31-12-2025 31-12-2025

Surondha Construction LLP
Kavi Kant Kumar.
Designated Partner

11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	25% 60% N/A 60% 20% 20%	31-12-2025 31-12-2025 31-12-2025 31-12-2025 31-12-2025

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	50%	30-12-2025
2.	Water Supply	YES	60%	31-12-2025
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	31-12-2025
4.	Storm Water Drains	YES	50%	31-12-2025
5.	Landscaping & Tree Planting	YES	0%	31-12-2025
6.	Street Lighting	YES	0%	31-12-2025
7.	Community Buildings	NO		

Surondha Construction LLP
Ravi Kant Kumar.
Designated Partner

8.	Treatment and Disposal of Sewage and Sullage Water	NO		
9.	Solid Waste Management & Disposal	YES	0%	31-01-2026
10.	Water Conservation / Rain Water Harvesting	YES	0%	31-01-2026
11.	Energy Management	YES	10%	31-01-2026
12.	Fire Protection and Fire Safety Requirements			
13.	Closed Parking	YES	20%	31-12-2025
14.	Open Parking	NO		
15.	Electrical Meter Room, Sub-Station, Receiving Station	NO		
16.	Others (Option to Add More)			


VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			

Surondha Construction LLP
Ravi Kant Kumar.
Designated Partner

8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX.	GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT		
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	Attach

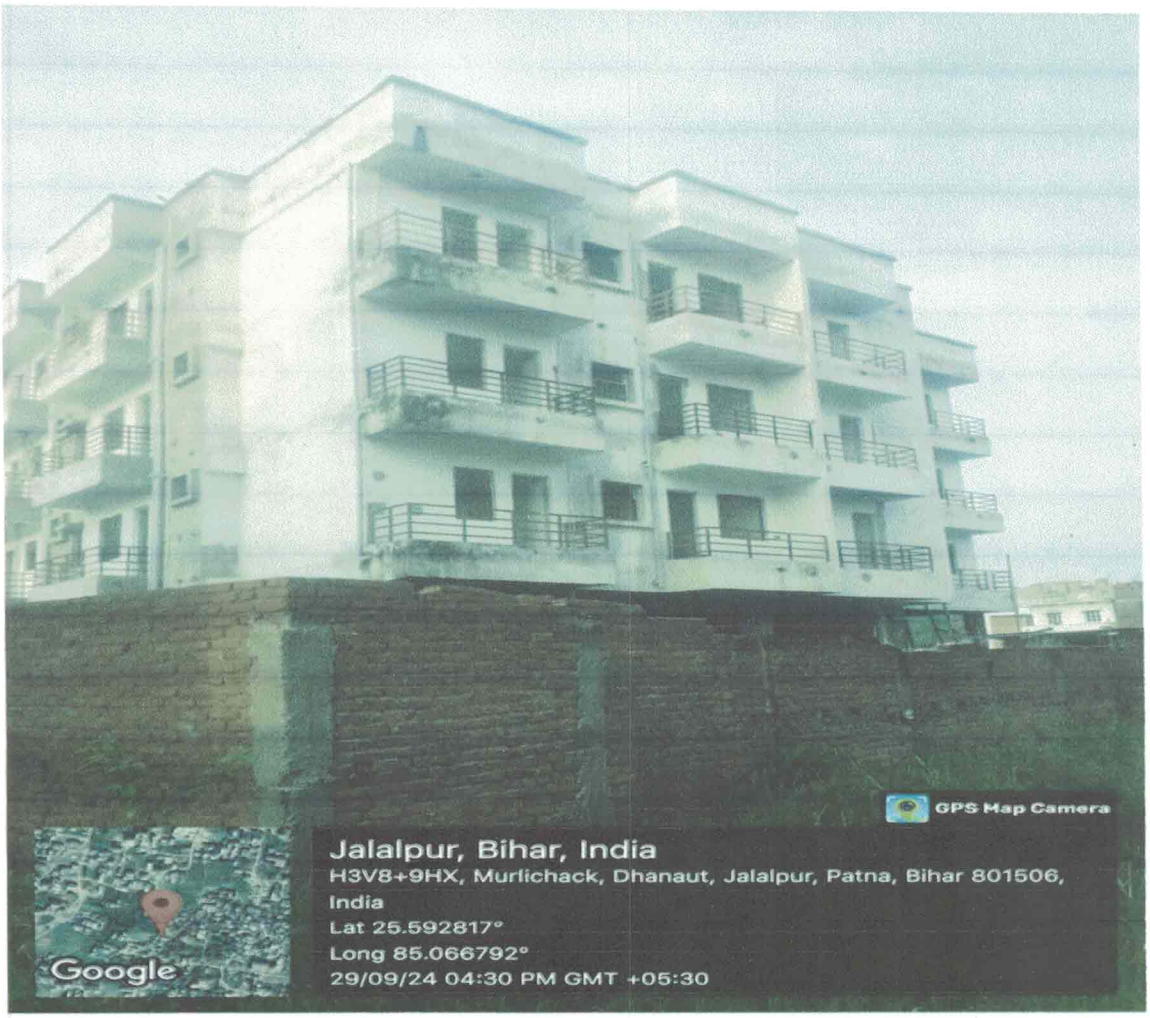

Surendha Construction LLP
Ravi Kant Kumar.
Designated Partner





Surondha Construction LLP

Ravi Kant Kumar.

Designated Partner



X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	2017102000003827
2.	Estimated Cost of the Project including land cost at the start of the Project	3,48,50,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	1,60,00,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project.	NO
5.	Amount received during the Quarter	43,26,000=00
6.	Actual Cost Incurred during the Quarter	42,50,000=00
7.	Net amount at end of the Quarter	76,000=00
8.	Total expenditure on Project **till date**	3,00,44,059=00
9.	Cumulative fund collected till the end of Quarter in question	1,79,32,000=00
10.	Cumulative expenditure done till the end of Quarter in question	3,00,44,059=00

Surondha Construction LLP
Ravi Kant Kumar.
Designated Partner

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART
Weather the project in progress is as per time schedule or lagging behind?

XIV UNITS ALLOCATION DETAILS		
Total Number of sanctioned apartments 1 BHK - 1 2 BHK, - 9 3 BHK 9 4 BHK - Shop- Bungalow - Plot etc	Details of allotment made so far with Flat number/ Bungalow - Plot etc Flat NO. 101 — 2 BHK 201 — 2 BHK 105 — 3 BHK 205 — 3 BHK 302 — 3 BHK 305 — 3 BHK	Cancellation of flat allotment, If any with Flat number/ Bungalow – Plot etc N/A

XV. BROCHURE /Prospectus

Surondha Construction LLP
Ravi Kant Kumar.
Designated Partner

XVI Grievance Redressal Officer

Name : DHARAMJEET KUMAR

Contact No :7488939664

Email id : surondhaconstruction@gmail.com

Address : C/O-DHARAMJEET KUMAR, KRISHNA CHAK, GOLA ROAD, DIGHA, PATNA

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Surondha Construction LLP

Ravi Kant Kumar.

Designated Partner

Signature of Promoter

Name: Ravi Kant Kumar.

Date:
