FORM-7

[REGULATION-9]

Quarterly Progress Report for quarter ending Jan-Mar of 2023 (Year)

I. PARTICULARS OF PROJECT	
Project Registration Number	BRERAP0005738-2/1166/R-974/2020
Name of Project/Phase of Registered Project	VAISHNAVI ENCLAVE
Name of Promoter	MAITREYEE MAHANIRMAN LLP.
Project Address	MAUZA RUSTAMPUR, SHAHPUR OR SIKANDERPUR, THANA DANAPUR, THANA NO. 17, TAUZI 5855, KHATA NO. 57,PLOT No.- 91, DANAPUR, DIST.- PATNA
Name of Co-promoter	NA
Project Registration is valid up to	20/01/2025
Starting date of Project or Phase of the Project	20/01/2020
Type of Project or Phase of the Project	Residential/Group Housing
Period of validity of map by the Competent Authority	Three Years from the date of passing of MAP

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building/Block Number	Apartment Type	Carpet Area (In Sqft)	Total Number of sanctioned apartments	Total Number of Apartment
Vaishnavi Enclave	3 BHK	1,006.00	8	1. Booked– 02 2. Cancelled–00
Vaishnavi Enclave	3 BHK	1,030.00	8	
Vaishnavi Enclave	2 BHK	906.00	2	

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of SanctionedGarages	Total Number of Garages:	
Vaishnavi Enclave	No Garages available	1. Booked/Allotted -	
		2. Sold -	

For Maitreyee Mahanirman LLP

Designated Partner

IV. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

V. Construction Progress of the Project

1. Plan Case Number- 66/19-20 (Vaishnavi Enclave) (To be added for each Building / Wing)

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	100%
2.	Basements (if any)	90%
3.	Podiums (if any)	NA
4.	Plinth	100%
5.	Stilt Floor	NA
6.	Slabs of Super Structure	70%
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	5%
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	20%
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%

For Maitreyee Mahanirman LLP

Designated Partner

11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as my be required to complete project as per specifications in Agreement of Sale. Any other activities.	11%

VI.	(Amenities and Common Area and External Infrastructure Development Works)			
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	No		
2.	Water Supply	Yes	50%	Pump Installed
3.	Sewerage (Chamber, Line, Septic Tank, STP)	Yes	0%	
4.	Storm Water Drains	No		
5.	Landscaping & Tree Planting	No		
6.	Street Lighting	No		
7.	Community Buildings	No		
8.	Treatment and Disposal of Sewage and Sullage Water	No		
9.	Solid Waste Management & Disposal	No		
10.	Water Conservation / RainWater Harvesting	No		
11.	Energy Management	No		
12.	Fire Protection and FireSafety Requirements	No		
13.	Closed Parking	Yes	70%	
14.	Open Parking	No		

For Maitreyee Mahanirman LLP

Designated Partner

15.	Electrical Meter Room, Sub-Station, Receiving Station	No		
16.	Others (Option to AddMore)	No		

VII. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT		
(A)	**S. No.**	**Particulars**
	1.	**Front Elevation.**- Attached Below
	2.	**Rear Elevation.**- Attached Below
	3.	**Side Elevation.**- Attached Below
(B)		**Photograph of each floor**

VIII. Financial Progress of the Project

S.No.	Particulars	Amount (in Rs.)
1	Project Account No.	19230200003509
2	Estimated Cost of the Project including land cost atthe start of the Quarter (In Lakh)	361.27/-
3	Amount received during the Quarter	0.00/-
4	Actual Cost Incurred during the Quarter	10,27,233.32/-
5	Net amount at end of the Quarter	0.00/-
6	Total expenditure on Project **till date**	1,47,36,102.51/-
7	Cumulative fund collected till the end of Quarter in question	18,58,501.00/-
8	Cumulative expenditure done till the end of Quarter in question	1,47,36,102.51/-


IX. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

For Maitreyee Mahanirman LLP

Designated Partner

X. MISCELLANEOUS		
A	List of Legal Cases (if any)	
1.	Case No.	NA
2.	Name of Parties	NA
B	Sale/Agreement for Saleduring the Quarter	
1.	Sale Deed	
2.	Agreement for Sale	

XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART
Weather the project in progress is as per time schedule or lagging behind?

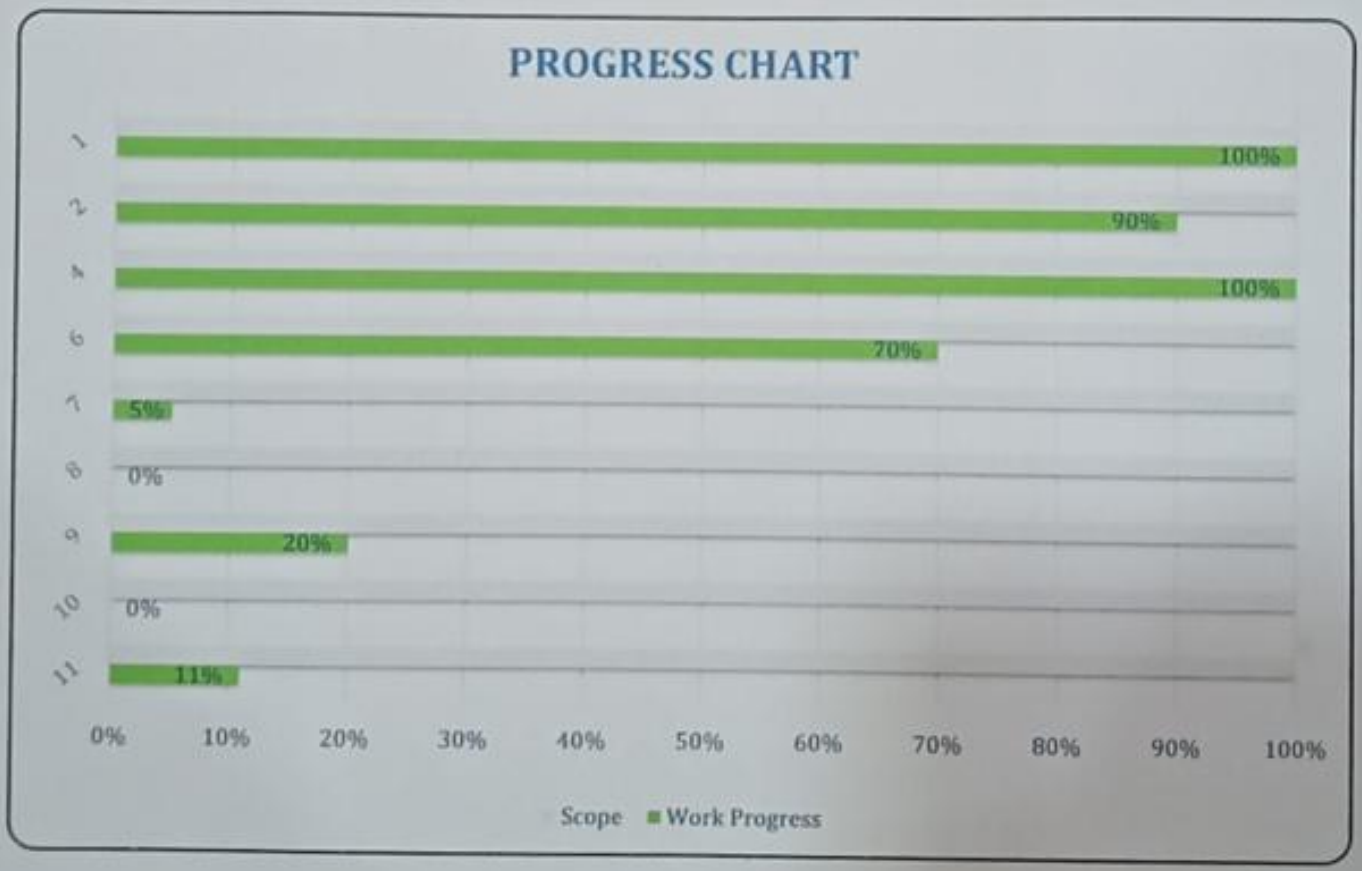

For Maitreyee Mahanirman LLP

Designated Partner

Project Site Photographs



For Maitreyee Mahanirman LLP

Designated Partner



Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Signature of Promoter
Maitreyee Mahanirman LLP

For Maitreyee Mahanirman LLP

Designated Partner

Partner
Date :
