PANORAMA GROUP
A unit of Simanchal Infratech Pvt. Ltd.

SIMANCHAL INFRATECH PVT.LTD.

Corporate Office : 3rd Floor, Zila School Road, Bhatta Bazar
Purnea (Bihar) 854 301

Ref.No.: SIPL/RRP/QPR-IV/24-25 Date..11-04-25

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending 31st March of 2025

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN : U45200BR2016PTC032419 GSTIN: 10AAXCS5343L1ZX	Name of Firm SIMANCHAL INFRATECH PVT. LTD.	
Firm Address:	Corp. Office at: 3rd Floor jnj Panorama Square, Zila School Road, Purnia, Bihar-854301.		
Total Experience of promoter in Real Estate sector	8 Years.		
Total Experience in Real Estate after Implementation of RERA	8 Years.		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential-cum Commercial 4. Plotted project	NONE	
No. of Project done After Implementation of RERA	1. Residential - 16 2. Commercial 3. Residential- cum Commercial - 3 4. Plotted project		

II. PARTICULARSOFPROJECT			
Project Registration Number	**BRERAP00270-4/1034/R-849/2019**	Name of Project/Phase of Registered Project	**RR PLAZA**
Name of Promoter	**SIMANCHAL INFRATECH PVT. LTD.**	Project Address	NEAR RANGBHUMI MAIDAN, PURNIA, BIHAR-854301.
Name of Co-promoter	NA		
Project Registration is valid upto	25/07/2022		
Starting date of Project or Phase of the Project	25/07/2019		
Type of Project or Phase of the Project	1. Residential 2. Commercial 3. Residential-cum-Commercial 4. Plotted project	RESIDENTIAL CUM COMMERCIAL APARTMENT B+G+7	
Period of validity of map by the Competent Authority		5 Yrs.	

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share -24 FLAT & 26 Shop	Total Number of Apartments in Landowner's share- 18 FLAT 16 units 08 Shop
BLOCK A (Residential)	1. 1 BHK 2. 2 BHK, - 3. 3 BHK	FLAT FLAT FLAT	3111.15 12758.70 9197.7	42 FLATS	1. Booked / Allotted - Flat -6 Shop-5 1. Sold- 0	Booked/ Allotted- 0 Sold - 0
BLOCK B (Commercial	4. Shop 5. Bungalow - 1 BHK etc.		6504.58 2182.94	34 SHOP 16 UNITS	Percentage of booking 25% in Residential 19% in commercial	Percentage of booking NIL

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name Not created yet will constitute as soon as possible.

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	Contact number	Email id(If any)

IV. DISCLOSURE OF SOLD/BOOKED INVENTORY OF GARAGES

Building/Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted -	
		2. Sold -	

V.	DETAILS OF BUILDING APPROVALS				
(If already filed along with Registration Application, then there is no need of further filing)					
S. No.	Name of the Approval/ N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	Na			
2.	Fire N.O.C.	Na			
3.	Water Supply Permission	Na			
4.	NOC from Airport Authority of India	Na			
5.	Other Approval(s), if any, required for the Project.				

VI. CONSTRUCTION PROGRESS OF THE PROJECT			
1. Plan Case No. **322/2017-18**			
S. No. (1)	Tasks/Activity(2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	100%	
3.	Podiums (if any)	NA	NA
4.	Plinth	100%	
5.	Stilt Floor	NA	NA
6.	Slabs of Super Structure	Block- B-100%, Block-A-40%	31/03/25 30/06/26
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	Block- B-100%, Block-A-10%	31/01/26
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	Block- B-75%, Block-A-Yet to Start	T2 31/03/26 T1 30/04/26
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks	Block- B-100%, Block-A-0%	YET TO START
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	Block- B-100%, Block-A-WIP	YET TO START
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities.	Block- B- 60 % Block-A-	

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed(Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	40%	
2.	Water Supply	YES	YET TO START	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES, LOCAL AUTHORITY	YET TO START	
4.	Storm Water Drains	NA	NA	
5.	Landscaping & Tree Planting	YES		
6.	Street Lighting	YES		
7.	Community Buildings	NONE	NA	
8.	Treatment and Disposal of Sewage and Sullage Water	LOCAL AUTHORITY	NA	
9.	Solid Waste Management & Disposal	LOCAL AUTHORITY	NA	
10.	Water Conservation / Rain Water Harvesting	NA	NA	
11.	Energy Management	NA	NA	
12.	Fire Protection and Fire Safety Requirements	YES	YET TO START	
13.	Closed Parking	YES	70%	
14.	Open Parking	YES	70%	
15	Electrical Meter Room, Sub-Station, Receiving Station	YES	YET TO START	
16.	Others (Option to AddMore)	NA	YET TO START	

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT				
		PROPOSED YES/NO.	PERCENTAGEOF ACTUAL WORK DONE (As On date of certificate)	Expected Completion date in (dd /mm /yy) Format
1.	Internal Roads and foot paths	NA		
2.	Water Supply	NA		
3.	Sewerage Chambers Septic Tank	NA		
4	Drains	NA		
5.	Parks, Land-Scaping and Tree Planting	NA		
6.	Street Lighting	NA		
7.	Disposal of sewage & sullage water	NA		
8.	Water conservation/Rain Water Harvesting	NA		
9.	Energy Management	NA		

IX. GEOTAGGED AND DATE PHOTOGRAPH OF (EACH BLOCK) OF THE PROJECT			
(A)	Sr. No.		
	1.	Front Elevation	ATTACHED
	2.	Rear Elevation	ATTACHED
	3.	Side Elevation	ATTACHED
(B)		Photograph of each floor	ATTACHED

X. FINANCIALPROGRESSOFTHEPROJECT		
S.No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	55150200000426
2.	Estimated Cost of the Project including land cost at the start of the Project	944.84 LAKH
3.	Estimated Development Cost of the Project at the start of the Project. (Excluding Land Cost)	582.34 lakh
4.	Any Variation in Development Cost which is declared at the start of the Project.	NIL
5.	Amount received during the Quarter	NIL
6.	Actual Cost Incurred during the Quarter	10,000/-
7.	Net amount at end of the Quarter	32,240.10/-
8.	Total expenditure on Project **till date**	8,60,28,149/-
9.	Cumulative fund collected till the end of Quarter in question	
10.	Cumulative expenditure done till the end of Quarter in question	

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED/DETAILS OF LOAN TAKEN BY PROMOTERS AGAINST THE PROJECT, If any
NO, MORTGAGE OR CHARGE CREATED BY PROMOTER AGAINST PROJECT

XII.MISCELLANEOUS		
A	List of Legal Cases (if any)–On Project/ Promoter	
1.	Case No.	Pending at Municipal Corporation (Lower Court)
2.	Name of Parties	Municipal Commissioner Purnia (NNP)
3.	No of Execution Cases against this project Case No. Name of Parties	NIL
4.	No of Suo-Moto cases against this project Case No. Name of Parties	NIL
5.	No of Certificate cases/PDR cases against this project Case No. Name of Parties	NIL
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	0
2.	Agreement for Sale	0
3.	No. of possessions given to allottees	0

XIII.PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

YES, Project was in progress as per schedule. Block B of Project is about to complete whereas Block A is delayed by 15 months as work has been stopped by NNP Purnia and petition is pending in Lower court. We are following direction of court in this matter.

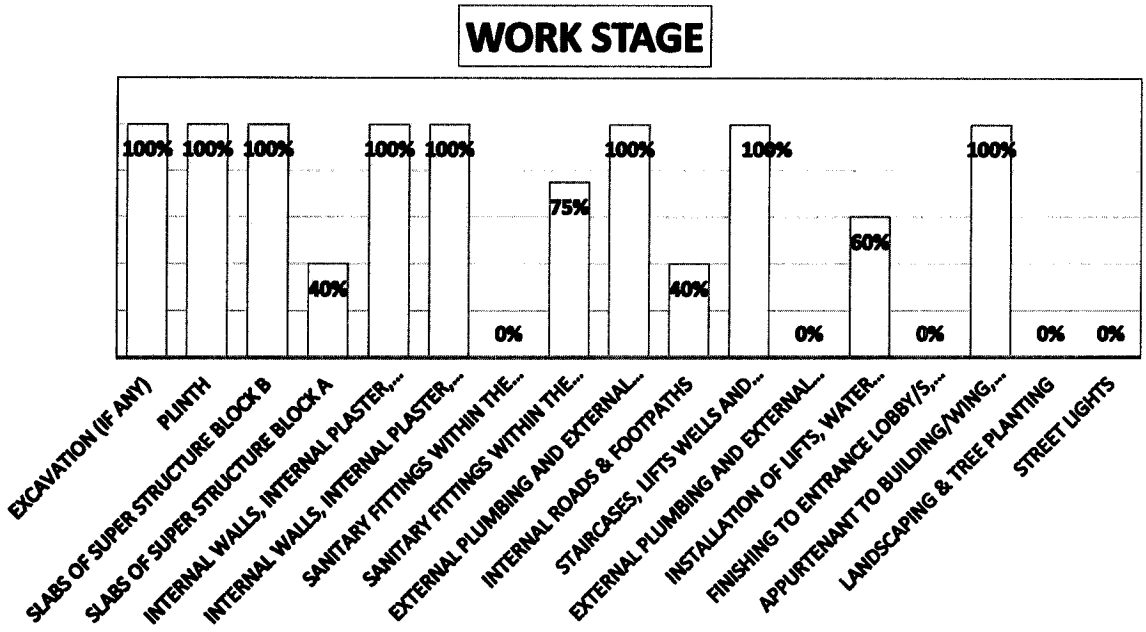
WORK STAGE
100%
100%
100%
40%
100%
100%
0%
75%
100%
40%
100%
0%
60%
0%
100%
0%
0%
EXCAVATION (IF ANY)
PLINTH
SLABS OF SUPER STRUCTURE BLOCK B
SLABS OF SUPER STRUCTURE BLOCK A
INTERNAL WALLS, INTERNAL PLASTER,...
INTERNAL WALLS, INTERNAL PLASTER,...
SANITARY FITTINGS WITHIN THE...
SANITARY FITTINGS WITHIN THE...
EXTERNAL PLUMBING AND EXTERNAL...
INTERNAL ROADS & FOOTPATHS
STAIRCASES, LIFTS WELLS AND...
EXTERNAL PLUMBING AND EXTERNAL...
INSTALLATION OF LIFTS, WATER...
FINISHING TO ENTRANCE LOBBY/S,...
APPURTENANT TO BUILDING/WING,...
LANDSCAPING & TREE PLANTING
STREET LIGHTS

XIV UNITS ALLOCATION DETAILS		
Total Number of sanctioned Apartments 42 FLATS 34 SHOP 16 UNITS	Details of allotment made so far With Flat number/Bungalow-Plot etc	Cancellation of Flat allotment, If any with Flat number/Bungalow-Plot etc
XV.BROCHURE/Prospectus		
XVI Grievance Redressal Officer **Name:** **Pragya Singh** **Contact No:** **7549000065** **Email id:** jnjpanoramasquare@gmail.com **Address:** 3rd floor, jnj panorama square, Zila School Road, Purnia, BR-854301		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the fore going and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Signature of Promoter

Simanchal Infratech Pvt. Ltd.

Director

Name: SANJEEV MISHRA

Date: 11.04.2025

R K RANJAN & ASSOCIATES
Chartered Accountants.
Rajeshwari Niwas, Beside OBC Bank,
Bhatta Bazar, Purnea,
Purnia--854301
Phone: +91-9155982424, 7488447789
e mail:carkranjan@yahoo.in

FORM-3
CHARTERED ACCOUNTANT'S CERTIFICATE

Date: 11.04.2025

BRERA Registration Number: BRERAP00270-4/1034/R-849/2019
Project Name : RR PLAZA
Promoter Name: SIMANCHAL INFRATECH PRIVATE LIMITED
Cost of Real Estate Project: Rs.944.84Lakh

This Certificate is issued in accordance with the provisions of the Real Estate (Regulation and Development) Act, 2016 read with the Karnataka Real Estate (Regulation and Development Rules, 2017.

The Promoter in compliance with section 4(2)(l)(D), of the Real Estate (Regulation and Development) Act, 2016 has deposited 70% of the amounts received from the allottees of this project in the following account:

Name of the Account Holder: SIMANCHAL INFRATECH PRIVATE LIMITED RR PLAZA
Designated Account Number: 55150200000426
Bank Name: BOB
IFSC Code: BARB0BHATTA
Branch Name: PURNIA

R. K. RANJAN & ASSOCIATES
M. No. 304639
Purnia
CHARTERED ACCOUNTANT

I have verified the sanctioned drawing and Architect Certificate .

Sl. No	Particulars	Estimated Amt in Rs.	Incurred Amt in Rs.
1	i. Land Cost: a. The cost incurred by the promoter for the acquisition of ownership and title of the land parcels for the project as an outright purchase lease etc. b. Amount paid for Acquisition/ purchase of TDR (if any) c. Amount paid to the Competent Authority for project approval, No Objection Certificates, stamp duty, transfer charges, Registration charges, conversion charges, change, taxes, statutory payments to state and Central Government.	3,61,66,000/-	
	Sub – Total Land Cost	3,61,66,000/-	
	ii. Development Cost/ Cost of Construction: a. (i) Estimated Cost of Construction as certified by Engineer (ii) Actual Cost of construction incurred as per the books of accounts as verified by the CA **Note: (for adding to total cost of construction incurred, minimum of (i) or (ii) is to be considered)** (iii) On-site expenditure for development of entire project excluding cost of construction as per (i) or (ii) above, i.e. salaries, consultants fees, site overheads, development works, cost of services (including water, electricity, sewerage, drainage, layout roads etc.) cost of machineries and equipment including its hire and maintenance costs, consumables etc. all costs directly incurred to complete the construction of the entire phase of the project registered. b. Payment of Taxes, cess, fees, charges, premiums,	5,82,34,000/-	NIL



	interest etc., to any statutory Authority. c. Principal sum and interest payable to financial institutions, scheduled banks, non- banking financial institution (NBFC) or money lenders on construction funding or money borrowed for construction;		
Sub – Total Development Cost		944.84 LAKH	
	2. Total Estimated Cost of the Real Estate Project [1(i) +1(ii)] of estimated Column. 3. Total Cost Incurred of the Real Estate Project [1(i) + 1(ii)] of Incurred Column. 4. Percentage of completion of construction work (as per Project Architect's Certificate) 5. Proportion of the Cost incurred on Land Cost to the Total Estimated Cost. 6. Proportion of the Cost incurred on Construction Cost /to the Total Estimated Cost. 7. Amount which can be withdrawn from Designated Account (Total Estimated Cost as * Proportionof cost incurred as per (2 & 5)	Rs 944.84 Lakh .....% 72% .....%	
	8. Less: Amount withdrawn till date of this certificate as per the Books of Accounts and Bank Statement. 9. Net Amount which can be withdrawn from the Designated Bank Account under this certificate.	Rs Nil NIL	
2	**Borrowings / Mortgage Details (If Applicable)**		
	A. Borrowing Details **1. Name of the Lender:** **2. Amount Disbursed:** **3. Amount pending for disbursement from Lender:** **4. Amount to be repaid to lender:** **B. Mortgage Details** **1. Mortgaged to (Name of the Entity/ Institution) :** **2. Amount Disbursed:** **3. Amount pending for disbursement:** **4. Amount to be repaid to lender:**	 Rs ...nil..... Rs .....nil..... Rs .....nil..... Rs ...nil..... Rs .....nil..... Rs .....nil..... Rs .....nil.....	

R. K. RANJAN & ASSOCIATES
M. No. 304635
Purnia
CHARTERED ACCOUNTANTS

This certificate is being issued for the project **RR PLAZA** with RERA Registration No. BRERAP00270-4/1034/R-849/2019 in compliance of the provisions of section 4(2) (l) (D) of the Act and based on the records and documents produced before me and explanations provided to me by the Management of the Company.

*** Remark on Project :** Work has been stopped in Project and ***status quo*** is maintained as per direction of court. Builder has filed his petition and same is pending in lower court.

Yours Faithfully,

Signature of the Chartered Accountant



Name: CA RAJEEV KUMAR RANJAN
Membership Number: 304639

FORM No.1
[Regulation 3]

ARCHITECT'S CERTIFICATE

(To be submitted at the time of Registration of Ongoing Project and for withdrawal of Money from Designated Account)

No.....
Project : RR PLAZA

Date: 08-04-2025

To,
Simanchal Infratech Private Limited
3rd Floor , Panorama Square
Zila School Road, Purnia,BR-854301.

Subject: Certificate of Percentage of Completion of Construction Work of RR PLAZA, No. of Building(s)/ Block(s) of the ____ Phase of the Project [BRERA Registration Number BRERAP00270-4/1034/R-849/2019] situated on the Khasra No. / Plot no. 1310 , Village- Near Rangbhoomi Miadan, Tehsil - Purnea east, K.Hat Competent/ Development authority - Nagar Nigam, Purnia , District - Purnia PIN - 854301 admeasuring _____ sq.mts. area being developed by [SIMANCHAL INFRATECH PRIVATE LIMITED].

I/We Saurabh Kumar Mishra have undertaken assignment as Architect/Licensed Surveyor of certifying Percentage of Completion Work of the RR Plaza Building(s)/ Block/ Tower (s) of A & B Phase of the Project, situated on the Khasra No. / Plot no.1310 of village Near Rangbhoomi Maidan, Purnia tehsil-Purnea East, K. Hat , competent/ development authority Nagar Nigam Purnia District Purnia PIN 854301 admeasuring sq.mts. area being developed by [SIMANCHAL INFRATECH PRIVATE LIMITED]

1. Following technical professionals are appointed by owner / Promotor:-
   i. M/s/Shri/Smt Saurabh Kumar Mishra as L.S. / Architect;

Based on Site Inspection, with respect to each of the Buildings /Blocks/Towers of the aforesaid Real Estate Project : RR Plaza, I certify that as on the date of this certificate, the Percentage of Work done for each of the Buildings /Blocks/Towers of the Real Estate Project as registered vide number under BRERA is as per table A attached herewith. The percentage of the work executed with respect to each of the activity of the entire phase is detailed in the Table B attached herewith.

Yours Faithfully

Name of L.S./Architect
Saurabh Kumar Mishra
Saurabh Kumar Mishra
(License No. CA/2019/114348)
SAURABH KUMAR MISHRA
Registered Architect
UDHD- Govt. of Bihar
CoA Reg No. - CA/2019/114348

TABLE-A

CONSTRUCTION PROGRESS OF THE PROJECT			
Project : RR PLAZA			
S. No. (1)	Tasks/Activity(2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	100%	
3.	Podiums (if any)	NA	NA
4.	Plinth	100%	
5.	Stilt Floor	NA	NA
6.	Slabs of Super Structure	Block- B-100%, Block-A-40%	31/03/25 30/06/26
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	Block- B-100%, Block-A-10%	31/01/26
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	Block- B-75%, Block-A-Yet to Start	T2 31/03/26 T1 30/04/26
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks	Block- B-100%, Block-A-0%	YET TO START
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	Block- B-100%, Block-A-WIP	YET TO START
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities.	Block- B- 60 % Block-A-	

SAURABH KUMAR MISHRA
Registered Architect
UDHD- Govt. of Bihar
CoA Reg No. - CA/2019/114348

TABLE-B

AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed(Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	40%	
2.	Water Supply	YES	YET TO START	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES, LOCAL AUTHORITY	YET TO START	
4.	Storm Water Drains	NA	NA	
5.	Landscaping & Tree Planting	YES		
6.	Street Lighting	YES		
7.	Community Buildings	NONE	NA	
8.	Treatment and Disposal of Sewage and Sullage Water	LOCAL AUTHORITY	NA	
9.	Solid Waste Management & Disposal	LOCAL AUTHORITY	NA	
10.	Water Conservation / Rain Water Harvesting	NA	NA	
11.	Energy Management	NA	NA	
12.	Fire Protection and Fire Safety Requirements	YES	YET TO START	
13.	Closed Parking	YES	70%	
14.	Open Parking	YES	70%	
15	ElectricalMeterRoom,Sub-Station,ReceivingStation	YES	YET TO START	
16.	Others(OptiontoAddMore)	NA		**Remark on Project:** *Work has been stopped as per direction of Court will start after conclusion and order of court.*

SAURABH KUMAR MISHRA
Registered Architect
UDHD- Govt. of Bihar
CoA Reg No. - CA/2019/114348
