SIMANCHAL INFRATECH PVT.LTD.

(PANORAMA GROUP)

Corporate Office : 3rd Floor, Zila School Road, Bhatta Bazar
Purnea (Bihar) 854 301

Ref.No.: PC-2/PPR-1/24-25 Date: 14/07/2024

FORM-7
[REGULATION9]

Quarterly progress report for quarter ending 30th June of 2024

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN: U45200BR2016PTC032419 GSTIN: 10AAXCS5343L1ZX	Name of Firm **SIMANCHAL INFRATECH PVT. LTD.**	
Firm Address:	Corp. Office: 3RD Floor, JNJ Panorama Square, Zila School Road, Purnia, Bihar-854301.		
Total Experience of promoter in Real Estate sector	8 Years		
Total Experience in Real Estate after Implementation of RERA			
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	14 03	

II. PARTICULARS OF PROJECT			
Project Registration Number	**BRERAP00270-08/1133/R-728/2020**	Name of Project/Phaseof Registered Project	**PANORAMA CITY PHASE -II**
Name of Promoter	**SIMANCHAL INFRATECH PVT. LTD.**	Project Address	NH-31, BY PASS ROAD, GULABBAG, PURNIA, BR-854326.
Name of Co-promoter	NA		
Project Registration is valid up to	09/12/2021		
Starting date of Project or Phase of the Project	06/12/2019		
Type of Project or Phase of the Project	1. Residential 2. Commercial 3. Residential- cum-Commercial, 4. Plotted project	RESIDENTIAL TOWNSHIP	
Period of validity of map by the Competent Authority	5YRS.		

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Numberof sanctioned apartments	Total Number of Apartments in Promoter's share -	Total Number of Apartments in Landowner's share -
	2/3 BHK G+1	DUPLEX COMMUNITY HALL	11778 4096	18+1=19	18DUPLEX 1. Booked- / Allotted - 18 2. Sold- 18	NA Booked/ Allotted- 0 Sold 0
					Percentage of booking 100%	Percentage of booking NA

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	NA
	NA	1. Booked/Allotted - 2. Sold -	NA

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	NA	NA		
2.	Fire N.O.C.				
3.	Water Supply Permission	NA			
4.	NOC from Airport Authority of India	NA			
5.	Other Approval(s), if any, required for the Project.	NA			

PANORAMA GROUP
A unit of Simanchal Infratech Pvt. ltd.

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No.

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	NA	
3.	Podiums (if any)	NA	
4.	Plinth	100%	
5.	Stilt Floor	NA	
6.	Slabs of Super Structure	100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	100%	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	100%	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other	100%	

PANORAMA GROUP

	requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities.		

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	100%	
2.	Water Supply	YES	100%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES, LOCAL AUTHORITY	100%	
4.	Storm Water Drains	NA	NA	
5.	Landscaping & Tree Planting	YES	100%	
6.	Street Lighting	YES	100%	
7.	Community Buildings	YES	100%	
8.	Treatment and Disposal of Sewage and Sullage Water	LOCAL AUTHORITY	NA	
9.	Solid Waste Management & Disposal	LOCAL AUTHORITY	NA	
10.	Water Conservation / Rain Water Harvesting	NA	NA	
11.	Energy Management	NA	NA	

PANORAMA GROUP

12.	Fire Protection and Fire Safety Requirements	NA		
13.	Closed Parking	YES	100%	
14.	Open Parking	YES	100%	
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	100%	
16.	Others (Option to Add More)	NA		

VIII. EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENTAGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths	NA		
2.	Water Supply	NA		
3.	Sewerage Chambers Septic Tank	NA		
4	Drains	NA		
5.	Parks, Land Scaping and Tree Planting	NA		
6.	Street Lighting	NA		
7.	Disposal of sewage & sullage water	NA		
8.	Water conservation/Rain Water Harvesting	NA		
9.	Energy Management	NA		

PANORAMA GROUP
A Unit of Simanchal Infratech Pvt. ltd.

IX. GEO TAGGED AND DATE PHOTOGRAPH OF (EACH BLOCK) OF THE PROJECT			
(A)	Sr. No.		
	1.	Front Elevation	ATTACHED
	2.	Rear Elevation	ATTACHED
	3.	Side Elevation	ATTACHED
(B)		Photograph of each floor	ATTACHED

X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	51010101653287
2.	Estimated Cost of the Project including land cost at the start of the Project	398LAKH
3.	Estimated Development Cost of the Project at the start of the Project. (Excluding Land Cost)	233 LAKH
4.	Any Variation in Development Cost which is declared at the start of the Project.	NO
5.	Amount received during the Quarter	NIL
6.	Actual Cost Incurred during the Quarter	NIL
7.	Net amount at end of the Quarter	
8.	Total expenditure on Project **till date**	Rs.428.02 LAKH
9.	Cumulative fund collected till the end of Quarter in question	NIL
10.	Cumulative expenditure done till the end of Quarter in question	

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

PANORAMA GROUP
A unit of Sunrise Infrastructure Pvt. Ltd.

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	nil
2.	Name of Parties	na
3.	No of Execution Cases against this project Case No. Name of Parties	nil
4.	No of Suo - Moto cases against this project Case No. Name of Parties	nil
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	nil
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	0
2.	Agreement for Sale	0
3.	No. of possessions given to allottees	18

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

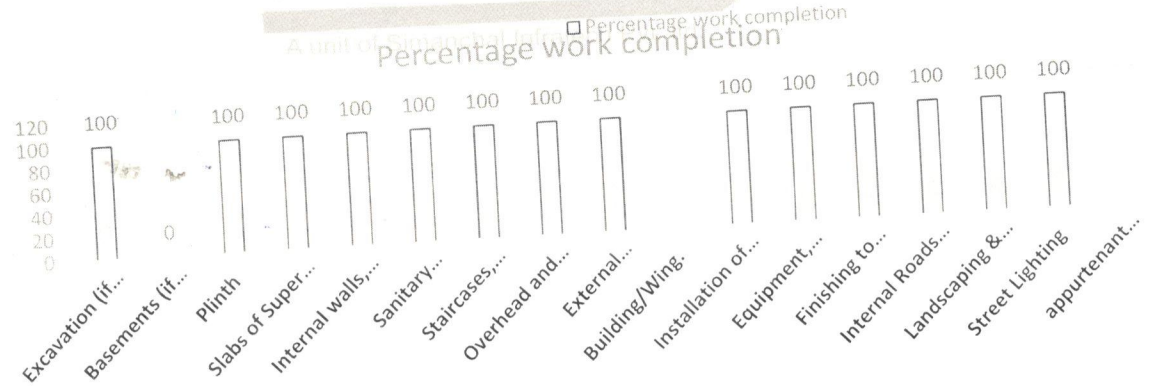

Weather the project in progress is as per time schedule or lagging behind?

Project completed

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

SIMANCHAL INFRATECH PVT. LTD.

Signature of Promoter Director

Name: Simanchal Infratech Pvt. Ltd.

Date:14/07/2024

PANORAMA GROUP
A unit of Simanchal Infratech Pvt. ltd.

कार्यालय नगर निगम, पूर्णियाँ

फारम–XII

कार्य पूर्णता की सूचना (प्रमाण–पत्र)

उप–विधि सं०–15

Case No 335/19-20

प्रेषक,

सीमांचल इंफ्राटेक प्रा० लि०
प्र० नि० - सजीव मिश्रा
पूर्णिया बिहार
854301

(आवेदक का नाम और पता बड़े अक्षरों में)

सेवा में,

श्रीमान नगर आयुक्त
नगर निगम
पूर्णिया बिहार

महोदय,

एतद द्वारा मैं प्रमाणित करता हूँ कि .....के विकास योजना क्षेत्र के अंतर्गत बिहार शहरी आयोजना तथा विकास अधिनियम, 2012 के अधीन अधिसूचित विभिन्न विकास योजना/आयोजना प्राधिकारों/या योजना स्कीम के अधीन आच्छादित सुसंगत आयोजना प्राधिकार/ग्राम पंचायत क्षेत्रों के अधीन पूर्णिया नगर निगम/नगर परिषद/नगर पंचायतों/महानगर क्षेत्रों/आयोजना क्षेत्र की वार्ड नं० 44 प्लौट नं० (सी०एस०) 1106, 1145, 1116 प्लौट नं० (एम०एस०पी०) ..... खाता नं० 550/595 होल्डिंग नं० ... 810 गाँव A. Nagar की बाबत निर्माण, पुनर्निर्माण या तात्विक परिवर्तन के लिए विकास का सर्वेक्षण मेरे द्वारा किया गया है और स्वीकृति सं० 335/19-20 दिनांक– 26/11/2019 के अधीन स्वीकृत योजनाओं के अनुसार तारीख 19/01/23 को पूरा कर लिया गया है। कार्य मेरे सर्वोतम समाधानपरक ढंग से किया गया है, कारीगरी और सभी सामग्री (प्रकार एवं ग्रेड) का उपयोग पूरी तरह से सामान्य तथा विस्तृत विनिर्देशों के अनुसार किया गया है। कार्य के दौरान संहिता के किसी उपबंध, विहित शर्तों या उसके अधीन जारी आदेशों का कार्य के दौरान उल्लंघन नहीं किया गया है। भूमि जिस निर्माण के लिए विकसित पुनर्विकसित किया गया है उसके लिए दुरूस्त है या भवन उस उपयोग के लिए दुरूस्त है जिसके लिए वह निर्मित, पुनर्निर्मित, या परिवर्तित किया गया है अथवा बनाया और परिबर्धित किया गया है।

एतदु द्वारा मैं सभी दृष्टियों से पूर्ण किए गए भवन की योजना भी अनुलग्न कर रहा हूँ।

सूचीवद्ध तकनीकि व्यक्ति/भूस्वामी का हस्ताक्षर

तकनीकि व्यक्ति/भूस्वामी का नाम

Saurabh Kumar Mishra

तकनीकी व्यक्ति का हस्ताक्षर 20/1/23

तारीख 19-01-2023

पता– पूर्णिया बिहार 854301

Saurabh Kumar Mishra
Registered Architect
Nagar Nigam, Purnea
Co A Reg. No.-CA/2019/114340

कार्यालय नगर निगम

24/03/23



