FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending June of 2024 (year)

I. PARTICULARS OF PROMOTERS

Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U45201BR2009PTC015027	Name of Firm	ELEVATION SOLUTIONS PRIVATE LIMITED
Firm Address :	304, TRIVENI NIWAS, R.K.AVENUE ROAD, RAJENDRA NAGAR, PATNA-800016		
Total Experience of promoter in Real Estate sector	15 YEARS		
Total Experience in Real Estate after Implementation of RERA	06 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	02 NIL NIL NIL	RESIDENTIAL
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	01 NIL 01 NIL	RESIDENTIAL-01 RESIDENTIAL-CUM-COMMERCIAL-01

II. PARTICULARS OF PROJECT

Project Registration Number	BRERAP00271-4/1018/R-831/2019	Name of Project/Phase of Registered Project	PASHUPATI LILA ENCLAVE
Name of Promoter	ELEVATION SOLUTIONS PRIVATE LIMITED	Project Address	NEAR GATE NO.5, ARMY CAMP, PAHARPUR, CHANDAUTI, GAYA-823004
Name of Co-promoter	N/A		
Project Registration is valid up to	25/02/2024		
Starting date of Project or Phase of the Project	14/11/2019		
Type of Project or Phase of the Project	Residential and Commercial		
Period of validity of map by the Competent Authority			

For Elevation Solutions Pvt. Ltd.

Director

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share -	Total Number of Apartments in Landowner's share -
	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.				1. Booked / Allotted - 2. Sold-	3. Booked/ Allotted- Sold -
					Percentage of booking	Percentage of booking

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted -	
		2. Sold -	

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.	FIRE OFFICE PATNA		15-04-2016	
3.	Water Supply Permission				
4.	NOC from Airport Authority of India	AIRPORT AUTHORITY OF INDIA			GAYA/EAST/B/041823/752905
5.	Other Approval(s), if any, required for the Project.				

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. _____(To beaded for each Building / Wing)

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format

For Elevation Solutions Pvt. Ltd.

Director

1.	Excavation (if any)	N/A	
2.	Basements (if any)	100%	
3.	Podiums (if any)	N/A	
4.	Plinth	100%	
5.	Stilt Floor	N/A	
6.	Slabs of Super Structure	40%	31-12-2024
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	0%	

For Elevation Solutions Pvt. Ltd.

Director

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	
2.	Water Supply	YES	100%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	
4.	Storm Water Drains	YES	0%	
5.	Landscaping & Tree Planting	YES		
6.	Street Lighting	YES		
7.	Community Buildings	NO		
8.	Treatment and Disposal of Sewage and Sullage Water	NO		
9.	Solid Waste Management & Disposal	YES		
10.	Water Conservation / Rain Water Harvesting	YES		
11.	Energy Management	YES		
12.	Fire Protection and Fire Safety Requirements	YES	0%	
13.	Closed Parking	YES	40%	
14.	Open Parking	YES	0%	
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	
16.	Others (Option to Add More)	NO		

For Elevation Solutions Pvt. Ltd.

Director

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT				
		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT			
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

For Elevation Solutions Pvt. Ltd.

Niharika Mishra

Director

X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	1914635746
2.	Estimated Cost of the Project including land cost at the start of the Project	10,09,82,040
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	
4.	Any Variation in Development Cost which is declared at the start of the Project .	
5.	Amount received during the Quarter	00=00
6.	Actual Cost Incurred during the Quarter	00=00
7.	Net amount at end of the Quarter	1,50,306=00
8.	Total expenditure on Project **till date**	
9.	Cumulative fund collected till the end of Quarter in question	30,30,144=00
10.	Cumulative expenditure done till the end of Quarter in question	28,12,348=00

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

For Elevation Solutions Pvt. Ltd.

Nihcuika Mishra

Director

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

For Elevation Solutions Pvt. Ltd.

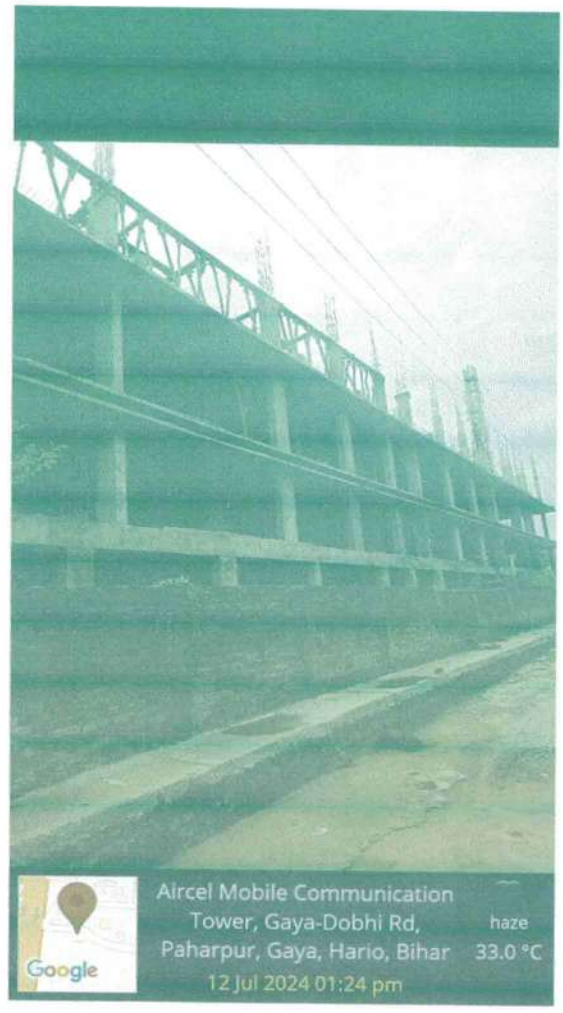
Director

Signature of Promoter

Name:

Date:


5 NO GATE OTA, MAYA PALACE, Paharpur, Gaya, Bihar 823005, India
12 Jul 2024 12:58 pm
Google


Aircel Mobile Communication Tower, Gaya-Dobhi Rd, Paharpur, Gaya, Hario, Bihar
haze
33.0 °C
12 Jul 2024 01:24 pm
Google


5 NO GATE OTA, MAYA PALACE, Paharpur, Gaya, Bihar 823005, India
haze
33.0 °C
12 Jul 2024 01:04 pm
Google
