FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	PARNERSHIP DEED NO. 3195	Name of Firm	SHREE KRISHNA HOMES
Firm Address :	Bidya Tower, Sheikhpura, Opp- Pillar Number 79, Bailey Road, Patna-14		
Total Experience of promoter in Real Estate sector	15 YEARS		
Total Experience in Real Estate after Implementation of RERA	10YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP00863-1/614/R-456/2019	Name of Project/Phase of Registered Project	KRISHNA RAM ISHWAR TOWER
Name of Promoter	SHREE KRISHNA HOMES	Project Address	URJA NAGAR, KHAGUAL ROAD, SAGUNA, NEAR ARCADE BUSINESS, OPP LAFARZ MIXING PLANT PATNA.
Name of Co-promoter	N/A		
Project Registration is valid up to	15/11/2022		
Starting date of Project or Phase of the Project	26/02/2019		
Type of Project or Phase of the Project	Residential and commercial		
Period of validity of map by the Competent Authority	3 YEARS		

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Shree Krishna Homes

Partner

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - FLAT-12, SHOP-16	Total Number of Apartments in Landowner's share - FLAT-12, SHOP-16
	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.	 24 35	 20535.54 12100.82	FLAT-24 SHOP-35	1. Booked / Allotted -03 2. Sold-NIL	3. Booked/ Allotted-NIL Sold -NIL
					Percentage of booking 10%	Percentage of booking 0%

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.			
Association of allottees name			
Details of allottees - Name, Address, Email id (if any), contact number. These details may not be available to common people			
Name	Address	contact number	Email id (If any)

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted -	03
	24	2. Sold -	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	STATE FIRE OFFICER, BIHAR, PATNA		13-09-2027	
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

VI. CONSTRUCTION PROGRESS OF THE PROJECT

Shree Krishna Homes

Partner

11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	0% 100% 0% 20% 10%	

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	
2.	Water Supply	YES	0%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	
4.	Storm Water Drains	YES	0%	
5.	Landscaping & Tree Planting	YES	0%	
6.	Street Lighting	YES	0%	
7.	Community Buildings	NO	N/A	

Shree Krishna Homes

Partner

8.	Treatment and Disposal of Sewage and Sullage Water	NO	N/A	
9.	Solid Waste Management & Disposal	YES	0%	
10.	Water Conservation / Rain Water Harvesting	YES	0%	
11.	Energy Management	YES	0%	
12.	Fire Protection and Fire Safety Requirements	YES	0%	
13.	Closed Parking	YES	0%	
14.	Open Parking			
15.	Electrical Meter Room, Sub-Station, Receiving Station			
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			

Shree Krishna Homes

Partner

8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX.	GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT		
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

X.	FINANCIAL PROGRESS OF THE PROJECT	
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	916020065836008
2.	Estimated Cost of the Project including land cost at the start of the Project	13,29,93,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	7,00,00,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	NIL
6.	Actual Cost Incurred during the Quarter	NIL
7.	Net amount at end of the Quarter	4,211=00
8.	Total expenditure on Project **till date**	
9.	Cumulative fund collected till the end of Quarter in question	
10.	Cumulative expenditure done till the end of Quarter in question	

XI.	DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

Shree Krishna Homes

Partner

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	RERA/CC-546/2022-A.O-65/2022
2.	Name of Parties	Mr. Ram Ishwar Rai
3.	No of Execution Cases against this project Case No. Name of Parties	
4.	No of Suo - Moto cases against this project Case No. Name of Parties	
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART
Weather the project in progress is as per time schedule or lagging behind?

XIV UNITS ALLOCATION DETAILS

Shree Krishna Homes

Partner

Total Number of sanctioned apartments 1 BHK- 2 BHK - 3 BHK-24 4 BHK- Shop- 35 Bungalow - Plot etc	Details of allotment made so far with Flat number/ Bungalow - Plot etc	Cancellation of flat allotment, If any with Flat number/ Bungalow – Plot etc
XV. BROCHURE /Prospectus		
XVI Grievance Redressal Officer **Name :** GYAN KAUSHIK **Contact No :** 9123409961 **Email id :** modernbathpvtltd@gmail.com **Address :** Bidya Tower, Sheikhpura, Opp- Pillar Number 79, Bailey Road, Patna-14		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

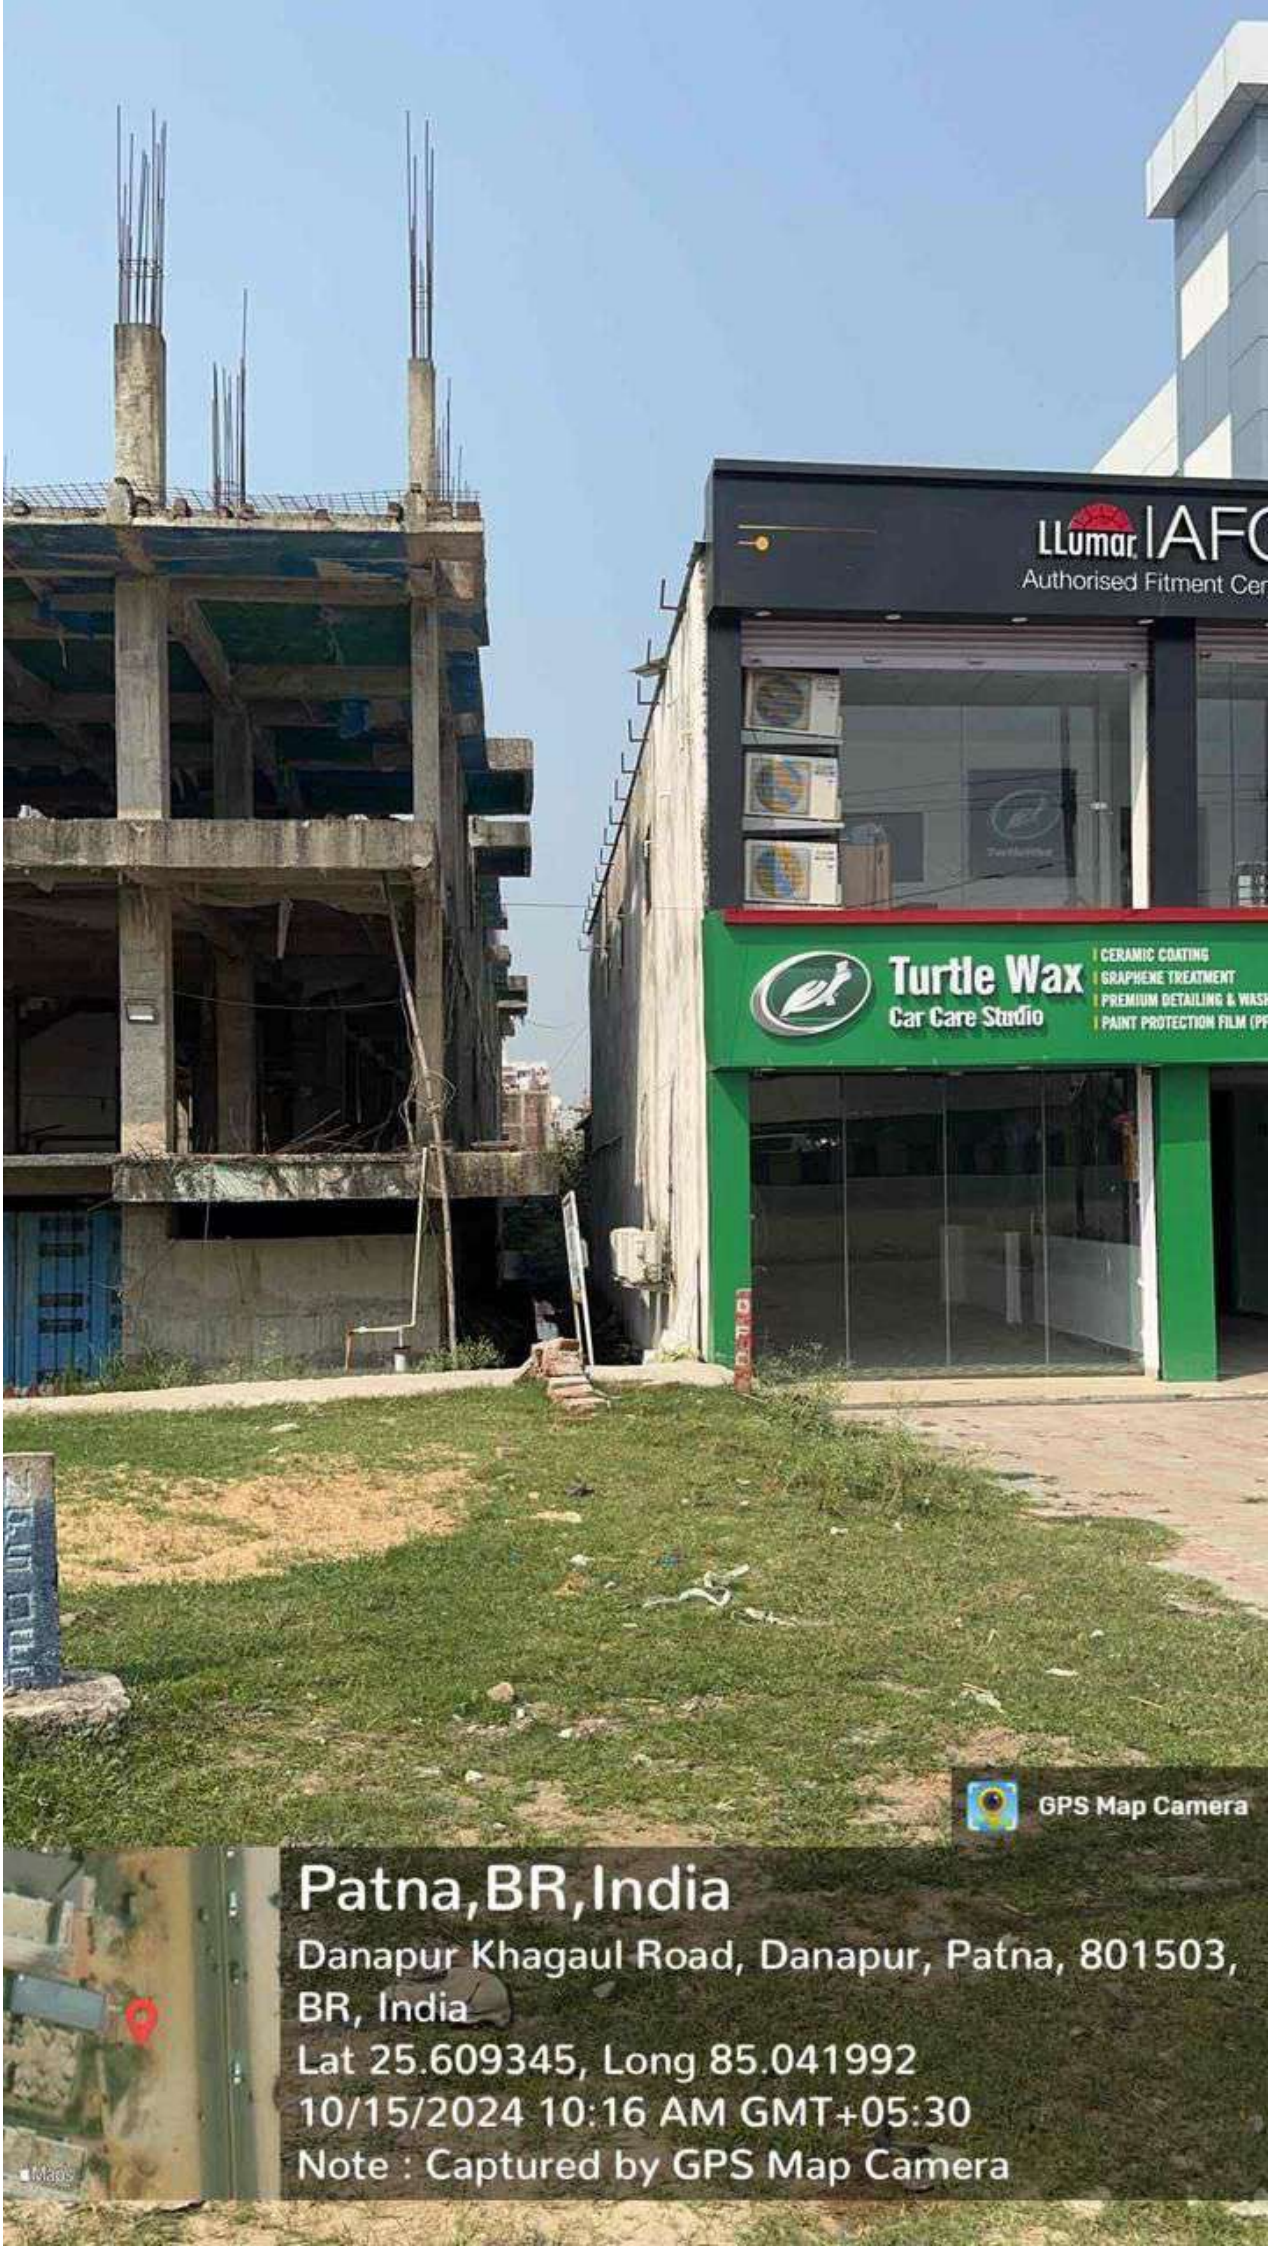
Shree Krishna Homes

Partner

Signature of Promoter

Name:

Date:


LLumar IAFC
Authorised Fitment Cen
Turtle Wax
Car Care Studio
CERAMIC COATING
GRAPHENE TREATMENT
PREMIUM DETAILING & WASH
PAINT PROTECTION FILM (PF
GPS Map Camera
Patna,BR,India
Danapur Khagaul Road, Danapur, Patna, 801503, BR, India
Lat 25.609345, Long 85.041992
10/15/2024 10:16 AM GMT+05:30
Note : Captured by GPS Map Camera


GPS Map Camera
Patna,BR,India
Danapur Khagaul Road, Danapur, Patna, 801503, BR, India
Lat 25.609272, Long 85.041999
10/15/2024 10:16 AM GMT+05:30
Note : Captured by GPS Map Camera


GPS Map Camera
Patna,BR,India
Danapur Khagaul Road, Danapur, Patna, 801503, BR, India
Lat 25.609285, Long 85.042020
10/15/2024 10:16 AM GMT+05:30
Note : Captured by GPS Map Camera
