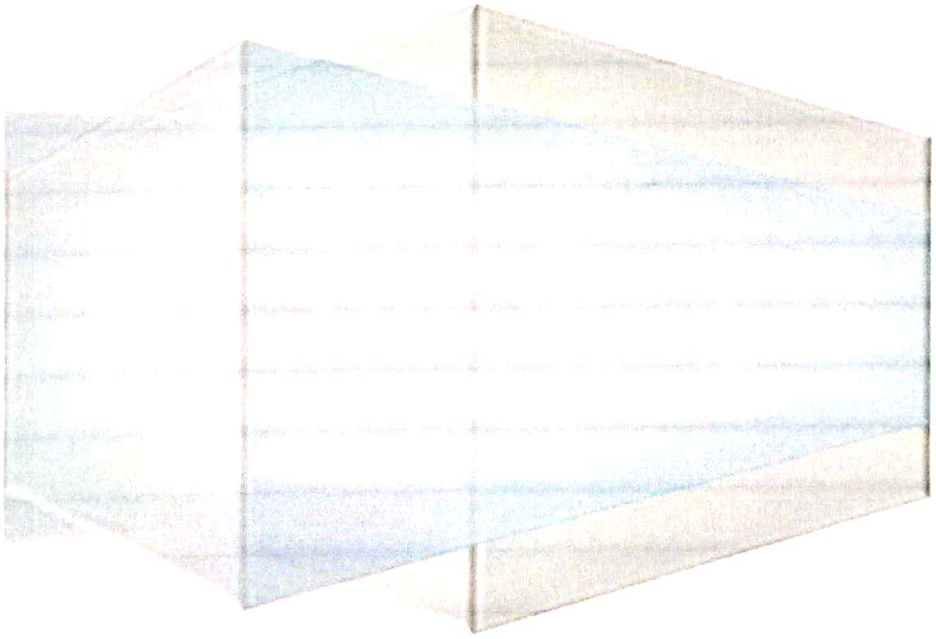
PROJECT NAME –KRISHNA SAVITRI GARDENS

PROMOTER NAME –KASCRETE BUILDMAT PRIVATE LIMITED

RERA REGISTRATION NO. BRERAP12764-001/69/R-1695/2024

QUARTERLY PROGRESS REPORT FOR RERA, BIHAR

Period – JUL TO SEP 2024



2024

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024 (year)

I. PARTICULARS OF PROMOTERS

Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U45500BR2018PTC038337	Name of Firm	KASTCREATE BUILMAT PRIVATE LIMITED
Firm Address :	2nd Floor, Commercial Building II, Maurya Complex, South Gandhi Maidan, Patna-800001		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA			
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	01	Residential
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	01	Residential

II. PARTICULARS OF PROJECT

Project Registration Number	BRERAP12764-001/69/R-1695/2024	Name of Project/Phase of Registered Project	KRISHNA SAVITRI GARDENS
Name of Promoter	KASTCREATE BUILMAT PRIVATE LIMITED	Project Address	Mohanpur, Punaichak, Patna
Name of Co-promoter	N/A		
Project Registration is valid up to	07-01-2029		
Starting date of Project or Phase of the Project	10-04-2024		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	07-01-2029		

Bharti

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - Flat -16	Total Number of Apartments in Landowner's share - Flat -15
ONE	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.	04 27		31	1. Booked / Allotted -06 2. Sold-NIL	3. Booked/ Allotted-03 Sold -NIL
					Percentage of booking 37.5%	Percentage of booking 20%

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted -	09
ONE	31	2. Sold -	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

Bharti

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. P/DHAKANPURA/PRN-1B+G+3/738/2023

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	60%	30-11-2024
3.	Podiums (if any)		
4.	Plinth		
5.	Stilt Floor		
6.	Slabs of Super Structure	0%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%	

Bharti

11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	0%	

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	
2.	Water Supply	YES	0%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	
4.	Storm Water Drains	YES	0%	
5.	Landscaping & Tree Planting	YES	0%	
6.	Street Lighting	YES	0%	
7.	Community Buildings	NO	N/A	
8.	Treatment and Disposal of Sewage and Sullage Water			

Bharti

9.	Solid Waste Management & Disposal	YES	0%	
10.	Water Conservation / Rain Water Harvesting	YES	0%	
11.	Energy Management	YES	0%	
12.	Fire Protection and Fire Safety Requirements	YES	0%	
13.	Closed Parking	YES	0%	
14.	Open Parking			
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			

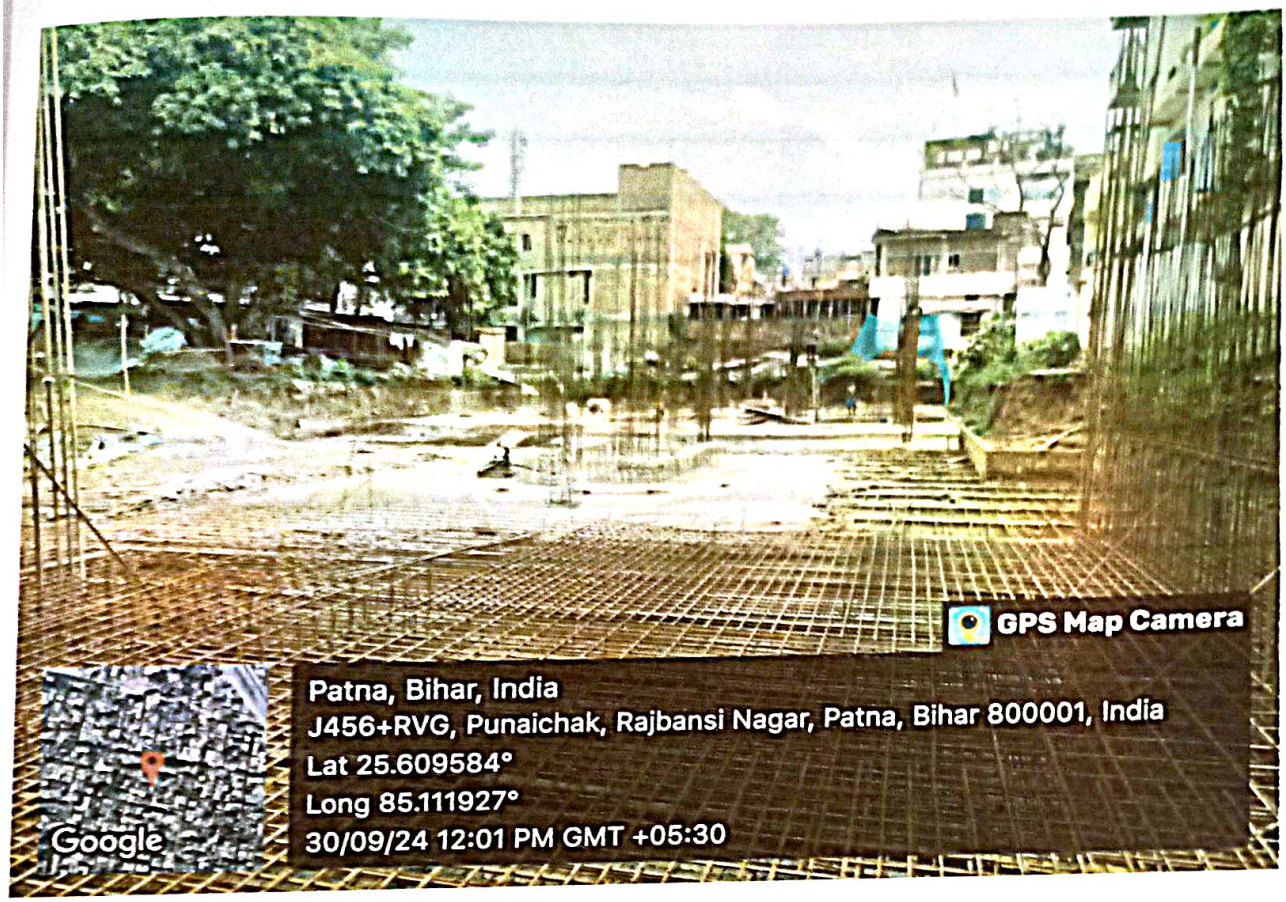
Bharti

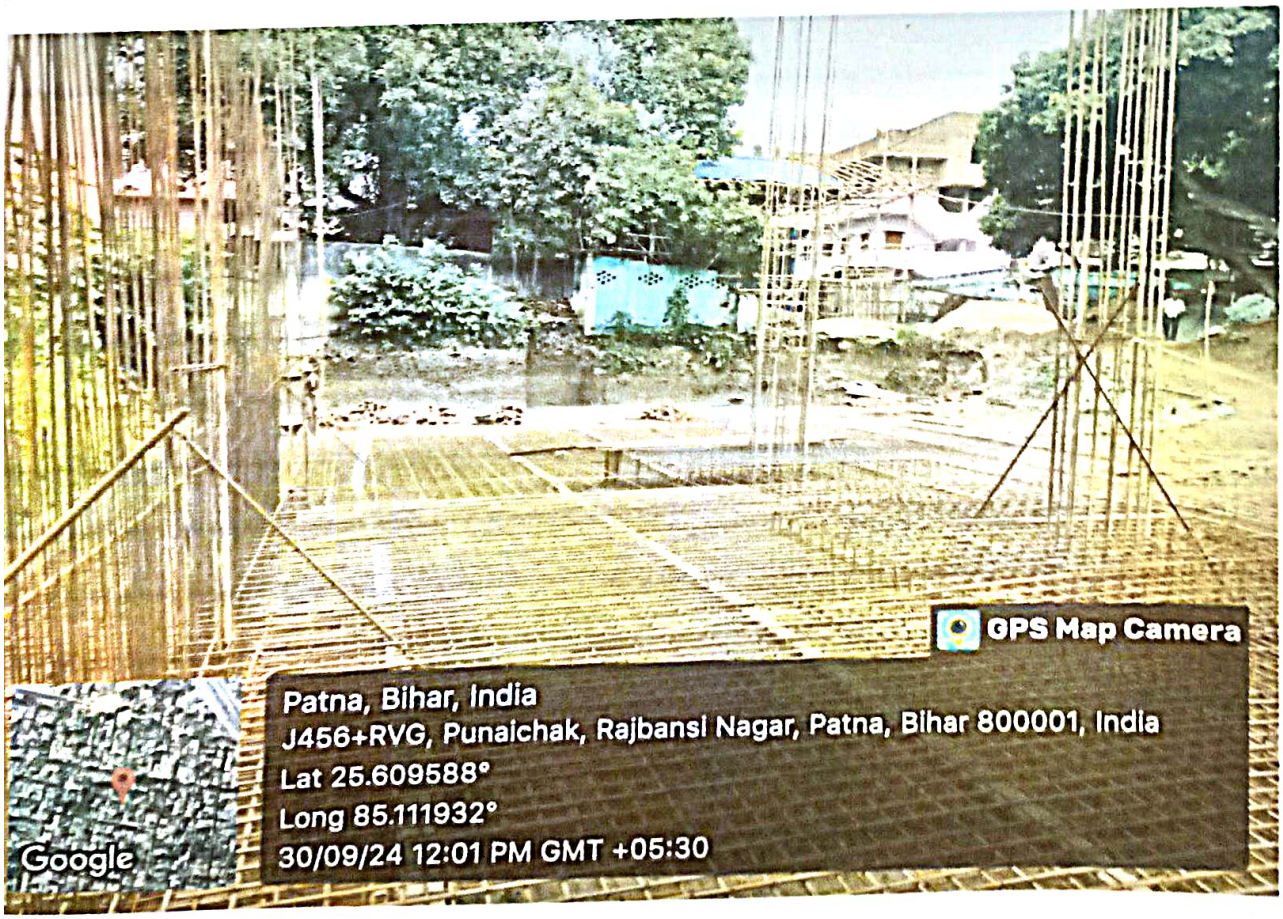
9.	Energy Management			

IX.	GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT		
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	



Bharti


GPS Map Camera
Patna, Bihar, India
J456+RVG, Punaichak, Rajbansi Nagar, Patna, Bihar 800001, India
Lat 25.609584°
Long 85.111927°
30/09/24 12:01 PM GMT +05:30
Google


GPS Map Camera
Patna, Bihar, India
J456+RVG, Punaichak, Rajbansi Nagar, Patna, Bihar 800001, India
Lat 25.609588°
Long 85.111932°
30/09/24 12:01 PM GMT +05:30
Google

Bharti

X. FINANCIAL PROGRESS OF THE PROJECT

S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	057905004882
2.	Estimated Cost of the Project including land cost at the start of the Project	13,95,34,286=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	7,01,08,286=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	44,75,801=00
6.	Actual Cost Incurred during the Quarter	36,30,614=00
7.	Net amount at end of the Quarter	11,35,898=00
8.	Total expenditure on Project till date	66,92,049=00
9.	Cumulative fund collected till the end of Quarter in question	49,05,671=00
10.	Cumulative expenditure done till the end of Quarter in question	66,92,049=00

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS

A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO

Bharti

B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

XIV UNITS ALLOCATION DETAILS

Total Number of sanctioned apartments	Details of allotment made so far with Flat number/ Bungalow - Plot etc	Cancellation of flat allotment, If any with Flat number/ Bungalow – Plot etc
1 BHK- 2 BHK -04 3 BHK-27 4 BHK- Shop- Bungalow - Plot etc		

XV. BROCHURE /Prospectus

XVI Grievance Redressal Officer

Name : Faisal Alam
Contact No : 9835037271
Email id : kastcretesales@gmail.com
Address : COMMERCIAL BUILDING-II, 2ND FLOOR, MOURYA COMPLEX, SOUTH GANDHI MAIDAN, PATNA

Bharti

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Kastcrete Buildmat Pvt. Ltd.

Signature of Promoter

Name: Bharti Sinha Bharti

Director

Date: 14/10/2024

BOOKING DETAILS

FLAT NO	TYPE
G-2	3 BHK
208	3 BHK
301	3 BHK
302	3 BHK
304	3 BHK
104	3 BHK
