QUARTERLY PROGRESS REPORT FOR RERA BIHAR

Apr - Jun, 2019

ABSTRACT

This report documents and describes the updates on project work progress, with updates on status of financials, bookings in the project along with status of the approvals for the quarter.

PROJECT NAME

SAI SHANTI ENCLAVE

PROMOTER NAME

AASTIK BUILDTECH PVT. LTD.

RERA REGISTRATION NO.

BRERAP00278-1/247/R-193/2018

Report Drafted by Limpid Construction Consulting LLP

For AASTIK BUILDTECH PVT. LTD.

Director

PROJECT QUARTERLY PROGRESS STATUS

Quarter: Apr-Jun, 2019

Project Description: *The Project is located just 3 minutes away from Saguna more and at a walking distance from St. Karen's Secondary School. The project comprises of a single residential building with G+3 floor.*

Progress Update of each Block/Wing separately

S. No.	Task/Activity	Applicable (Yes/No)	Percentage of Work Done	Remarks
1	Excavation	Yes	100%	Overall excavation works- complete
2	Foundation Works	Yes	100%	Overall foundation works- complete
3	Ground Floor	Yes	81%	Finishing works ongoing in ground floor with plastering works having being completed and putty works is under progress.
4	Slabs of super- structure	Yes	99%	Overall slab casting is complete and parapet wall construction is 90% complete.
5	Walls	Yes	93%	Construction of walls almost complete in 1st and 2nd floor. 3rd floor brickwork is under progress and is nearing completion.
6	Internal Plaster & Putty	Yes	47%	Plastering and putty works is going on in full swing
7	Flooring inside units and common areas	Yes	4%	Tiling works in floors and bathrooms has commenced and is going on in full swing.
8	Doors and Window to each of unit and common areas	Yes	30%	Door and window frame installation under progress.
9	Sanitary fittings within the unit including water proofing and plumbing	Yes	71%	Installation of SWR and CPVC pipes almost complete. Waterproofing and Koba works under progress.
10	Electrical fitting within the unit	Yes	29%	Conduit laying works almost complete.

For AASTIK BUILDTECH PVT. LTD.


Director

Progress Update of each Block/Wing separately

S. No.	Task/Activity	Applicable (Yes/No)	Percentage of Work Done	Remarks
11	Staircase, lift walls and lobbies at each floor	Yes	52%	Staircase, lift wall, and lobby structure works complete. Lobby finishing works started and Finishing works inside lift walls and staircase yet to start.
12	Water tank	Yes	30%	
13	External Plumbing works and completion of terrace with waterproofing of the building if specified.	Yes	0%	
14	External Plaster	Yes	69%	External plastering works almost complete on left, right and back elevation. It is yet to start on front elevation.
15	External Paint	Yes	13%	External putty and painting works under progress.
16	Installation of lifts water pumps, firefighting fittings as NOC, Electricals fittings to the common areas, electro mechanic equipment, finishing to the entrance lobby, plinth protection, paving of areas, compound walls and other requirements as may be required to obtain completion/occupancy certificate. (Misc. Works)	Yes	0%	

For AASTIK BUILDTECH PVT. LTD.

Director

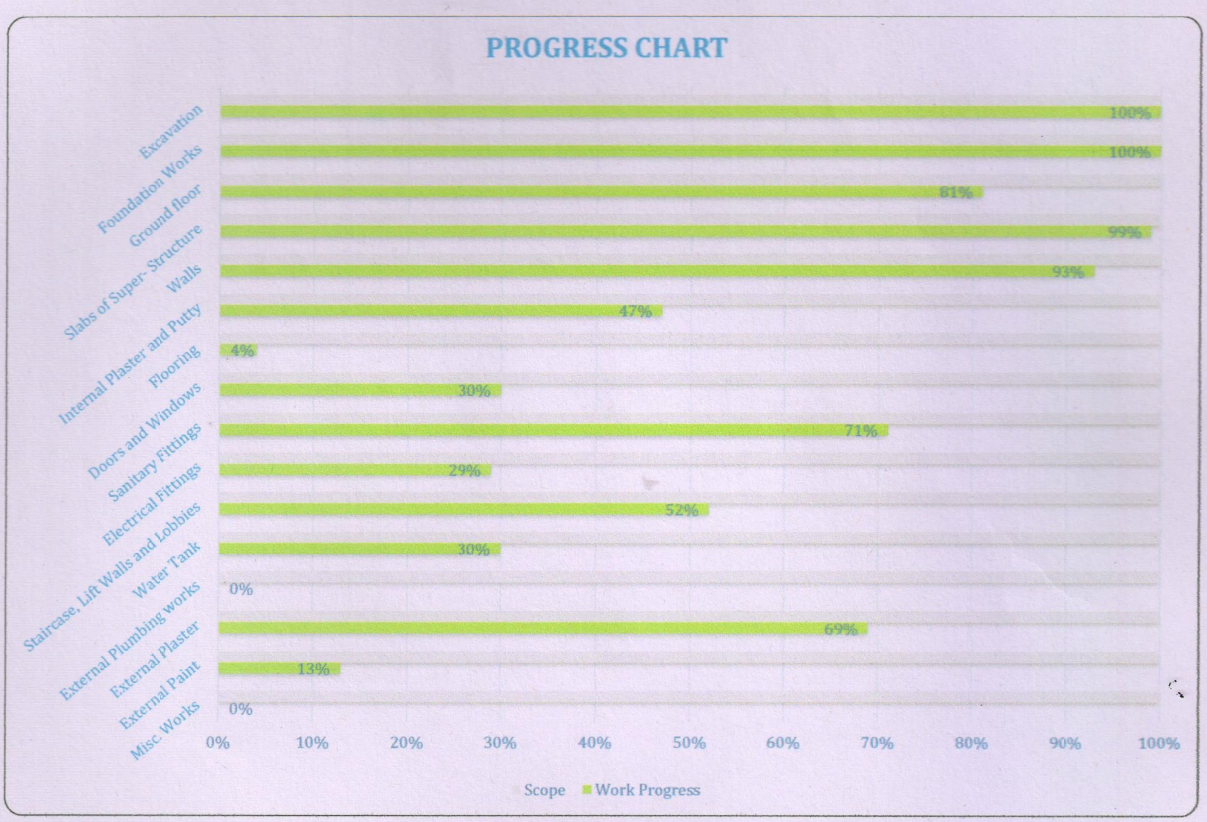

For AASTIK BUILDTECH PVT. LTD.

Director

Progress Updatefor Common Areas, Facilities and Amenities in the Project

S. No.	Description	Applicable (Yes/No)	Percentage of Work Done	Remarks
1	Compound Walls	Yes	40%	Compound wall construction under progress
2	Water supply	Yes	40%	Boring works complete and supply pipes installation balance.

For AASTIK BUILDTECH PVT. LTD.

Director

Update on number and types of flats/plots booked during the quarter

S.No	Unit Type	Total No. of Units in builder's Share	No. of Flats / Plot Booked				No. of Garages/ Covered Parking Booked			
			Opening Balance	Booked in the quarter	Cancelled in the quarter	Closing Balance	Opening Balance	Booked in the quarter	Cancelled in the quarter	Closing Balance
1	3 BHK	17	17	0	0	17	17	0	0	17
2	2 BHK	9	9	0	0	9	9	0	0	9

Status of financials in the project up to 30th June, 2019

S.No.	Description	Amount (in lacs Rs.)
1	Amounts received from allottees against booking of units(for builder's share)	890.59
2	Expenditure done towards completion of project	665.93
3	Balance in Designated Bank A/c as on this quarter end	0.00

Status of Approvals

A. Approval Received

S. No.	Description	Date of Receipt
1	Provisional Fire Clearance	06.05.16
2	Sanctioning of Building Plan	29.06.16
3	RERA Registration	27.09.18

B. Approval Applied

S. No.	Description	Expected Date
NA	NA	NA

C. Approvals to be applied

S. No.	Description	Expected Date of application
NA	NA	NA

D. Modifications amendments or revisions, if any, issued by competent authority with regard to any sanctioned plans, layout plans, specifications, license, permit or approval for the project - NA

For AASTIK BUILDTECH PVT. LTD.

Director

Project Site Photographs




For AASTIK BUILDTECH PVT. LTD.

Director



For AASTIK BUILDTECH PVT. LTD.

Director

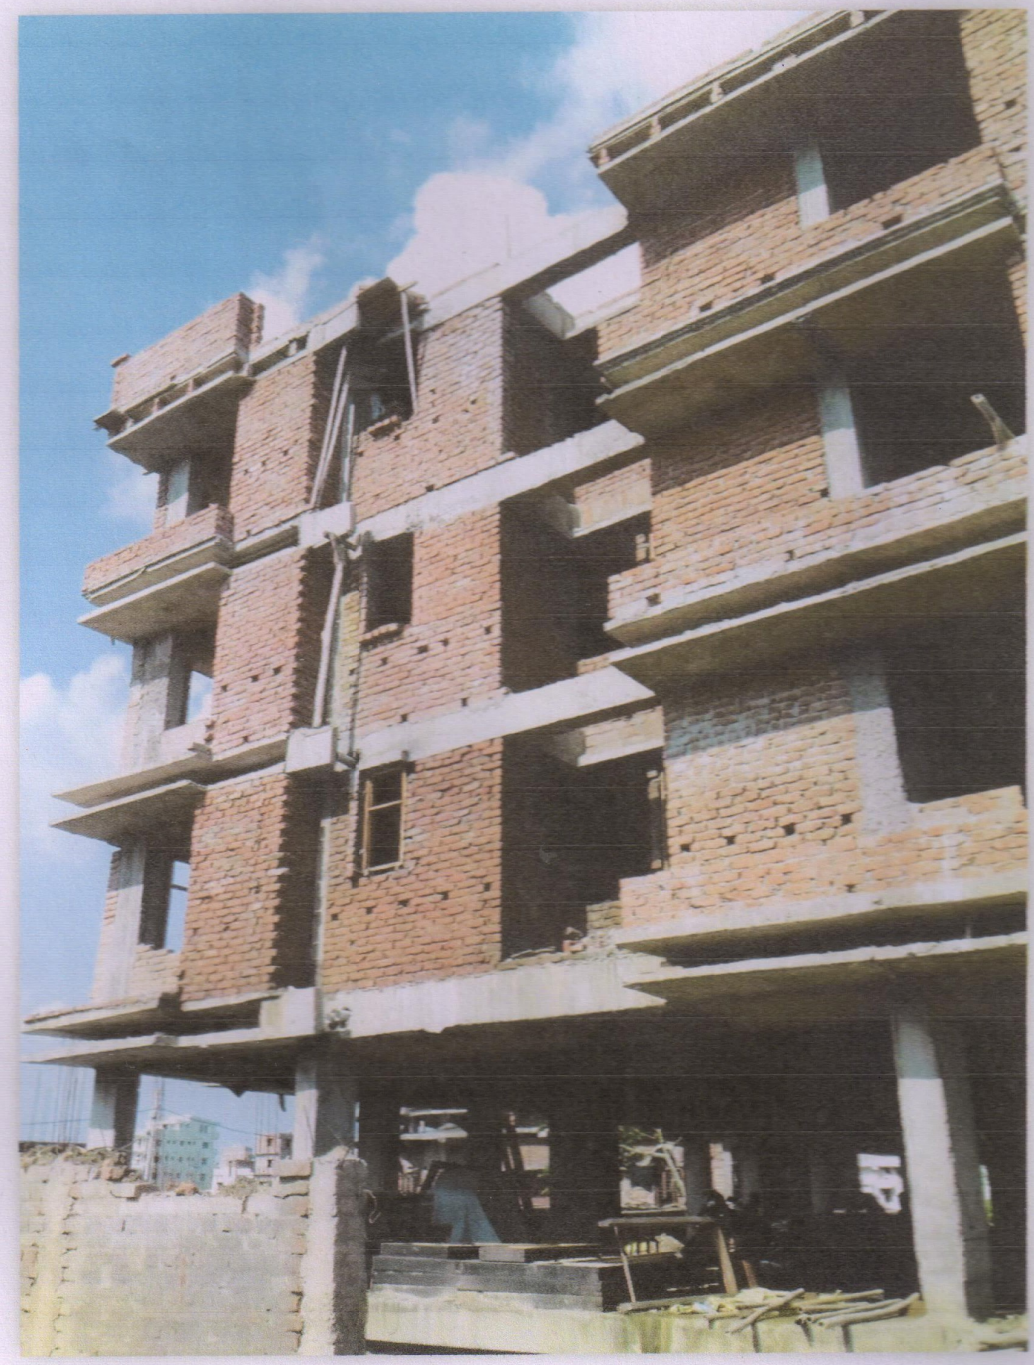

For AASTIK BUILDTECH PVT. LTD.

Director
