FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending June of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies		Name of Firm	BRIJ KISHORE MISHRA
Firm Address :	11-KAUTILYAPURI COLONY, OPPOSITE SSP RESIDENCE, GAYA-823001		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA			
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	01	JAI RAM RESIDENCY
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	01	CHANDRASHEKHAR APARTMENT

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP00282-2/174/R-1473/2022	Name of Project/Phase of Registered Project	CHANDRASHEKHAR APARTMENT, BLOCK-B,C,D
Name of Promoter	BRIJ KISHORE MISHRA	Project Address	Village-Kendua,P.S-Magadh Medical College, Anchal-Chandauti, District-Gaya
Name of Co-promoter	N/A		
Project Registration is valid up to	15/08/2027		
Starting date of Project or Phase of the Project	14/10/2022		
Type of Project or Phase of the Project	Residential-Cum-Commercial		
Period of validity of map by the Competent Authority	4 YEARS 10 MONTHS		

Brij Kishore Mishra

Brij Kishor Mishra

Proprietor

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share -	Total Number of Apartments in Landowner's share -
BLOCK-B.C,D	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.	20 50	12647.57 41432.00	70	1. Booked / Allotted -32 2. Sold-NIL	3. Booked/ Allotted-02 Sold -NIL
					Percentage of booking	Percentage of booking 0%

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted -	32
BLOCK-B.C,D	70	2. Sold -	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No.118/22-23

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	BLOCK-B-100% BLOCK-C-100% BLOCK-D-50%	30-08-2024

Brij Kishore Mishra

Brij Kishore Mishra

Proprietor

2.	Basements (if any)	N/A	
3.	Podiums (if any)	N/A	
4.	Plinth	BLOCK-B-100% BLOCK-C-100% BLOCK-D-50%	30-08-2024
5.	Stilt Floor	N/A	
6.	Slabs of Super Structure	BLOCK-B-40% BLOCK-C-20% BLOCK-D-0%	14-06-2024
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	BLOCK-B-0% BLOCK-C-0% BLOCK-D-0%	10-02-2025
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	BLOCK-B-0% BLOCK-C-0% BLOCK-D-0%	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	BLOCK-B-0% BLOCK-C-0% BLOCK-D-0%	10-10-2025
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	BLOCK-B-0% BLOCK-C-0% BLOCK-D-0%	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	BLOCK-B-0% BLOCK-C-0% BLOCK-D-0%	

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

Brij Kishore Mishra

Brij Kishore Mishra

Proprietor

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	BLOCK-B-0% BLOCK-C-0% BLOCK-D-0%	
2.	Water Supply	YES	BLOCK-B-0% BLOCK-C-0% BLOCK-D-0%	22-02-2026
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	BLOCK-B-0% BLOCK-C-0% BLOCK-D-0%	22-02-2026
4.	Storm Water Drains	YES	BLOCK-B-0% BLOCK-C-0% BLOCK-D-0%	22-02-2026
5.	Landscaping & Tree Planting	NO		
6.	Street Lighting	YES	BLOCK-B-0% BLOCK-C-0% BLOCK-D-0%	22-02-2026
7.	Community Buildings	NO		
8.	Treatment and Disposal of Sewage and Sullage Water	YES	BLOCK-B-0% BLOCK-C-0% BLOCK-D-0%	22-02-2026
9.	Solid Waste Management & Disposal	YES	BLOCK-B-0% BLOCK-C-0% BLOCK-D-0%	22-02-2026
10.	Water Conservation / Rain Water Harvesting	YES	BLOCK-B-0% BLOCK-C-0% BLOCK-D-0%	22-02-2026
11.	Energy Management	YES	BLOCK-B-0% BLOCK-C-0% BLOCK-D-0%	
12.	Fire Protection and Fire Safety Requirements	YES	BLOCK-B-0% BLOCK-C-0% BLOCK-D-0%	25-05-2026
13.	Closed Parking	YES	BLOCK-B-0% BLOCK-C-0% BLOCK-D-0%	25-05-2026
14.	Open Parking	NO		
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	BLOCK-B-0% BLOCK-C-0% BLOCK-D-0%	25-05-2026

Brij Kishore Mishra

Brij Kishore Mishra

Proprietor

16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

Brij Kishore Mishra

Brij Kishore Mishra

Proprietor

X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	7274868076
2.	Estimated Cost of the Project including land cost at the start of the Project	
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	
4.	Any Variation in Development Cost which is declared at the start of the Project .	
5.	Amount received during the Quarter	69,26,000=00
6.	Actual Cost Incurred during the Quarter	93,78,187=00
7.	Net amount at end of the Quarter	12,09,973=00
8.	Total expenditure on Project **till date**	3,78,29,559=00
9.	Cumulative fund collected till the end of Quarter in question	NIL
10.	Cumulative expenditure done till the end of Quarter in question	NIL

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO

Brij Kishore Mishra

Brij Kishore Mishra

Proprietor

B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	32
3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Brij Kishore Mishra

Proprietor

Signature of Promoter

Name:

Date:



Q235+8QX, Gaya, Bihar 823003, India

Latitude
24.7531766666666665°

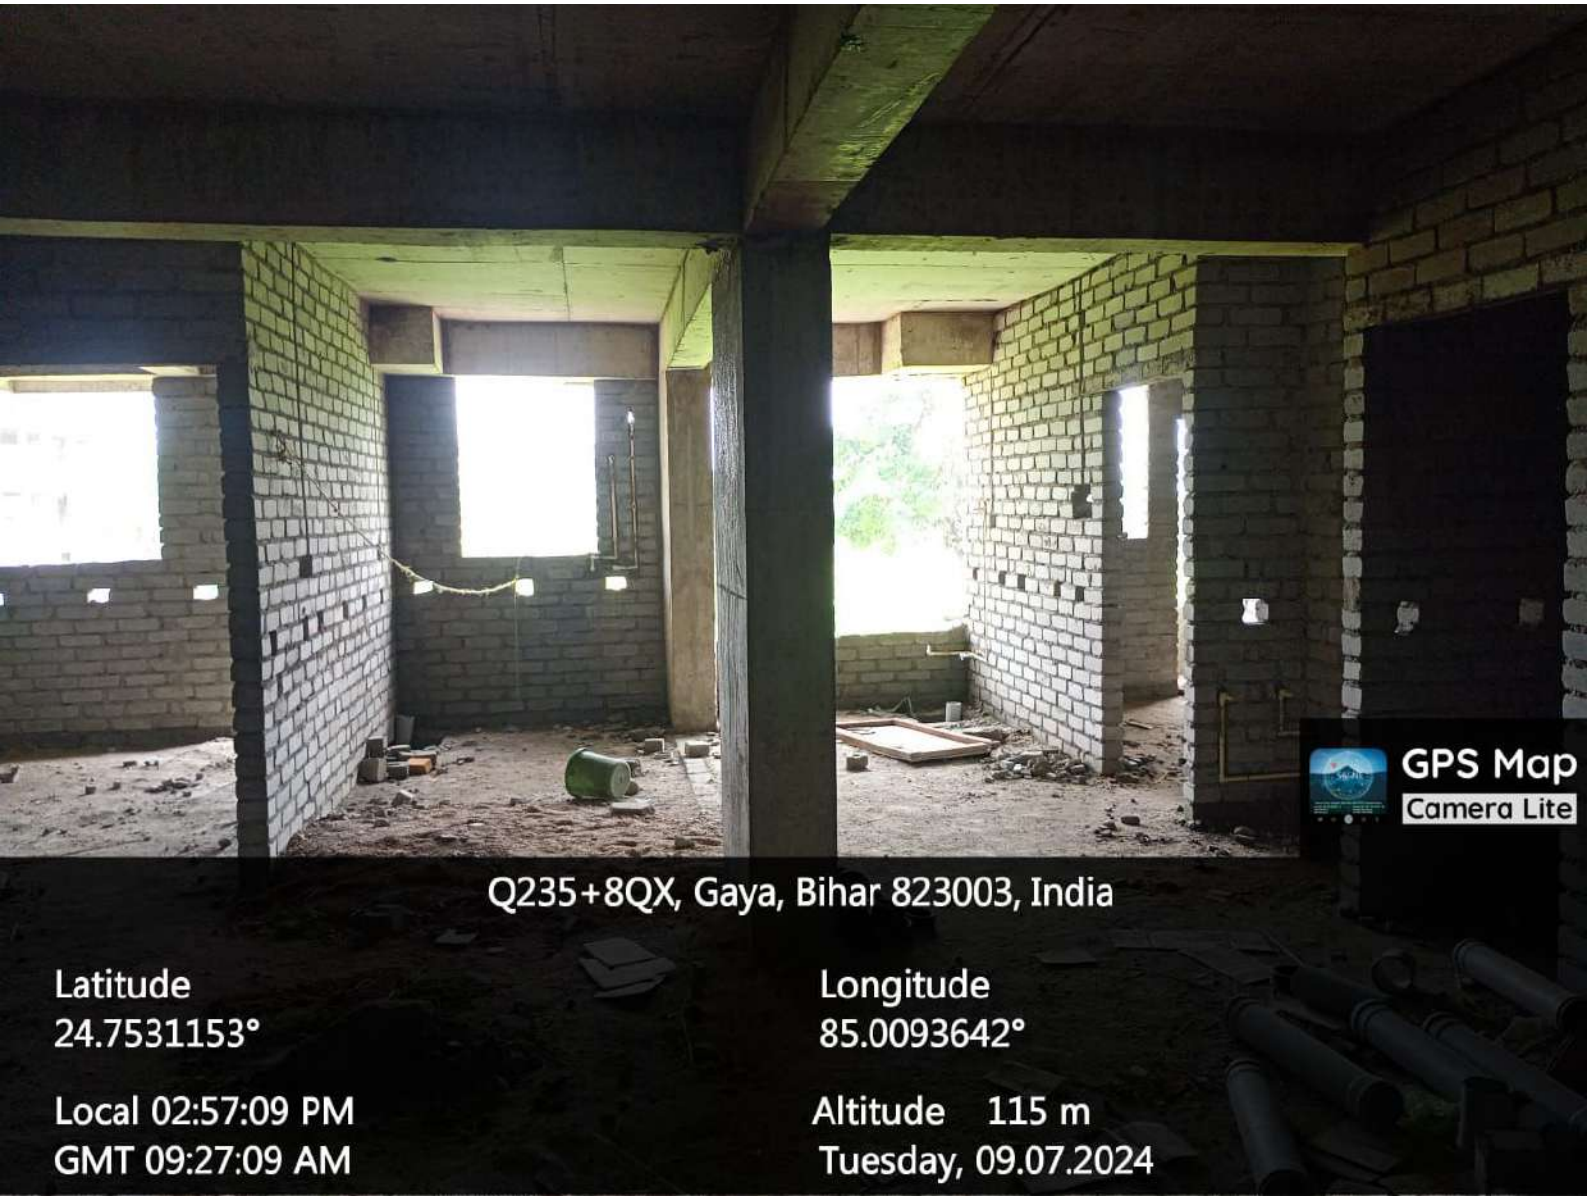
Longitude
85.00886999999999°

Local 03:05:31 PM
GMT 09:35:31 AM

Altitude 115 m
Tuesday, 09.07.2024


GPS Map
Camera Lite
Q235+8QX, Gaya, Bihar 823003, India
Latitude
24.753106666666667°
Longitude
85.00937°
Local 03:00:42 PM
GMT 09:30:42 AM
Altitude 115 m
Tuesday, 09.07.2024


GPS Map
Camera Lite
Q235+8QX, Gaya, Bihar 823003, India
Latitude
24.7529050000000002°
Longitude
85.009150000000002°
Local 02:58:12 PM
GMT 09:28:12 AM
Altitude 115 m
Tuesday, 09.07.2024


GPS Map
Camera Lite
Q235+8QX, Gaya, Bihar 823003, India
Latitude
24.7531153°
Longitude
85.0093642°
Local 02:57:09 PM
GMT 09:27:09 AM
Altitude 115 m
Tuesday, 09.07.2024
