FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending March of 2025

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Registration no. of the Partnership firm/LLP Identification number/Any other	CIN NO. U70102BR2013PTC021650	Name of the Promoter's Entity SAI RAM REAL ESTATE PRIVATE LIMITED	Remarks
Address of the Promoter's Entity :	BUILDING NO. 1/MB, INDRASAN MITRA VIHAR COLONY, WEST BORING CANAL ROAD, PATNA, BIHAR, INDIA - 800001		
Total Experience of the promoter in Real Estate sector (In Completed years)			
Total Experience in Real Estate Sector after Commencement of RERA (In Completed years)			
No of Projects done before Commencement of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	01	
No of Project done After Commencement of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	01	

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP00890-2/793/R-719/2019	Name of Project	SAI PALACE
Name of Promoter	SAI RAM REAL ESTATE PRIVATE LIMITED	Project Address	PLOT NO-1530, 1531, 1532 LAKHNI BIGHA DANAPUR PATNA
Project Registration is valid up to	31/12/2022		
Starting date of Project	13/08/2019		
Type of Project	Residential		
Name of the Competent Authority which sanctioned the project map			

SAI RAM REAL ESTATE PVT. LTD.

Managing Director

Period of validity of map as granted by the Competent Authority concerned	3 YEARS		

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building/ Block Number	Apartment/ Unit Type	Carpet Area	Total Number of sanctioned apartments/ unit-wise	Total Numbers of apartments in Promoter's share-20	Total Numbers of apartments in Promoter's share-20	Total Numbers of apartments in Landowner's share-20	Total Numbers of apartments in Landowner's share-20
				Booked	Agreement for sale Executed	Booked	Agreement for sale Executed
	1-BHK						
	2-BHK						
	3-BHK		40	17		NIL	NIL
	4-BHK and over						
	shop						
	Office Space						
	Bunglow						
	Plots (in case of plots specific area of plot must be mentioned)						
		Total Carpet Area		% of total Units 85%	% of total Units	% of total Units 0%	% of total Units 0%

IV. DETAILS OF ASSOCIATION OF ALLOTTEES :

Mandatory in case the booking percentage exceeds 50% of the total sanctioned flats/plots/buildings/commercial space

The details of the Association of Allottees need to be provided in the proforma of Association of Allottees attached with this Form.

V. CANCELLATION OF FLAT ALLOTMENT, IF ANY WITH FLAT NUMBER/BUNGALOW/PLOT NO./OFFICE SPACE/SHOP/ETC.

(A) Cancelled by Allottees	(B) Cancelled by Promoters
Flat No./Plot no./Shop No./Etc. :	Flat No./Plot no./Shop No./Etc. :
*whether notice and reminder of cancellation was	*whether notice and reminder of cancellation has

SAI RAM REAL ESTATE PVT. LTD.

Managing Director

Served to the promoters by Allottee/s Yes/No	been Served to the Allottees by serving Yes/No

VI. DISCLOSURE OF BOOKED INVENTORY OF GARAGES/PARKING SPACE

Building Wise / Block Number	Total Number of Sanctioned Garages/Parking Space	Total Number of Garages/Parking Space: 1. Booked/Allotted
	30	06

VII. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Validity up to		Attach Copy
1.	Environment Clearance	N/A			
2.	Fire N.O.C.	STATE FIRE OFFICER, BIHAR	12-09-2017		
3.	Airport Authority of India N.O.C.	N/A			
4.	Water Supply Permission	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

VIII. PROGRESS OF THE PROJECT–INTERNAL INFRASTRUCTURE DEVELOPMENT

In case of more than one Block/Building/Apartment/Plots/Bungalow, the details have to be filled for each Block separately

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)		
2.	Basements (if any)		
3.	Podiums (if any)		
4.	Plinth	100%	
5.	Stilt Floor		

SAI RAM REAL ESTATE PVT. LTD.

Managing Director

6.	Slabs of Super Structure	100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100% 90%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	90% 50%	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.		
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	100%	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per prescribed norms	0%	
12.	N.O.C, Electrical fittings, Mechanical Equipment, compliance to conditions of environment as per prescribed norms	0%	
13.	Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per Specifications in Agreement of Sale. Any other activities	0%	
14.	Overall Percentage of Actual work Done and Final Completion date		

IX. EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS – PEOGRESS RELATED TO AMENITIES AND COMMON AREA

SAI RAM REAL ESTATE PVT. LTD.

Managing Director

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES		
2.	Water Supply	YES		
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES		
4.	Storm Water Drains	NO		
5.	Landscaping & Tree Planting	NO		
6.	Street Lighting	YES		
7.	Community Buildings	NO		
8.	Treatment and Disposal of Sewage and Sullage Water	NO		
9.	Solid Waste Management & Disposal	YES		
10.	Water Conservation / Rain Water Harvesting	YES		
11.	Energy Management	YES		
12.	Fire Protection and Fire Safety Requirements	YES		
13.	Closed Parking	YES		
14.	Open Parking	YES		
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES		
16.	Others (Option to Add More)			
17.	Overall Percentage of Actual Work Done and final Completion date			

SAI RAM REAL ESTATE PVT. LTD.

Managing Director

X.	EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT			
		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

XI.	FINANCIAL PROGRESS OF THE PROJECT	
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	6236002100000433
2.	Estimated Cost of the Project including land cost at the start of the Project	12,99,00,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	7,99,00,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	17,69,833=00

SAI RAM REAL ESTATE PVT. LTD.


Managing Director

6.	Actual Cost Incurred during the Quarter	17,69,000=00
7.	Net amount at end of the Quarter	833=00
8.	Total expenditure on Project **till date**	
9.	Cumulative fund collected till the end of Quarter in question	
10.	Cumulative expenditure done till the end of Quarter in question	
11.	Percentage of Expenditure incurred of the total Estimated development cost of the project	

XIII. GEO TAGGED AND DATE PHOTOGRAPH (EACH BLOCK/BUILDING/APARTMENT/PLOTS/BUNGLOW) OF THE PROJECT


The photograph must have date.


(A)	Sr. No.		
	1.	Photographs showing Front Elevation	ATTACH
	2.	Photographs showing Rear Elevation	ATTACH
	3.	Photographs showing Side Elevation (Both Sides)	ATTACH
	4.	Photograph of each floor showing the progress of interior works	
	5.	Photographs of Common Areas (Staircase, Lift Area, Terrace, parking, etc.)	
(B)	Sr. No.		
	1.	Photograph of the display board set up at the project site providing requisite information along with the QR code of the project allotted by the Authority	

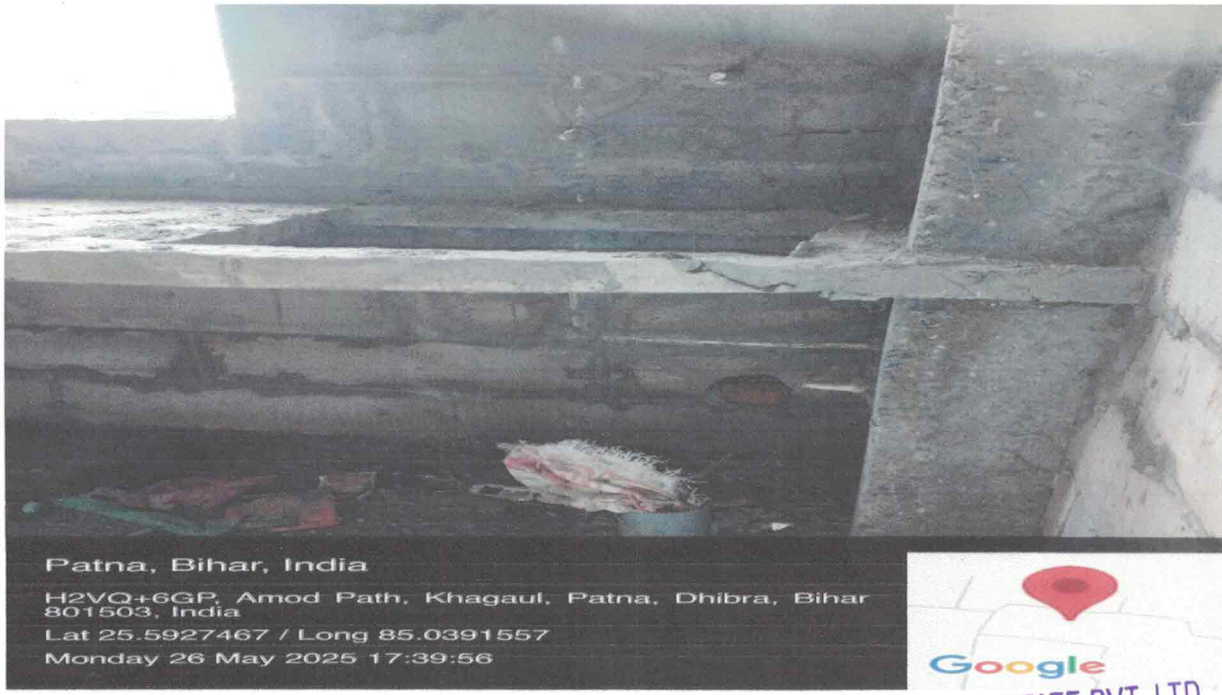

SAI RAM REAL ESTATE PVT. LTD.


Managing Director

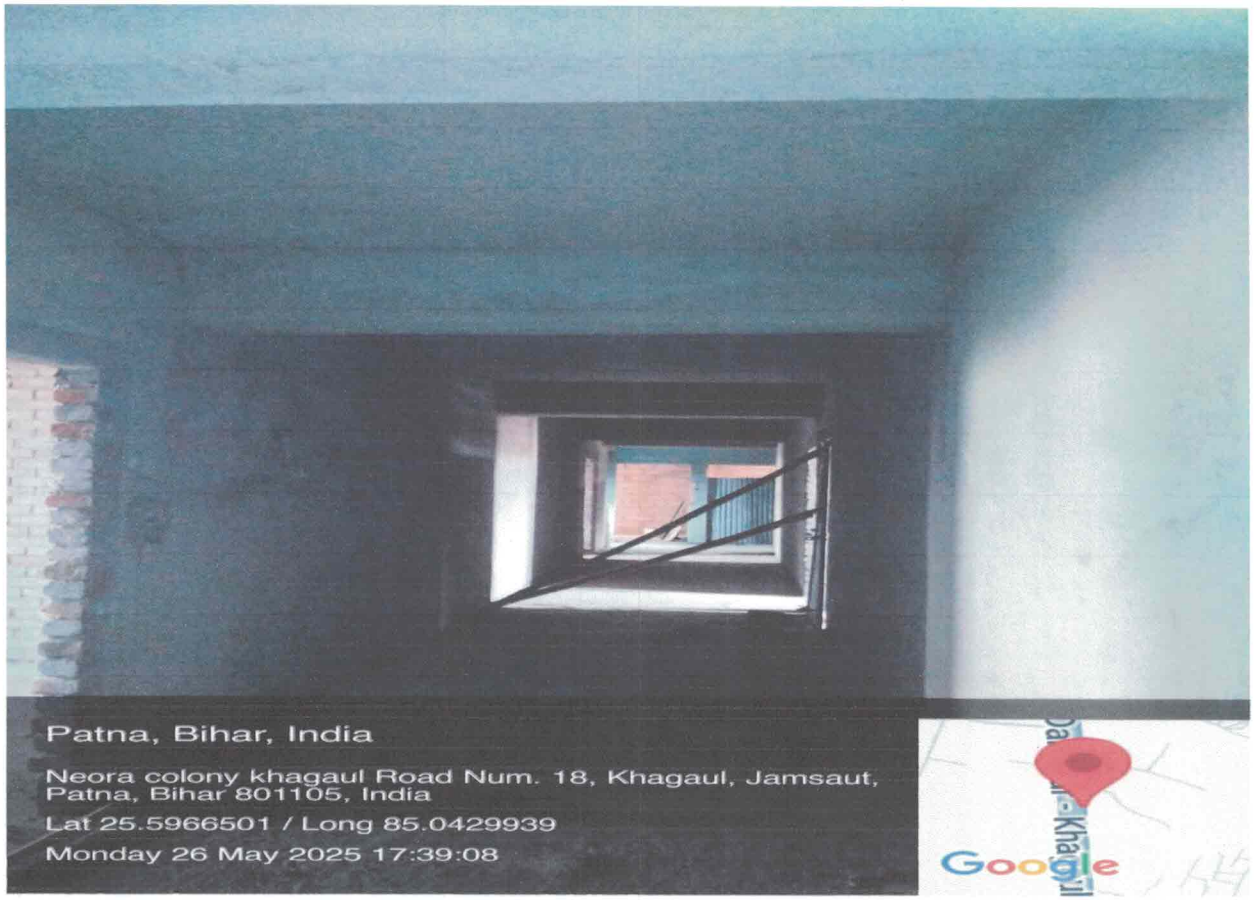

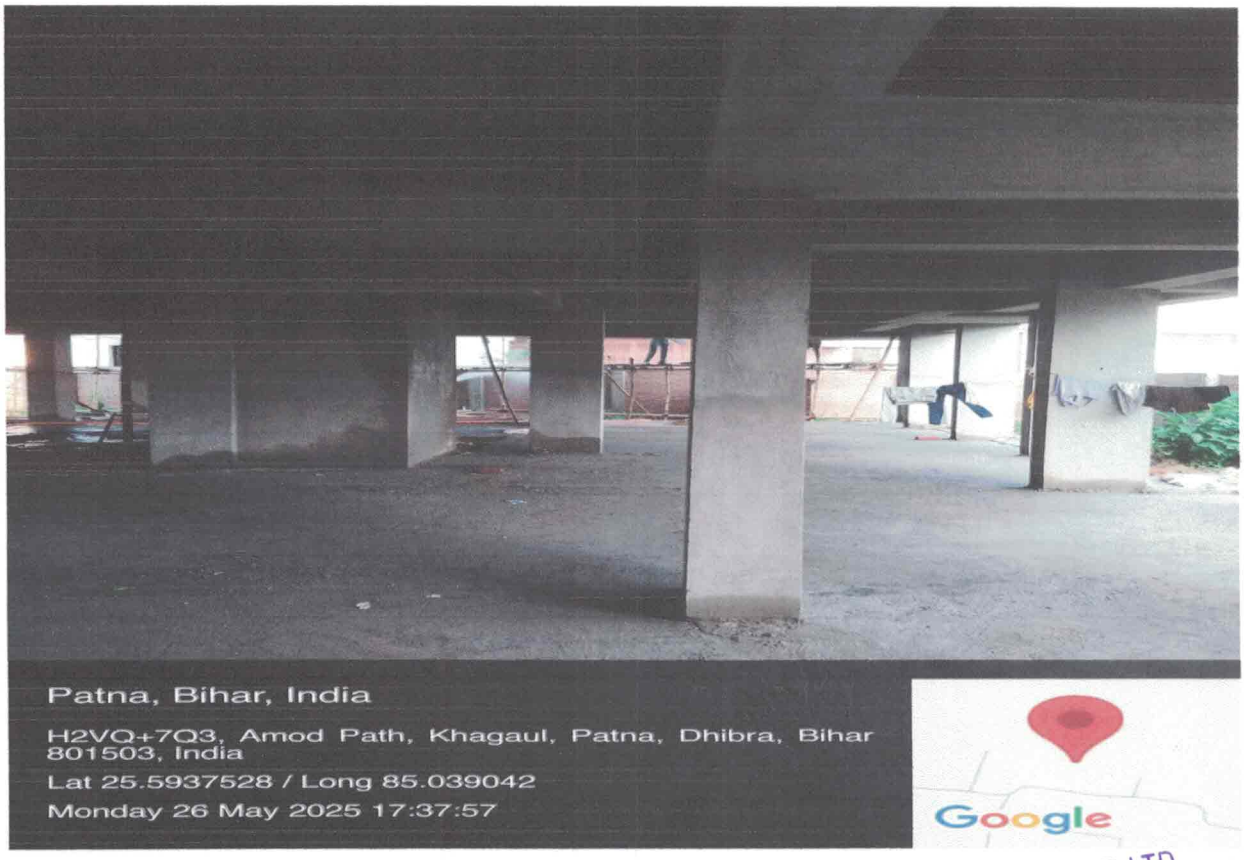

SAI RAM REAL ESTATE PVT. LTD.

Managing Director

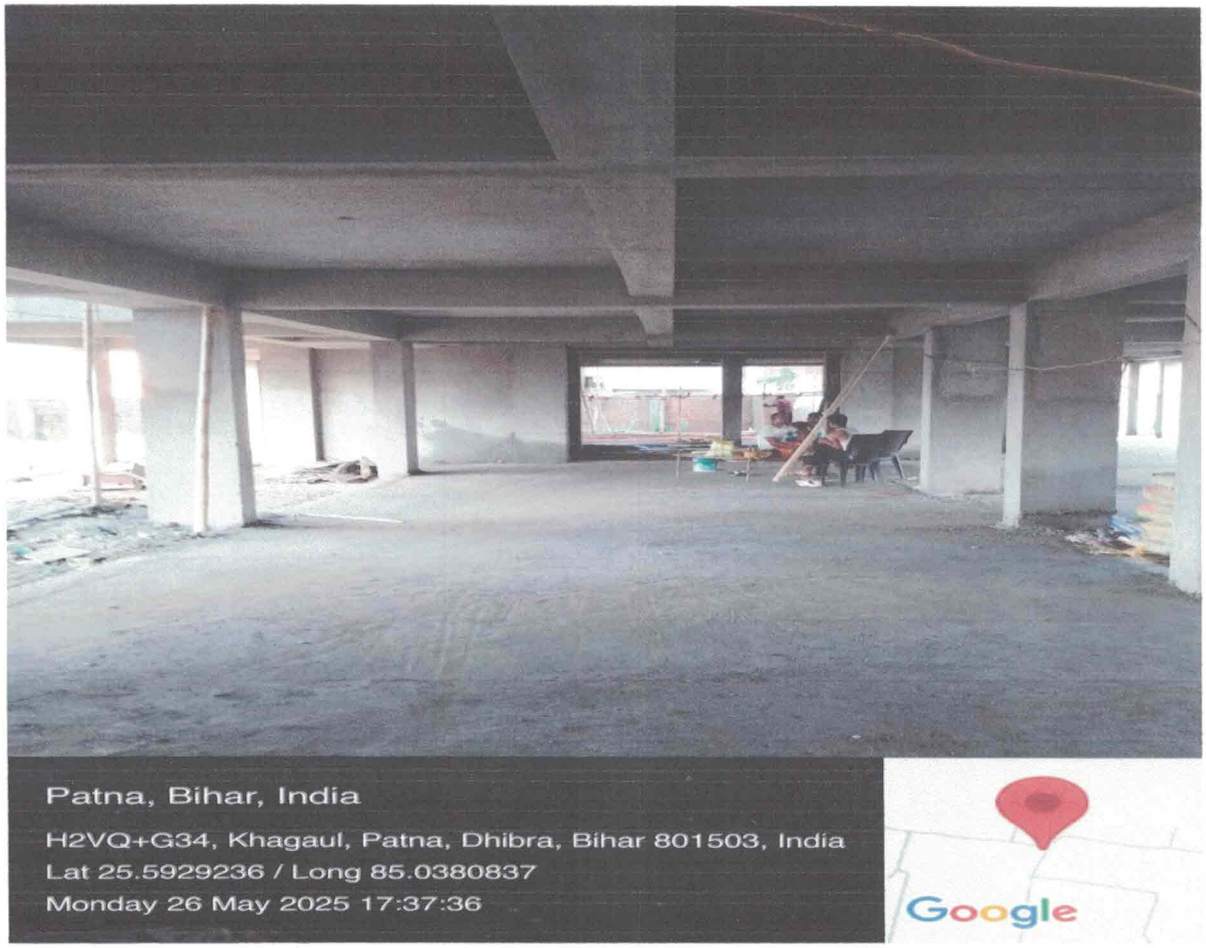

XIV. MISCELLANEOUS	
A	List of Legal Cases (if any) – Against Project / Promoter
1.	(a) Case No. (b) Name of Parties Order passed, if Yes, Whether complied (Yes/No) NO
2.	No of Execution Cases against this project (a) Case No. (b) Name of Parties Order passed, if Yes, Whether complied (Yes/No) NO
3.	No of Suo - Moto cases against this project (a) Case No. (b) Name of Parties Order passed, if Yes, Whether complied (Yes/No) NO

SAI RAM REAL ESTATE PVT. LTD.

Managing Director

4.	No of Certificate cases /PDR cases against this project (a) Case No. (b) Name of Parties Order passed, if Yes, Whether complied (Yes/No) NO

XV. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

a. Weather the project in progress as per time schedule or lagging behind? Yes/No
b. If yes, whether it would be completed on the completion date fixed as per RC. Yes/No.
c. If No, then Reason for delay:

XVI. BROCHURE /Prospectus : Copy of the brochure/prospectus to be uploaded with Form-7

XVII Name of Grievance Redressal Officer nominated by the promoter whom allottee can contact in case of any query or grievance

Name : SURENDRA KUMAR
Contact No : 9262548665
Email id : saiestate2014@gmail.com
Address : H/O-APARNA KUMARI,SHIVPURI,OPP MAMTA APPARTMENT,SHASTRI NAGAR PATNA

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

SAI RAM REAL ESTATE PVT. LTD.
Managing Director

Signature of Promoter

Name:

Date:
