FORM-7

[REGULATION-9]

Quarterly Progress Report for quarter ending Apr-Jun of 2024 (Year)

I. PARTICULARS OF PROMOTERS	
Promoter's Registration Number/CIN No.	U00500BR2002PTC009717
Firm Address:	PO+PS-AMARPUR, DISTRICT-BANKA BIHAR 813101
Total Experience of promoter in Real Estate Sector	6 Years
Total Experience in Real Estate After Implementation of RERA	6 Years
No of Project done Before Implementation of RERA	No Any
No of Project done After Implementation of RERA	1. Raghukul Padmalaya 2. Ram Asha Aashram

II. PARTICULARS OF PROJECT	
Project Registration Number	BRERAP00314-2/140/R-1272/2022
Name of Project/Phase of Registered Project	RAM ASHA AASHRAM
Name of Promoter	AMARPUR CONSTRUCTION COMPANY PRIVATE LIMITED
Project Address	Mohhala- Naya Tola, Bhikhanpur, At Gyanandra Mukharjee Road, Thana- Ishakchak, Anchal- Jagdishpur, Ward No- 36, Holding No- 47, Khata No- 121, Khesra No- 281, Under Municipal Corporation Bhaglapur,Bihar., Dist.- Bhaglapur
Name of Co-promoter	NA
Project Registration is valid up to	22/02/2023
Starting date of Project or Phase of the Project	28/09/2021
Type of Project or Phase of the Project	Residential/Group Housing
Period of validity of map by the Competent Authority	Three Years from the date of passing of MAP

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building/Block Number	Apartment Type	Carpet Area (In Sqft)	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share –	Total Number of Apartments in Landowner's share –
Ram Asha Aashram	2 BHK	922.00	1	**1. Booked/ Alloted - 00** **2. Sold –**	**3. Booked/ Alloted -** **4. Sold -**
Ram Asha Aashram	3 BHK	1075.00	1		
Ram Asha Aashram	3 BHK	1348.00	1		
Ram Asha Aashram	3 BHK	1591.00	4		
Ram Asha Aashram	3 BHK	1190.00	3	Percentage of booking-	
Ram Asha Aashram	3 BHK	1075.00	3		Percentage of booking-
Ram Asha Aashram	3 BHK	1348.00	3		

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of SanctionedGarages	Total Number of Garages:	
Ram Asha Aashram	No Garages available	**1. Booked/Allotted -** **2. Sold -**	

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission /Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

VI. Construction Progress of the Project

Building / Wing / Layout Number- Ram Asha Aashram (To be added for each Building / Wing)

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	**100%**	**Completed**
2.	Basements (if any)	**100%**	**Completed**
3.	Podiums (if any)	**NA**	
4.	Plinth	**100%**	**Completed**
5.	Stilt Floor	**NA**	
6.	Slabs of Super Structure	**100%**	**Completed**
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	**100%**	**Completed**
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	**100%**	**Completed**
9.	Staircases, Lifts Walls and Lobbies at each Floor level, Overhead and Underground Water Tanks.	**100%**	**Completed**
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	**90%**	**Completed**
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as my be required to complete project as per specifications in Agreement of Sale. Any other activities.	**70%**	**10-08-2024**

VII. (Amenities and Common Area and External Infrastructure Development Works)				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	No		
2.	Water Supply	Yes	100%	Completed
3.	Sewerage (Chamber, Line, Septic Tank, STP)	Yes	100%	Completed
4.	Storm Water Drains	No		
5.	Landscaping & Tree Planting	No		
6.	Street Lighting	No		
7.	Community Buildings	No		
8.	Treatment and Disposal of Sewage and Sullage Water	No		
9.	Solid Waste Management & Disposal	No		
10.	Water Conservation / RainWater Harvesting	No		
11.	Energy Management	No		
12.	Fire Protection and FireSafety Requirements	Yes	**100%**	Completed
13.	Closed Parking	Yes	100%	Completed
14.	Open Parking	No		
15.	Electrical Meter Room, Sub-Station, Receiving Station	Yes	100%	Completed
16.	Others (Option to AddMore)	No		

VIII. EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT
Not Applicable because our project is Residential/Group Housing.


IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT		
(A)	S.No.	Particulars
	1.	Front Elevation.- Attached Below
	2.	Rear Elevation- Attached Below
	3.	Side Elevation- Attached Below
(B)		Photograph of each floor

X. Financial Progress of the Project		
Sr.No.	**Particulars**	**Amount (in Rs.)**
1	Project Account No.	180805000749
2	Estimated Cost of the Project including land cost atthe start of the Project	163.00 /- **(In Lakh)**
3	Estimated Development Cost of the Project at the start of the Project (Excluding Land Cost)	148.00/- **(In Lakh)**
4	Any Variation in Development Cost which is declared at the start of the Project	
5	Amount received during the Quarter	0.00/-
6	Actual Cost Incurred during the Quarter	56,78,569.00/-
7	Net amount at end of the Quarter	
8	Total expenditure on Project **till date**	3,72,53,020.00/-
9	Cumulative fund collected till the end of Quarter in question	0.00/-
10	Cumulative expenditure done till the end of Quarter in question	3,72,53,020.00/-

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any)	
1.	Case No.	NA
2.	Name of Parties	NA
3.	No of Execution Cases against this project Case No. Name of Parties	
4.	No of Suo - Moto cases against this project Case No. Name of Parties	
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	
B	Sale/Agreement for Saleduring the Quarter	
1.	Sale Deed	
2.	Agreement for Sale	

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART
Weather the project in progress is as per time schedule or lagging behind?

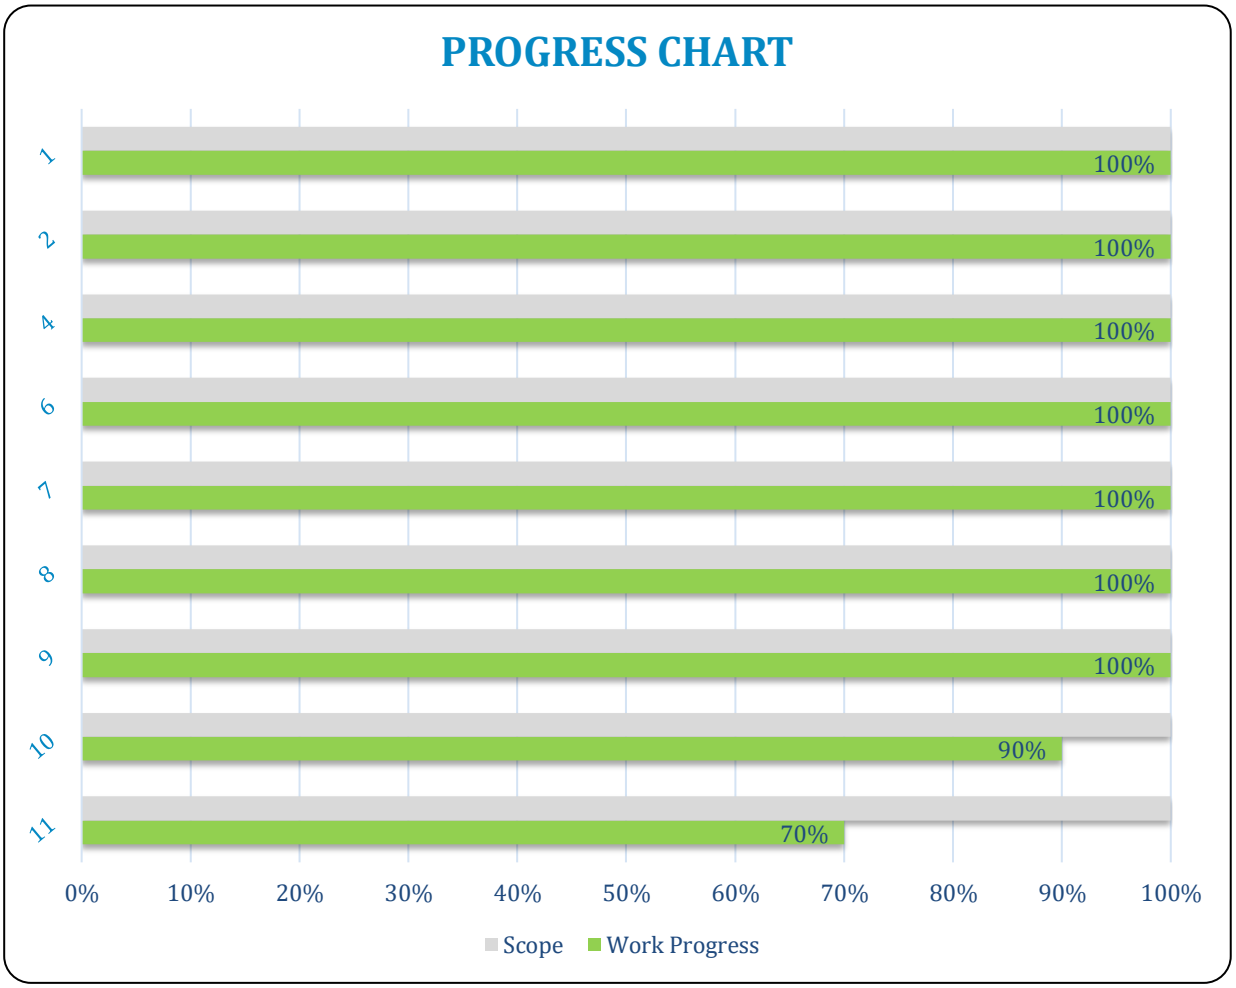

Project Site Photographs

Front Elevation



Side Elevation




Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Signature of Promoter

Amarpur Construction Company Private Limited.



Director

Date :
