FORM -7

[REGULATION-9]

Quarterly Progress Report for quarter ending March/June/Sept/**December** of **2022** (Year)

I. PARTICULARS OF PROJECT			
Project Registration Number	**BRERAP00057-2/30/R-1368/2022**	Name of Project/Phase of Registered Project	**SURYA SIGNATURE / 1**
Name of Promoter	**Surya Nestbuild Limited**	Project Address	**Mauza-Mustafapur Saguna Khagual Main Road, PS Khagaul, Patna**
Name of Co-promoter			
Project Registration is valid up to	**10/06/2027**		
Starting date of Project or Phase of the Project	**08/04/2022**		
Type of Project or Phase of the Project	1. Residential 2. Commercial 3. Residential-cum-Commercial 4, Plotted project	**Commercial Cum Residential**	
Period of validity of map by the Competent Authority	5 Years		

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS					
Building/Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments – 4
4 / Block-A, Block-B, Block-C, Block-D EWS/LIG.	1. 1 BHK - 2. 2 BHK - 3. 3 BHK - 4. 4 BHK - 5. Shop/Office space/unit - 5.Bungalow - 6. Plot etc. -	13 7	- - - - -	4	1. Booked/ Allotted - 20 2. Sold -0

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES			
Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages: 1. Booked/Allotted -	20
4	20	2. Sold -	0

IV. DETAILS OF BUILDING APPROVALS (If already filed along with Registration Application, then there is no need of further filing)					
S. No.	Name of the Approval / N.O.C. / Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	-	-	-	Attached
2.	Fire N.O.C.	-	-	-	Attached
3.	Water Supply Permission	-	-	-	-
4.	NOC from Airport Authority of India	-	-	-	Attached
5.	Other Approval(s),	-	-	-	-

	if any required for the Project.				

V. Construction Progress of the Project		
1. Plan Case Number_____(To beaded for each Building / Wing)		
S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	70 % of Block-'C'
2.	Basements (if any)	70 % of Block-'C'
3.	Podiums (if any)	N/A
4.	Plinth	70 % of Block-'C'
5.	Stilt Floor	50 %
6.	Slabs of Super Structure	Block- C 70 % 2nd Basement 70 % 1st Basement 70% Ground Floor
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0 %
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0 %
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0 %
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0 %
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as my be required to complete project as per specifications in Agreement ofSale. Any other activities.	0%

VI. Amenities and Common Area and External Infrastructure Development Works)				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	Yes	0 %	
2.	Water Supply	Yes	0 %	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	Yes	0 %	
4.	Storm Water Drains	Yes	0%	
5.	Landscaping & Tree Planting	Yes	0 %	
6.	Street Lighting	Yes	0 %	
7.	Community Buildings	Yes	0 %	
8.	Treatment and Disposal of Sewage and Sullage Water	Yes	0%	
9.	Solid Waste Management & Disposal	N/A	N/A	
10.	Water Conservation / Rain Water Harvesting	Yes	50 %	
11.	Energy Management	N/A	N/A	
12.	Fire Protection and Fire Safety Requirements	Yes	0 %	
13.	Closed Parking	Yes	0 %	
14.	Open Parking	No	N/A	
15.	Electrical Meter Room, Sub-Station, Receiving Station	Yes	0 %	
16.	Others (Option to Add More)			

VI A. EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT				
		Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	Yes	0 %	
2.	Water Supply	Yes	0 %	
3.	Sewerage Chamber Septic Tank	Yes	0 %	
4.	Drains	Yes	0%	
5.	Parks, Landscaping & Tree Planting	Yes	0 %	
6.	Street Lighting	Yes	0 %	
7.	Disposal of Sewage and Sullage Water	N/A	0%	
8.	Solid Waste Management & Disposal	N/A	N/A	
9.	Energy Management	N/A	N/A	

VII. GEO TAGGED AND DATE PHOTOGRAPH OF THE BLOCKS (EACH BLOCK) OF THE PROJECT			
S. No. (A)	Particulars		
1.	Front Elevation	-	Attached
2.	Rear Elevation	-	Attached
3.	Side Elevation	-	Attached
(B)	Photograph of each floor	-	

VIII.	Financial Progress of the Project	
S. No.	Particulars	Amount (In Rs.)
(1)	(2)	(3)
1.	Project Account No.	**40661165474**
2.	Estimated Cost of the Project including land cost at the start of the Quarter	12,05,52,000/-
3.	Amount received during the Quarter	76,90,472/-
4.	Actual Cost Incurred during the Quarter	2,20,83,000/-
5.	Net amount at end of the Quarter	2,20,83,000/-
6.	Total expenditure on Project **till date**	**14,26,35,000/-**
7.	Cumulative fund collected till the end of Quarter in question	2,40,63,570/-
8.	Cumulative expenditure done till the end of Quarter in question	14,26,35,000/-

IX . DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

X. MISCELLANEOUS		
A	List of Legal Cases (if any)	NO
1.	Case No.	NO
2.	Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	NO
1.	Sale Deed	NO
2.	Agreement for Sale	NO

XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Tarun Kumar

Signature of Promoter

Name: Tarun Kumar

Date : 14/11/23

F. No. - SIA/8(a)/987/2020

STATE LEVEL ENVIRONMENT IMPACT ASSESSMENTAUTHORITY, BIHAR

2nd Floor, Beltron Bhawn
Shastri Nagar
Patna - 800 023
E-mail:- seiaabihar@gmail.com
seiaa.ms.br@gmail.com
Telephone No.:- 0612 - 2281255

Dated:- 24/11/2020

To,

Shri Tarun Kumar,
Director,
M/s Surya Nestbuild Limited,
Surya Signature Building,
Hira Sweet Lane,
Boring Canal Road,
Patna- 800001,
Email:-suryanestbuild11@gmail.com,
Telephone No. - 0612 - 2264150.
Mo No.-9334112572.

Sub: **Proposed Commercial Cum Residential building Project "M/S Surya Nestbuild Limited" at Mauza - Mustafapur, Tehsil - Danapur-cum-Khagaul, District - Patna, State - Bihar, with proposed Built-up Area of 1,03,891.91m^2 in the proposed plot area of 19,675.14 m^2- Environment Clearance regarding.**

Reference: - 1. Online Application - SIA/BR/MIS/135121/2020.

Member Secretary
SEIAA, Bihar

2. Your application dated 06-02-2020 &06-05-2020 (hard copy submission).

3. Minutes of the SEAC meeting held on 27&28 February 2020, 19, 21&22 May 2020, 11&12 June 2020, 06 October 2020.

4. Minutes of the SEIAA meeting held on 30-10-2020.

Sir,

This has reference to your online application for the above proposal ofPropo sed Commercial CumResidential building Project "M/S Surya Nestbuild Limited" at Patna, for building construction project at District- Patna.

The details of the project provided by project proponent -

Sl. No.	Item	Details
1.	Name of the project	Proposed Commercial CumResidential building Project "Surya Nestbuild Limited" at Mauza - Mustafapur, Tehsil - Danapur-cum-Khagaul, District - Patna, State - Bihar
2.	S. No. in the Schedule of EIA	8(a) {Building & Construction Project}
3.	Total Plot Area of the project	19,675.14 m^2
4.	Proposed total Built-up Area of the project	1,03,891.91m^2
5.	Proposed total Parking Area of the project	26,252.90m^2
6.	Total GreenBelt / Landscape Area of the project	9,141 m^2
7.	Geo-Coordinates of the project	Corner NE -25° 35'48.19" N 85° 02'43.59" ECorner NW- 25° 35'50.70" N 85° 02'37.32" ECorner SE - 25° 35'46.09" N 85° 02'43.01" ECorner SW- 25° 35' 46.92" N 85° 02' 36.54" E
8.	Location of the Project	Plot No.:-432, 434, 435, 442,446,445,439, 448, 464, 467, 466, 453,454,455,460, 461, 489, 463, 465, 449, 441, Khata No.- 167, 178, 181, 182, 187, 197 Mauza:-Mustafapur, Tehsil:- Danapur-cum-Khagaul, District:- Patna, State:- Bihar.
9.	New / Expansion / Modernization	New
10.	Proposed Occupancy of Residential Building	3,672 persons
11.	Visitors @15%	551 persons.
12.	Maximum height of Building	42.85 Meters.
13.	Proposed STP Capacity	STP - 450 KLD

Member Secretary
SEIAA, Bihar

14.	Municipal Solid waste Generation	**Operational phase** 1,763Kg/day [Solid waste includes paper, card board, plastic cans etc. and kitchen wastes from houses. Recyclable wastes like card boards and plastic cans will be sold to vendors. (@ 0.15 to 0.36 Kg per capita)].
15.	Total Power Requirement	2,890 KW (28.9 KW Energy i.e. 1% of total Energy generated by solar panels)
16.	Source of Power supply	Bihar State Electricity Board.
17.	D.G. Set Back up	03 Nos. of DG sets. (2 x 1,000 KVA and 1 x 400 KVA DG sets will be installed)
18.	Total Rain Water Harvesting Potential	7,765 m^3
19.	Total No. of Rain water harvesting pitsproposed	04 Nos.
20.	Total Water Requirement	677 KLD (338KLD Fresh Water through Bore-wells &239 KLD STP treated water) **Source:** - Ground water supply.
21.	Estimated project Cost	Total Project Cost - `1,33,00,00,000/- (approx.) Environment Management cost - `22,00,000/- (Recurring cost) Environment Management cost - `97,00,000/- (One Time Installation Cost)

PREMISES OF THE ENVIRONMENTAL CLEARANCE

This Environmental Clearance is being issued on the premises which have been substantiated/described in detail in the format of application along with enclosed affidavits/certificates/undertakings etc. furnished therewith by the project proponent:-

(i) Information provided, descriptions mentioned are complete, true and actual and no relevant fact has been concealed to obtain Environmental Clearance deceitfully by the project proponent.

Member Secretary
SEIAA, Bihar

(ii) Environmental Clearance shall be liable to be revoked if furnished information, provided description /Certificates/Affidavits/Undertaking etc. are found false/ concocted at any stage of its validity.

(iii) Project Proponent shall intimate SEIAA immediately if there is any change in their official address / E-mail / Ph. No / Cell. no etc failing which communication sent to them on old address shall be considered as delivered.

(iv) This Environmental Clearance is issued without affecting any court order / statutory other institutions as well as relevant other laws enactment by Ministry of Environment, Forest &Climate Change, Government of India, New Delhi.

I. Statutory compliance:

1. The project proponent shall obtain all necessary clearance/ permission from all relevantagencies including town planning authority before commencement of work. All theconstruction shall be done in accordance with the local building byelaws.

2. The Project proponent will obtain CTE from the BSPCB before preparing site for construction if applicable and CTO before giving occupancy.

3. The approval of the Competent Authority shall be obtained for structural safety ofbuildings due to earthquakes, adequacy of firefighting equipment etc. as per NationalBuilding Code including protection measures from lightening etc.

4. All directions of the Airport Authority, Director of Explosives and Fire Department etc. shall be complied with.

5. The project proponent shall obtain Consent to Establish / Operate under the provisions ofAir (Prevention & Control of Pollution) Act, 1981 and the Water (Prevention & Controlof Pollution) Act, 1974 from the concerned State Pollution Control Board/ Committee.

6. The project proponent shall obtain the necessary permission for drawl of ground water /surface water required for the project from the competent authority.

7. A certificate of adequacy of available power from the agency supplying power to theproject along with the load allowed for the project should be obtained.

Member Secretary
SEIAA, Bihar

8. All other statutory clearances such as the approvals for storage of diesel from ChiefController of Explosives, Fire Department, Civil Aviation Department shall be obtained, as applicable, by project proponents from the respective competent authorities.

9. The provisions of the Solid Waste (Management) Rules, 2016, e- Waste (Management)Rules, 2016, and the Plastics Waste (Management) Rules, 2016 shall be followed.

10. The project proponent shall follow the ECBC/ECBC-R prescribed by Bureau of EnergyEfficiency, Ministry of Power strictly.

11. The facilities provided for collection, segregation, handling, on site storage &processing of solid waste such as chute system for multi-storey buildings, wet& dry bins, collection center& mechanical composter etc. shall be properlymaintained. The collected solid waste shall be segregated at site. Therecyclable solid waste shall be sold out to the authorized vendors for which awritten tie-up must be done with the authorized recyclers.

12. Hazardous waste/E-waste should be disposed off as per Rules applicable and with the necessary approval of the Bihar State Pollution Control Board.

13. Solar power plant or other solar energy related equipment's shall be operated and maintained properly.

14. Provisions shall be made for the integration of solar water heating system.

15. EC conditions applicable for construction and operation phase which are in the interest of public at large must be displayed at prominent place which can be easily accessible to public along with address and contact number of authority to whom violation of EC conditions can be reported.

Project site shall be adequately barricaded before the start of construction activity by erecting suitable windscreen upto. 1/3rd of the building height or 10 meters height whichever is more to prevent dispersion of particulate matter from the construction site.

16. Free Parking facility for visitors shall be provided within the project premises to avoid congestions on public road.

Member Secretary
SEIAA, Bihar

17. Construction of appropriate civil structure and creation of other facilities shall be undertaken to provide benefit of persons suffering from disability in accordance with Hon'ble Supreme Court of India order dated 15th December 2017 in Writ Petition (Civil) 292 of 2006 with WP (Civil) 997 of 2013 (Disabled Rights Grout & Anr. Vs Union of India &Ors).

II. Air quality monitoring and preservation

1. Notification GSR 94(E) dated 25.01.2018 of MoEF&CC regarding Mandatory Implementation of Dust Mitigation Measures for Construction and Demolition Activitiesfor projects requiring Environmental Clearance shall be complied with.

2. Project site shall be adequately barricaded before the start of construction activity by erecting suitable windscreen upto. 1/3rd d of the building height or upto 10 meters height whichever is more to prevent dispersion of particulate matter from the construction site' Dust, smoke & other air pollution prevention measures shall be provided for the building as well as the site. Plastic / tarpaulin sheet covers shall be provided for vehicles bringing all loose construction material e.g sand, cement, muffam and other construction materials prone to causing dust pollution at the site as well as taking out debris from the site.

3. A management plan shall be drawn up and implemented to contain the current exceedance in ambient air quality at the site.

4. Diesel power generating sets proposed as source of backup power should be of enclosedtype and conform to rules made under the Environment (Protection) Act, 1986. Theheight of stack of DG sets should be equal to the height needed for the combined capacityof all proposed DG sets. Diesel to be used should have lower in sulphur content. The location of the DG sets may bedecided with in consultation with State Pollution Control Board.

5. Dust,smoke & other air pollution prevention measures shall be provided for the building aswell as the site. Plastic/tarpaulin sheet covers shall be provided for vehicles bringing all lose construction material e.g sand, cement, murram and other construction materials prone to causing dust pollution at the site aswell as taking out debris from the site.

6. All loose construction material e.g sand, soil, cement, stored on site shall be covered adequately so as toprevent dust pollution.

7. Wet jet shall be provided for grinding and stone cutting.

8. Unpaved surfaces and loose soil shall be adequately sprinkled with water to suppressdust.

9. All construction and demolition debris shall be stored at the site (and not dumped on theroads or open spaces outside) before they are properly disposed. All demolition andconstruction waste shall be managed as per the provisions of the Construction andDemolition Waste Rules 2016.

10. The diesel generator sets to be used during construction phase shall be low sulphur dieseltype and shall conform to Environmental (Protection) prescribed for air and noise mission standards.

11. The gaseous emissions from DG set shall be dispersed through adequate stack height asper CPCB standards. Acoustic enclosure shall be provided to the DG sets to mitigate thenoise pollution. Low sulphur diesel shall be used. The location of the DG set and exhaustpipe height shall be as per the provisions of the Central Pollution Control Board (CPCB)norms.

12. For indoor air quality the ventilation provisions as per National Building Code of India shall be implemented.

III. Water quality monitoring and preservation:

1. The natural drain system should be maintained for ensuring unrestricted flow of water.No construction shall be allowed to obstruct the natural drainage through the site, onwetland and water bodies. Check dams, bio-swales, landscape, and other sustainableurban drainage systems (SUDS) are allowed for maintaining the drainage pattern and toharvest rain water.

2. Buildings shall be designed to follow the natural topography as much as possible.Minimum cutting and filling should be done.

Member Secretary
SEIAA, Bihar

3. Total fresh water use shall not exceed the proposed requirement as provided in the projectdetails.

4. The quantity of fresh water usage, water recycling and rainwater harvesting shall bemeasured and recorded to monitor the water balance as projected by the projectproponent. The record shall be submitted to the, SEIAA/ Regional Office, MoEF&CC along with six monthly Monitoring reports.

5. A certificate shall be obtained from the local body supplying water, specifying the totalannual water availability with the local authority, the quantity of water alreadycommitted, the quantity of water allotted to the project under consideration and thebalance water available. This should be specified separately for ground water and surfacewater sources, ensuring that there is no impact on other users.

6. At least 20% of the open spaces as required by the local building bye-laws shall bepervious. Use of Grass pavers, paver blocks with at least 50% opening, landscape etc.would be considered as pervious surface.

7. Installation of dual pipe plumbing for supplying fresh water for drinking, cooking andbathing etc. and other for supply of recycled water for flushing, landscape irrigation, carwashing, thermal cooling, conditioning etc. shall be done.

8. Use of water saving devices/ fixtures (viz. low flow flushing systems; use of low flowfaucets tap aerators etc.) for water conservation shall be incorporated in the building plan.

9. Separation of grey and black water should be done by the use of dual plumbing system.In case of single stack system separate recirculation lines for flushing by giving dualplumbing system be done.

10. Water demand during construction should be reduced by use of pre-mixed concrete;curing agents and other best practices referred.

11. The local bye-law provisions on rain water harvesting should be followed. If local byelawprovision is not available, adequate provision for storage and recharge should befollowed as per the Ministry of Urban Development Model Building Byelaws, 2016.

Member Secretary
SEIAA, Bihar

Rainwater harvesting recharge pits/storage tanks shall be provided for ground waterrecharging as per the CGWB norms.

12. A rain water harvesting plan needs to be designed where the recharge bores of minimumone recharge bore per 5,000 square meters of built up area and storage capacity ofminimum one day of total fresh water requirement shall be provided. In areas whereground water recharge is not feasible, the rain water should be harvested and stored forreuse. The ground water shall not be withdrawn without approval from the CompetentAuthority.

13. All recharge should be limited to shallow aquifer.

14. No ground water shall be used during construction phase of the project.

15. Any ground water dewatering should be properly managed and shall conform to theapprovals and the guidelines of the CGWA in the matter. Formal approval shall be takenfrom the CGWA for any ground water abstraction or dewatering.

16. The quantity of fresh water usage, water recycling and rainwater harvesting shall bemeasured and recorded to monitor the water balance as projected by the projectproponent. The record shall be submitted to the Regional Office, MoEF&CC along withsix monthly Monitoring reports.

17. Sewage shall be treated in the STP with tertiary treatment. The treated effluent from STPshall be recycled/re-used for flushing, AC make up water and gardening. As proposed, notreated water shall be disposed in to municipal drain.

18. No sewage or untreated effluent water would be discharged through storm water drains.

19. Onsite sewage treatment of capacity of treating 100% waste water to be installed. Theinstallation of the Sewage Treatment Plant (STP) shall be certified by an independentexpert and a report in this regard shall be submitted to the Ministry before the project iscommissioned for operation. Treated waste water shall be reused on site for landscape,flushing, cooling tower, and other end-uses. Excess treated water shall be discharged asper statutory norms notified by Ministry of Environment, Forest and Climate Change.Natural treatment systems shall be promoted.

Member Secretary
SEIAA, Bihar

20. Periodical monitoring of water quality of treated sewage shall be conducted. Necessary measures should be made to mitigate the odour problem from STP.

21. Sludge from the onsite sewage treatment, including septic tanks, shall be collected,conveyed and disposed as per the Ministry of Urban Development, Central Public Healthand Environmental Engineering Organization (CPHEEO) Manual on Sewerage andSewage Treatment Systems, 2013.

22. Separate drainage system shall be developed for storm water so that end point discharge to nearest nallah / river is ensured to avoid water logging without any increase in the pollution load in receiving system.

23. Possibilities needs to be explored to use STP waste water during construction phase. Fresh water shall be used only after exhausting the possibility of obtaining STP waste water located in municipal jurisdiction

IV. Noise monitoring and prevention:

1. Ambient noise levels shall conform to residential area silence zone both during day and night as per Noise Pollution (Control andRegulation) Rules, 2000. Incremental pollution loads on the ambient air and noise qualityshall be closely monitored during construction phase. Adequate measures shall be madeto reduce ambient air and noise level during construction phase, so as to conform to thestipulated standards by CPCB / SPCB.

2. Noise level survey shall be carried as per the prescribed guidelines and report in thisregard shall be submitted to Regional Officer of the Ministry as a part of six-monthlycompliance report.

3. Acoustic enclosures for DG sets, noise barriers for ground-run bays, ear plugs foroperating personnel shall be implemented as mitigation measures for noise impact due toground sources.

V. Energy Conservation measures:

Member Secretary
SEIAA, Bihar

1. Compliance with the Energy Conservation Building Code (ECBC) of Bureau of EnergyEfficiency shall be ensured. Buildings in the States which have notified the ir own ECBC,shall comply with the State ECBC.

2. Outdoor and common area lighting shall be LED.

3. Concept of passive solar design that minimize energy consumption in buildings by usingdesign elements, such as building orientation, landscaping, efficient building envelope,appropriate fenestration, increased day lighting design and thermal mass etc. shall beincorporated in the building design. Wall, window, and roof u-values shall be as perECBC specifications.

4. Energy conservation measures like installation of CFLs/ LED for the lighting the areaoutside the building should be integral part of the project design and should be in placebefore project commissioning.

5. Solar, wind or other Renewable Energy shall be installed to meet electricity generationequivalent to 1% of the demand load or as per the state level/ local building bye-lawsrequirement, whichever is higher.

6. Solar power shall be used for lighting in the apartment to reduce the power load on grid.Separate electric meter shall be installed for solar power. Solar water heating shall beprovided to meet 20% of the hot water demand of the commercial and institutionalbuilding or as per the requirement of the local building bye-laws, whichever is higher.Residential buildings are also recommended to meet its hot water demand from solarwater heaters, as far as possible.

VI. Waste Management:

1. A certificate from the competent authority handling municipal solid wastes, indicating theexisting civic capacities of handling and their adequacy to cater to the M.S.W. generatedfrom project shall be obtained.

2. Proper composting / vermi-composting of municipal and biodegradable solid wastes shall be carried out. All municipal solid wastes shall be segregated, collected, transported,

Member Secretary
SEIAA, Bihar

File No. - **34/1492/2021**

प्रपत्र-ङ

औपबंधिक अग्नि निवारण एवं अग्नि सुरक्षा अनापत्ति प्रमाण पत्र

बिहार अग्निशमन सेवा अधिनियम, 2014 की धारा–02 की उपधारा–(छ) के अधीन
बिहार अग्निशमन सेवा नियमावली, 2021 के नियम 15 (च)(iii) के अन्तर्गत)

निदेशक, राज्य अग्निशमन सेवा, बिहार, पटना का कार्यालय।

सेवा में,

श्री तरूण कुमार,
पिता–स्व0 जगदिश प्रसाद
बोरिंग कैनाल रोड, पटना।

प्रेषक,

निदेशक,
राज्य अग्निशमन सेवा,
बिहार, पटना ।

संदर्भ :- क्रमांक..2692..... दिनांक..29/11/2021..
आवेदनकर्त्ता मे0 **अभियंता पंकज कुमार कर्ण** (विशिष्ट आई.डी.नं0 **ENGR/06/2015/NPDN**)

विषय :- भवन निर्माण के लिए औपबंधिक अनापत्ति प्रमाण पत्र निर्गत ।

महाशय,

राज्य अग्निशमन सेवा, बिहार, पटना के द्वारा गठित अग्नि सुरक्षा एवं निवारण स्कंध (FSPW) की संतुष्टि के उपरान्त व उक्त समिति में शामिल विशेषज्ञों की अनुशंसा के आलोक में भवन निर्माणकर्त्ता मे0 **उषा सिन्हा एवं अन्य** के द्वारा प्रस्तावित भवन/ब्लॉक का निर्माण हेतु बिहार अग्निशमन सेवा नियममावली, 2021 के नियम 15 (च) (iii) के अंतर्गत औपबंधिक अनापत्ति प्रमाण पत्र निर्गत किया जाता है ।

प्रस्तावित भवन योजना से संबंधित भवन का नाम **Surya Nesbuild Limited, निदेशक–श्री तरूण कुमार, पिता–स्व0 जगदिश प्रसाद, प्लॉट नं0–430,432,435,439,440,441,442,443,444,445,446,447, 448, 449,450,451,452,453,454,455,460,461,462,463,464,468,489,494, खाता नं0–167,1777,178,181,182, 188,189,196,197,204,205,206,207, थाना नं0–36, थाना–दानापुर, मौजा–मुस्तफापुर, जिला–पटना** अधिभोग **आवासीय–सह–व्यवसायीक** उप श्रेणी ..... भवन की ऊँचाई **44.95** (मीटर में) फर्श क्षेत्र **68826.40** वर्गमीटर, भवन के तलों की संख्या **14**, तलघर की संख्या **2**, स्लिट/भूतल की संख्या **1**, भवन के ब्लॉक की संख्या **4**, प्रत्येक मंजिल का औसत अधिभोग भार **282**, लिफ्ट की संख्या **17**, फायर लिफ्ट की संख्या **2**, रैम्प की संख्या **2**, आपातकालीन शरण स्थल (रिफ्यूजी एरिया) की संख्या **1**, फायर टावर की संख्या ..... है। राष्ट्रीय भवन संहिता के दिशा-निर्देश, स्थानीय भवन नियमावली एवं स्थानीय परिस्थिति के आधार पर निम्नलिखित सलाह/अनुशंसा के साथ भवन निर्माण योजना की स्वीकृति दी जाती है, जिसका अनुपालन संबंधित वास्तुविद/भवन निर्माणकर्त्ता/भू-स्वामी के द्वारा किया जाएगा।

भवन योजना पर प्रतिहस्ताक्षर के बाद आपके अनुमोदन हेतु अग्रसारित किया जाता है :-

(1) भवन निर्माणकर्त्ता द्वारा भवन के लिए खुली जगह (मीटर) (उत्तर **9.04 मी0**, दक्षिण **9.03 मी0**, पूर्व **17.04 मी0**, पश्चिम **9.05 मी0**) एवं पलायन के साधन (आंतरिक सीढ़ियों की संख्या **6**, चौड़ाई **1.37** (मीटर)/बाह्य सीढ़ियों की संख्या **6**, चौड़ाई **1.37** (मीटर) प्रस्तावित किया गया है ।

(2) खुला स्थान एवं पहुँच–

(क) भवन के चारो तरफ तत्समय प्रवृत भवन उपविधि एवं अन्य तत्संबंधी अधिनियम/नियम/विनियमन/स्थानीय आवश्यकता के अनुसार खुला स्थान होगा एवं अग्निशमन दस्ते के पहुँच एवं घुमाने के लिए न्यूनतम 3.60 मीटर जगह (भवन श्रेणी एवं निर्माण के अनुसार परिवर्तनीय) छोड़ा जाना चाहिए ।

(ख) भवन का पहुँच पथ मजबूत एवं चौड़ी हो जो 20 मिट्रिक टन अग्निशामक वाहन का भार आसानी से सहन कर सके।

(ग) भवन के प्रवेश द्वार की चौड़ाई 4.5 मीटर एवं ऊँचाई 5 मीटर से कम नहीं होना चाहिए।

(3) बनावट :-

(ख) भवन का फर्श क्षेत्र 750 वर्गमीटर से अधिक होने की स्थिति में अलग-अलग दिवारों से उचित रूप से छत तक बॉटा जाएगा, जिसमें कम से कम दो घंटे तक अग्नि प्रतिरोधक क्षमता होगा ।

(ग) भवन की आंतरिक सजावट अग्नि फैलाव निरोधक सामग्री से बना हुआ आई0एस0 गुण स्तर का होगा।

(घ) भवन के केन्द्रीय कोर डक्ट का बतवूद के पास वेन्टीलेशन का प्रावधान होगा । सभी उर्ध्व डक्ट का सीढ़ी पर्याप्त अग्नि निरोधक क्षमता के सामग्री से करने का व्यवस्था करना होगा ।

(4) सीढ़ी :-

(क) भवन का सीढ़ी बंद प्रकार का होगा। पूरे भवन निर्माण कार्य ईट/आर.सी.सी. से न्यूनतम 04 घंटे के अग्नि प्रतिरोधक क्षमता का होगा।

(ख) भवन का सीढ़ी के उपरी भाग में स्थायी भेन्ट होगा जो सीढ़ी के क्रॉस सेक्शन एरिया का 05 प्रतिशत होगा। साथ ही सीढ़ी के क्रॉस सेक्शन क्षेत्र का 15 प्रतिशत क्षेत्र के बराबर प्रत्येक मंजिल के स्तर पर खुलने योग्य Sashes होगा। यह भवन के बाहरी दीवार पर प्रदान किया जाएगा।

(ग) भवन के सभी सीढ़ियों का निर्माण कमरे से अलग होगा एवं किसी भी कमरे में प्रवेश किये बिना हर मंजिल पर एक दूसरे से परगम्य होगा, जिसे संबंधित छत के लेवल तक बढ़ाया जाएगा। सीढ़ी वाली दीवाल की छत आस-पास की छत के क्षेत्र से 1 मीटर ऊपर होगी।

(घ) विभिन्न श्रेणी के भवनों में सीढ़ी की चौड़ाई तथा कोरिडोर एवं यात्रा दूरी संबंधित भवन नियमों के अनुसार होगा ।

(ङ) दो सीढ़ी के मामले में एक सीढ़ी बाहरी दीवाल से होनी चाहिए ।

(च) तलघर तक पहुँच के लिए दोनों सीढ़ी तलघर मंजिल तक नहीं जाना चाहिए। पहुँच के लिए एक अलग सीढ़ी होगा ।

(5) अग्नि सुरक्षा प्रणाली :- राष्ट्रीय भवन संहिता, 2016 **समय-समय पर यथा संशोधित** के प्रावधानों के आलोक में निम्नलिखित अग्नि सुरक्षा उपायों के प्रावधान के साथ अनुमोदित भवन योजना अग्रसारित किया जाता है:-

(क) होज रील
(ख) वेट राईजर-सह-डाउन कमर सिस्टम (12 अदद्)
(ग) यार्ड हाईड्रेन्ट सिस्टम
(घ) हस्तचालित विद्युत अग्नि एलार्म सिस्टम
(ङ) पूरे भवन में ऑटोमेटिक डिटेक्शन एण्ड अलार्म सिस्टम
(च) स्प्रींक्लर सिस्टम (आवश्यकतानुसार)
(छ) भूतल स्टैटिक टैक की क्षमता 200000 लीटर
(ज) ओभर हेड वाटर टैक 37150 लीटर क्षमता
(झ) एक पम्प हाउस 650 एल.पी.एम., इलेक्ट्रीक एवं डीजल 650 एल.पी.एम., जॉकी पम्प 650 एल.पी.एम. बूस्टर पम्प
(ञ) फायर एक्सटींग्यूसर

(6) संबंधित अधिनियम/नियम/विनियमन जैसे- बिहार भवन उपविधि, 2014, **समय-समय पर यथा संशोधित** राष्ट्रीय भवन संहिता, 2016, **समय-समय पर यथा संशोधित** बहुमंजिली भवन निर्माण विनियम, 1981, बिहार अग्निशमन सेवा अधिनियम, 2014, बिहार अग्निशमन सेवा नियमावली, 2021 में संबंधित अधिभोग के लिए वांछित अन्य शर्तो का पालन किया जाएगाा । कुछ शर्ते निम्न प्रकार हैं :-

(क) **लिफ्ट :-**

(i) भवन का लिफ्ट की दीवार न्यूनतम 02 घंटे का अग्नि निरोधक क्षमता का होगा।

(ii) भवन का लिफ्ट उच्च गति ''फायर लिफ्ट'' पर डिजाइन की जाएगी और योजना में स्पष्ट रूप से चिन्हित होगा।

(iii) सामान्य विद्युत आपूर्ति की विफलता के मामले में, स्वचालित वैकल्पिक व्यवस्था होना चाहिए। अपार्टमेंट भवनों के लिए विद्युत आपूर्ति में परिवर्तन हेतु हस्ताचालित परिवर्तनीय स्वीच के माध्यम से यह व्यवस्था किया जा सकता है। वैकल्पिक रूप से लिफ्ट इस तरह से वायर्ड होगा कि बिजली की विफलता की स्थिति में भी यह जमीन स्तर तक आयेगा एवं दरवाजा आसानी से खुल सकेगा।

(iv) आग लगने की स्थिति में प्रति घंटा 30 बार हवा परिवर्तन करने हेतु स्मोक वेंटिंग सिस्टम का समावेश सभी लिफ्ट सॉफ्ट में कर धुँआ निकासी हेतु व्यवस्था की जाएगी। यह इस प्रकार का डिजाइन किया जाएगा कि स्प्रींक्लर एवं फायर एलार्म क्रियाशील हो सके। सामान्य विद्युत आपूर्ति की विफलता के मामले में यह स्वचालित रूप से वैकल्पिक आपूर्ति के लिए कार्य करेगा।

(v) अग्नि नियंत्रण कक्ष के साथ लिफ्ट का संचार व्यवस्था बनाये रखने सहित अन्य सभी आवश्यकताएँ आई0 एस0 गुण स्तर के अनुरूप करना होगा, जिसमें भवन के लिफ्ट कार, अग्नि नियंत्रण कक्ष के साथ जुड़ी होनी चाहिए, जिससे संचार व्यवस्था बनी रहे।

(vi) राष्ट्रीय भवन संहिता, 2016 **समय-समय पर यथा संशोधित** से संबंधित प्रावधानों का पालन करते हुए फायर लिफ्ट होना चाहिए जैसे 1200 वर्गमीटर के फर्श क्षेत्र के लिए एक फायर लिफ्ट होना चाहिए।

(ख) भवन में सक्रिय अग्नि सुरक्षा प्रणाली जैसे प्रत्येक मंजिल पर लैण्डिग भल्व के साथ डाउन कमर सिस्टम एवं होज रील, छत स्तर पर 900 एल0पी0एम0 पम्प के साथ होगा। आई0 एस0 2190/1992 तथा संबंधित विशिष्टियों का आई0एस0आई0 मार्कड अग्निशमन यंत्र, फायर चेक दरवाजा, हस्तचालित कॉल अलार्म प्वाईन्ट, अग्नि सुरक्षा चमकीला संकेत एवं भवन निर्माण संहिता के अनुसार अन्य अग्नि निरोध उपाय किये जायेंगे।

(ग) तलघर में स्वचालित स्प्रींक्लर सिस्टम होना चाहिए एवं दो अलग-अलग निकास द्वार होना चाहिए।

(घ) भूतल जल स्टैटिक टैंक (20,000 लीटर से कम क्षमता का नहीं) स्वचालित रिफिलिंग की व्यवस्था के साथ हो, जहाँ अग्निशामक वाहन आसानी से पहुँच सके। ओभर हेड वाटर स्टैटिक टैंक (10,000 लीटर क्षमता से कम नहीं) अधिवास के पूर्व हो जाना चाहिए ।

(ङ) भवन के प्रत्येक मंजिल पर विद्युत केबुल सील होनी चाहिए ।

(च) भवन का कम्पार्टमेन्टेशन इस प्रकार होगा कि आग एवं धुँआ उसी क्षेत्र में सीमित रहेगा जहाँ अग्निकांड हुआ है तथा भवन के अन्य भागों में नहीं फैले ।

(छ) भवन के अलगाव दीवार एवं फ्लोर में खुला स्थान - ऐसे सभी प्रकार के तथ्यों पर ध्यान देना होगा जो आग एवं धुँआ के फैलाव को इन खुला स्थानों में प्रवेश को सीमित कर सके और बनावट का फायर रेटिंग बरकरार रह सके। सभी दीवार में खुला स्थान न्यूनतम दो घंटे की फायर रेटिंग के अग्नि निरोधक दरवाजा से सुरक्षित रहेगा। मंजिलों में सभी खुला स्थान vertical enclosure से सुरक्षित रहेगा एवं ऐसे enclosure का दीवार न्यूनतम दो घंटे की फायर रेटिंग का होगा ।

(ज) मंजिलों के प्रत्येक vertical openings यथोचित रूप से बंद एवं सुरक्षित रहेगा तथा निम्नलिखित व्यवस्थाएँ की जाएगी :-

(i) पलायन के रास्ता का प्रयोग करते वक्त अधिवासियों को मंजिल दर मंजिल खुले स्थान से आग एवं धुँआ के फैलाव को रोकने के लिए प्रर्याप्त सुरक्षा प्रदान करना होगा। यह सुनिश्चित करना होगा कि अधिवासियों के निकासी मार्ग में कम से कम 21 मिली मीटर का उपरी भाग खुला हो।

(ii) दो घंटें की फायर रेटिंग का अग्नि दरवाजा बाहर भागने/निकलने के रास्ते एवं लिफ्ट में प्रवेश के रास्ते तथा सीढ़ी पर एवं अन्य उपयुक्त स्थानों पर आग एवं धुँआ के फैलाव को रोकने के लिए दिया जाएगा।

(iii) निकासी मार्ग का सुरक्षित प्रयोग हेतु स्मोक वेन्टिंग सुविधा प्रदान किया जाएगा ।

(iv) आंतरिक सजावट से जहरीला धुँआ के उत्पन्न होने से बचाने हेतु धुँआ निरोधी सामग्रियों का प्रयोग किया जाएगा ।

(v) भवन के निकासी मार्ग (सीढ़ी एवं कोरिडोर) का रौशनीकरण/सीढ़ियों का प्रेसराईजेशन/ तलघर का वेन्टीलेशन राष्ट्रीय भवन संहिता, 2016 **समय-समय पर यथा संशोधित** के अनुसार करना होगा ।

(vi) एयर कंडिशनिंग एवं वेंटिलेशन सिस्टम को इस प्रकार अधिष्ठापित किया जाएगा, जिससे आग एवं धुँआ एक फ्लोर से दूसरे फ्लोर और भवन से बाहर नहीं फैल सके। एयर फिल्टर में आग लगने पर धुँआ

को फैलने से बचाने के लिए स्मोक सेन्सिटीव डिवाईस भवन में होना चाहिए। प्रत्येक तल पर आग और धुँए के हजार्ड से बचाने के लिए प्रत्येक तल पर अलग-अलग एयर हैंडलिग यूनिट होना चाहिए। फायर डंपर्स को ए0सी0 सिस्टम में प्रदान किया जाएगा, ताकि आग की स्थिति में स्वचालित रूप से बंद हो सके और इस तरह अग्नि/धुँआ का फैलाव रोका जा सके ।

(vii) **विद्युत अधिष्ठापन**- विद्युत सुरक्षा भारतीय विद्युत नियमावली एवं संबंधित आई0एस0/संहिता के प्रावधान के आलोक में होगा। लाईसेंस विद्युत ठेकेदार के द्वारा विद्युत अधिष्ठापन किया जाएगा। मुख्य रूप से अलग नली में वायरिंग, अलग सर्किट, स्वचालित सर्किट ब्रेकर, मास्टर स्वीच, इंस्पेक्शन पैनल दरवाजा, आपातकालीन/वैकल्पिक विद्युत आपूर्ति का आवधिक सत्यापन आदि पर ध्यान दिया जाएगा ।

(viii) भवन का अधिवास प्राप्त करने के बाद प्रत्येक वर्ष कम से कम दो बार नियमित रूप से फायर एक्जीट ड्रिल किया जाना चाहिए ।

(ix) अग्नि सुरक्षा अधिकारी- एन0बी0सी0 2016 और बिहार अग्निशमन सेवा अधिनियम, 2014 के अनुसार।

(x) भवन में अधिष्ठापित अग्निशमन उपकरणों आदि का ए0एम0सी0 योग्य फर्म या व्यक्ति को दिया जाना चाहिए।

(xi) स्थापित नियम के आलोक में भवन के सेट बैक का चेकिंग वास्तुविद/पारित करने वाले द्वारा किया जाएगा।

(xii) यह स्पष्ट किया जाता है कि उपरोक्त सिफारिशों का पालन नहीं करने की स्थिति में भविष्य में होने वाली किसी भी कानूनी विवाद के मामले मे, जिम्मेवारी डेवलपर्स/वास्तुविद/जमीन मालिक पर होगी एवं किसी भी सरकारी प्राधिकार (जैसे कि राज्य अग्निशमन पदाधिकारी, बिहार, पटना) की नहीं होगी ।

(xiii) इसके द्वारा यह भी स्पष्ट किया जाता है कि इस कार्यालय (अर्थात राज्य अग्निशमन पदाधिकारी-सह-निदेशक, बिहार, पटना/प्राधिकृत पदाधिकारी) का कार्यालय उस भूमि के किसी भी कानूनी विवाद के लिए जिम्मेवार नहीं है, जिसपर प्रस्तावित भवन का निर्माण होगा।

(7) अनिवार्यत: अन्डरटेकिंग्स के सभी प्रावधानों का पालन करना होगा ।

(8) इसे औपबंधिक अनापत्ति प्रमाण पत्र माना जाएगा। उपरोक्त सभी अग्नि एवं जीवन सुरक्षा अनुशंसाओं के अनुपालन के बाद आवश्यक निरीक्षण एवं अधिष्ठापन के जॉच हेतु राज्य अग्निशमन कार्यालय को सूचित करना होगा। सभी बिन्दुओं की जाँच से संतुष्टि के बाद अंतिम अग्नि निवारण एवं अग्नि सुरक्षा अनापत्ति प्रमाण पत्र निर्गत किया जाएगा ।

(9) अनुमोदित भवन योजना में बिना पूर्व स्वीकृति के किसी भी प्रकार का विचलन या परिवर्तन किये जाने की स्थिति में इस औपबंधिक अनापत्ति प्रमाण पत्र को रद्द कर दिया जाएगा।

(10) हस्ताक्षर एवं मुहर के साथ नक्शा वापस किया जाता है/ऑनलाईन निर्गत किया जाता है।

अनुलग्नक

23/11/21

1) मे0 अभियंता पंकज कुमार कर्ण
2) अध्यक्ष नगर निगम, **पटना**

राज्य अग्निशमन पदाधिकारी-सह-निदेशक,
बिहार, पटना ।

(1028/19)

भारतीय विमानपत्तन प्राधिकरण
AIRPORTS AUTHORITY OF INDIA

Tarun Kumar

C/O Surya Nestbuild Ltd, Hari Lal Lane West
Boring Canel Road, Near Boring Road
Chauraha, Patna (Bihar) Pin 800001

Date: 22-10-2019

Valid Upto: 21-10-2027

No Objection Certificate for Height Clearance

1. This NOC is issued by Airports Authority of India (AAI) in pursuance of responsibility conferred by and as per the provisions of Govt. of India (Ministry of Civil Aviation) order GSR751 (E) dated 30th Sep. 2015 for Safe and Regular Aircraft Operations.

2. This office has no objection to the construction of the proposed structure as per the following details:

NOC ID :	**PATN/EAST/B/092819/431663**
Applicant Name*	**Bimal Kumar Srivastava**
Site Address*	**Plot No./Khata No./Thana No.- 430/167/36, 431/178/36, 432/197/36, 434/167/36, 435/181/36, 439/188/36, 440/189/36, 441/167/36, 442/178/36, 443/177/36, 444/197/36, 445/196/36, 446/204/36, 447/204/36, 448/188/36, 449/204/36, 450/204/36, 451/204/36, 452/189/36, 453/167/36454/182/36, 455/206/36, 460/206/36, 461/206/36, 462/207/36, 463/207/36, 464/188/36, 465/189/36, 466/178/36, 467/197/36, 489/188/36, 494/205/36, Saguna Khagaul Main , Patna,Saguna Khagaul Main**
Site Coordinates*	**25 35 48.97N 85 02 35.38E, 25 35 49.64N 85 02 35.39E, 25 35 51.03N 85 02 36.18E, 25 35 46.97N 85 02 36.52E, 25 35 48.61N 85 02 36.74E, 25 35 47.91N 85 02 36.76E, 25 35 50.71N 85 02 37.33E, 25 35 48.16N 85 02 38.38E, 25 35 49.92N 85 02 39.01E, 25 35 46.38N 85 02 40.01E, 25 35 45.28N 85 02 40.79E, 25 35 47.52N 85 02 40.98E, 25 35 48.77N 85 02 42.84E, 25 35 45.93N 85 02 43.13E, 25 35 48.25N 85 02 43.76E**
Site Elevation in mtrs AMSL as submitted by Applicant*	**53.92 M**
Permissible Top Elevation in mtrs Above Mean Sea Level(AMSL)	**96.81 M (Restricted)**

*As provided by applicant

3. This NOC is subject to the terms and conditions as given below:

a. Permissible Top elevation has been issued on the basis of Site coordinates and Site Elevation submitted by Applicant. AAI neither owns the responsibility nor authenticates the correctness of the site coordinates & site elevation provided by the applicant. If at any stage it is established that the actual data is different, this NOC will stand null and void and action will be taken as per law. The office in-charge of the concerned aerodrome may initiate action under the Aircraft (Demolition of Obstruction caused by Buildings and Trees etc.) Rules, 1994"

b. The Site coordinates as provided by the applicant in the NOC application has been plotted on the street view map and satellite map as shown in ANNEXURE. Applicant/Owner to ensure that the plotted coordinates corresponds to his/her site.In case of any discrepancy,Designated Officer shall be requested for cancellation of the NOC.

c. Airport operator or his designated representative may visit the site (with prior coordination with applicant or owner) to ensure that NOC terms & conditions are complied with.

d. The Structure height (including any superstructure) shall be calculated by subtracting the Site elevation in AMSL from the Permissible Top Elevation in AMSL i.e. Maximum Structure Height = Permissible Top Elevation minus (-) Site Elevation.

e. The issue of the 'NOC' is further subject to the provisions of Section 9-A of the Indian Aircraft Act, 1934 and any notifications issued there under from time to time including the Aircraft (Demolition of Obstruction caused by Buildings and Trees etc) Rules,1994.

f. No radio/TV Antenna, lighting arresters, staircase, Mumtee, Overhead water tank and attachments of fixtures of any kind shall project above the Permissible Top Elevation of 96.81 M (Restricted) (AMSL), as indicated in para 2.

g. Use of oil, electric or any other fuel which does not create smoke hazard for flight operations is obligatory, within 8 KM of the Aerodrome Reference Point.

h. The certificate is valid for a period of 8 years from the date of its issue.One time revalidation without assessment may be allowed, provided construction work has commenced,subject to the condition that such request shall be made within the validity period of the NOC and the delay is due to circumstances which are beyond the control of the developer.

i. No light or a combination of lights which by reason of its intensity, configuration or colour may cause confusion with the aeronautical ground lights of the Airport shall be installed at the site at any time, during or after the construction of the building. No activity shall be allowed which may affect the safe operations of flights

j. The applicant will not complain/claim compensation against aircraft noise, vibrations, damages etc. caused by aircraft operations at or in the vicinity of the airport.

k. Day markings & night lighting with secondary power supply shall be provided as per the guidelines specified in chapter 6 and appendix 6 of Civil Aviation Requirement Series B Part I Section 4, available on DGCA India website: www.dgca.nic.in

l. The applicant is responsible to obtain all other statutory clearances from the concerned authorities including the approval of building plans. This NOC for height clearances is to ensure the safe and regular aircraft operations and shall not be used as document for any other purpose/claim whatsoever, including ownership of land etc.

m. This NOCID has been assessed w.r.t Patna Airport(s). NOC has been issued w.r.t. the AAI aerodromes and other licensed civil aerodromes as listed in Schedule-III, Schedule-IV(Part-1), Schedule-IV(Part-2;RCS Airports Only) and Schedule-VII of GSR751(E)

n. Applicant needs to seek separate NOC from Defence, if the site lies within the jurisdiction of Defence Aerodromes as listed in Schedule-V of GSR751(E). As per Rule 13 of GSR751(E), applicants also need to seek NOC from the concerned State Govt. for sites which lies in the jurisdiction of unlicensed aerodromes as listed in Schedule-IV (Part-2:other than RCS airports) of GSR751(E) .

o. In case of any discrepancy/interpretation of NOC letter, English version shall be valid.

p. In case of any dispute w.r.t site elevation and/or AGL height, top elevation in AMSL shall prevail.

महा प्रबंधक (वायानी) पू.क्षे.
~~General Manager(ATM),ER~~
भा.वि.प्रा. / A.A.I.
ने.सु.च.बो.अ. हवाई अड्डा/N.S.C.B.I. Airport
कोलकाता/Kolkata 700052

Chairman NOC Committee

Region Name: EAST

Address: General Manager Airports Authority of India, Regional Headquarter, Eastern Region, N.S.C.B.I Airport, Kolkata-700052

Email ID: gmatmer@aai.aero

Contact No: 033-25111293


Name / Designation / Sign with Date	
Prepared By :	22/10/19
Verified By :	Choudhury. 22.10.19.

(1028/19)

Distance From Nearest Airport And Bearing


Airport Name	Distance (Meters) from Nearest ARP	Bearing (Degree) from Nearest ARP
Patna	4686.9	275.21
NOCID	PATN/EAST/B/092819/431663	

Street View

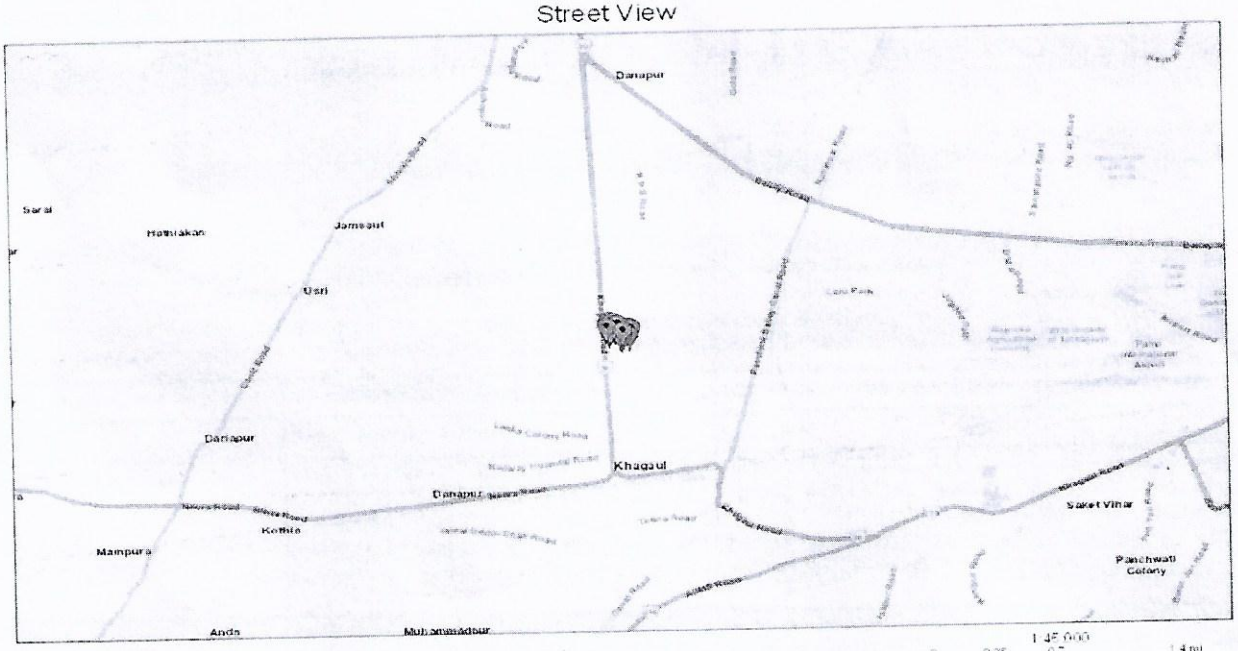

September 28, 2019

Satellite View

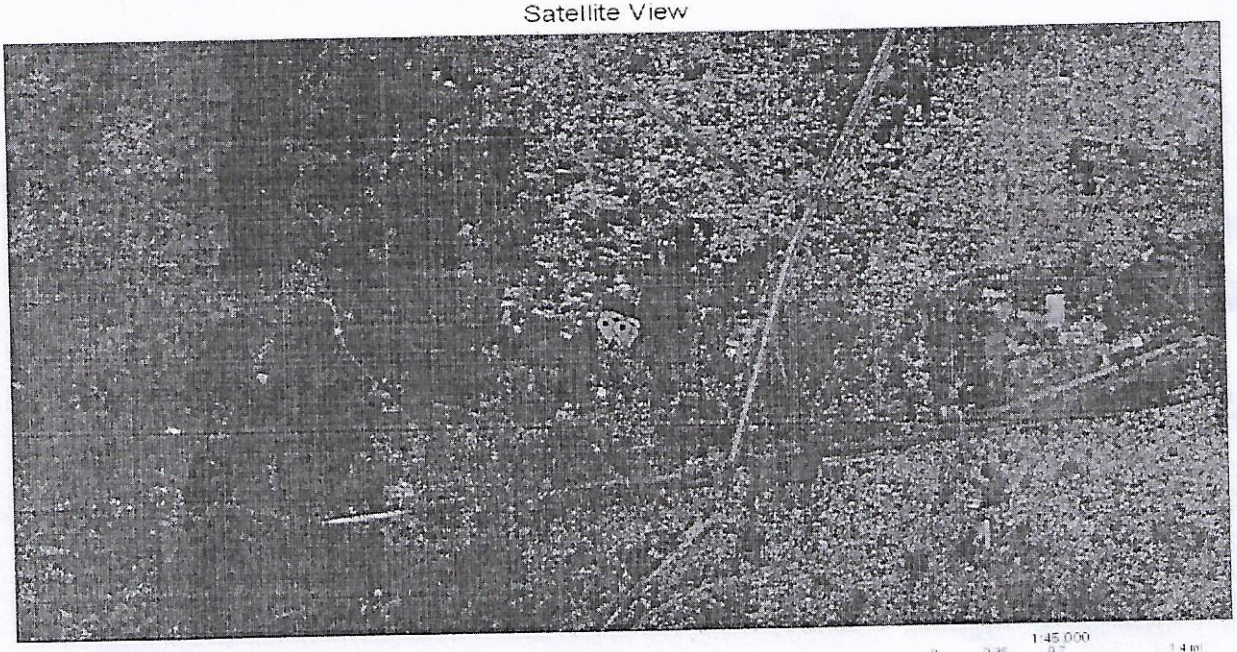

September 28, 2019
