FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending June of 2024 (year)

I. PARTICULARS OF PROMOTERS

Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U45309BR2016PTC031450	Name of Firm	ARANYA ENGICON PVT LTD
Firm Address :	MAHAVIR MARKET, C/O- BRIJI BAHAWAN, PRTHIVIPUR, CHIRAIYATAND, PATNA		
Total Experience of promoter in Real Estate sector	09 YEARS		
Total Experience in Real Estate after Implementation of RERA	07 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	N/A	
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	N/A	

II. PARTICULARS OF PROJECT

Project Registration Number	BRERAP00066-2/148/R-1295/2022	Name of Project/Phase of Registered Project	ARANYA YAMUNA RESIDENCY
Name of Promoter	ARANYA ENGICON PVT LTD	Project Address	BISCUIT FACTORY ROAD, MITHILA COLONY, DANAPUR, PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	02/04/2024		
Starting date of Project or Phase of the Project	14/03/2022		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	3 YEARS (From 02-04-2021 to 01-04-2024)		

ARANYA ENGICON PVT. LTD.

DIRECTOR

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share -	Total Number of Apartments in Landowner's share -
	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.	10 18	6276.10 15503.16	28	1. Booked / Allotted -02 2. Sold-NIL	3. Booked/ Allotted-NIL Sold -NIL
					Percentage of booking	Percentage of booking

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
	28	1. Booked/Allotted -	02
		2. Sold -	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. 02/21-22

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	100%	

ARANYA ENGICON PVT. LTD.

DIRECTOR

2.	Basements (if any)	100%	
3.	Podiums (if any)		
4.	Plinth	100%	
5.	Stilt Floor	100%	
6.	Slabs of Super Structure	100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	50%	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	50%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	20%	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	0%	

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

ARANYA ENGICON PVT. LTD.

DIRECTOR

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yy y) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	35%	
2.	Water Supply	YES	20%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	
4.	Storm Water Drains	YES	0%	
5.	Landscaping & Tree Planting	YES	0%	
6.	Street Lighting	YES	0%	
7.	Community Buildings	NO		
8.	Treatment and Disposal of Sewage and Sullage Water	NO		
9.	Solid Waste Management & Disposal	YES		
10.	Water Conservation / Rain Water Harvesting	YES	0%	
11.	Energy Management	YES	0%	
12.	Fire Protection and Fire Safety Requirements	YES	0%	
13.	Closed Parking	YES	30%	
14.	Open Parking	NO		
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

ARANYA ENGICON PVT. LTD.

DIRECTOR

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX.	GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT		
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

X. FINANCIAL PROGRESS OF THE PROJECT

ARANYA ENGICON PVT. LTD.

DIRECTOR

S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	921020032412503
2.	Estimated Cost of the Project including land cost at the start of the Project	48,80,72,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	3,80,00,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	2,64,500=00
6.	Actual Cost Incurred during the Quarter	2,19,359=00
7.	Net amount at end of the Quarter	2,31,258=70
8.	Total expenditure on Project **till date**	84,89,890=20
9.	Cumulative fund collected till the end of Quarter in question	
10.	Cumulative expenditure done till the end of Quarter in question	

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL

ARANYA ENGICON PVT. LTD.

DIRECTOR

3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

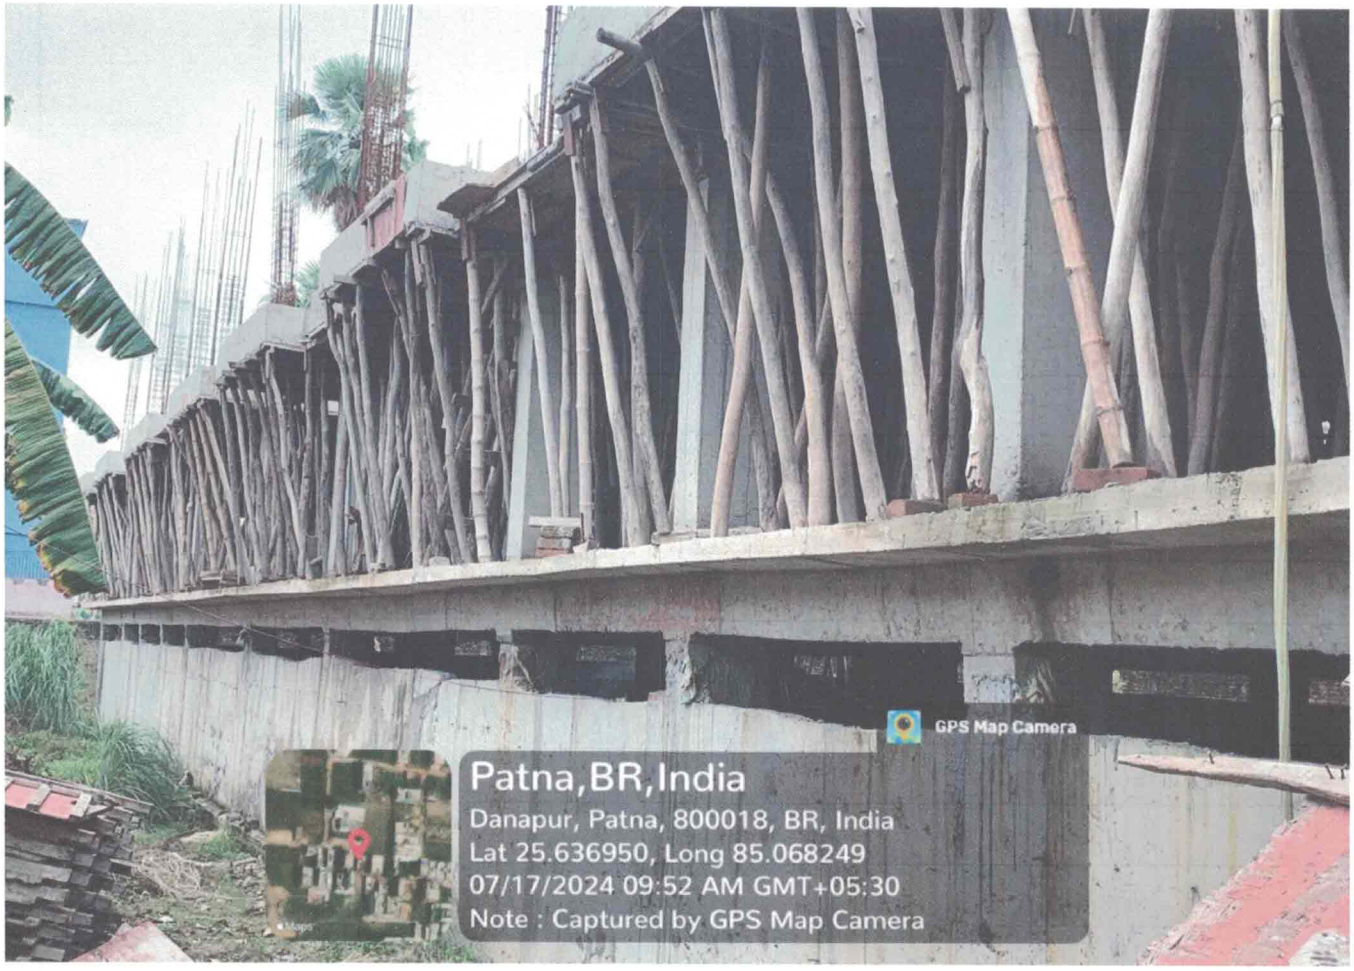
ARANYA ENGICON PVT. LTD.

DIRECTOR

Signature of Promoter

Name:

Date:


GPS Map Camera
Patna,BR,India
Danapur, Patna, 800018, BR, India
Lat 25.636950, Long 85.068249
07/17/2024 09:52 AM GMT+05:30
Note : Captured by GPS Map Camera


GPS Map Camera
Patna,BR,India
Danapur, Patna, 800018, BR, India
Lat 25.637304, Long 85.068333
07/17/2024 09:53 AM GMT+05:30
Note : Captured by GPS Map Camera

Patna,BR,India
GPS Map Camera

GPS Map Camera
Patna,BR,India
Danapur, Patna, 800018, BR, India
Lat 25.636916, Long 85.068320
07/17/2024 09:52 AM GMT+05:30
Note : Captured by GPS Map Camera
