FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U45201BR2012PTC018527	Name of Firm	SAI ASHRAY NIRMAN INDIA PRIVATE LIMITED
Firm Address :	RAJ COMPLEX NEW DAK BUNGLOW ROAD,PO.-GPO. , PATNA, BIHAR, INDIA - 800001		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA	06 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	02	RESIDENTIAL

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP00454-3/1229/R-1065/2020	Name of Project/Phase of Registered Project	SHREE GANESH SARASWATI ENCLAVE
Name of Promoter	SAI ASHRAY NIRMAN INDIA PRIVATE LIMITED	Project Address	BEHIND ST. KAREN'S SCHOOL, GOLA ROAD, PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	10/09/2024		
Starting date of Project or Phase of the Project	24/11/2020		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	09/05/2023		

Subodh kumar verma

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - FLAT-16	Total Number of Apartments in Landowner's share - FLAT-16
	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.	32	29024.00	32	1. Booked / Allotted -NIL 2. Sold-16	3. Booked/ Allotted-NIL Sold -NIL
					Percentage of booking 100%	Percentage of booking 0%

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted -	NIL
	32	2. Sold -	16

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	N/A			
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

Subodh kumar Verma

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. 04/20-21

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)		
2.	Basements (if any)	N/A	
3.	Podiums (if any)	N/A	
4.	Plinth	100%	
5.	Stilt Floor	N/A	
6.	Slabs of Super Structure	100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100% 100% 100% 100%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	100% 100%	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100% 100% 100%	
10.	External plumbing and external plaster, elevation, ompletion of terraces with waterproofing of the Building/Wing.	100% 100% 100% 100%	

Subodh Kumar Verma

11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	100% 100% 100% 100% 100% 100%	

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	100%	
2.	Water Supply	YES	100%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	100%	
4.	Storm Water Drains	YES	100%	
5.	Landscaping & Tree Planting	YES	100%	
6.	Street Lighting	YES	100%	
7.	Community Buildings	NO	N/A	

Subodh Kumar Verma

8.	Treatment and Disposal of Sewage and Sullage Water	YES	100%	
9.	Solid Waste Management & Disposal	YES	100%	
10.	Water Conservation / Rain Water Harvesting	YES	100%	
11.	Energy Management	YES	100%	
12.	Fire Protection and Fire Safety Requirements	YES	100%	
13.	Closed Parking	YES	100%	
14.	Open Parking	NO	N/A	
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	100%	
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			

Subodh kumar verma

8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX.	GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT		
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

X.	FINANCIAL PROGRESS OF THE PROJECT	
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	50524994493
2.	Estimated Cost of the Project including land cost at the start of the Project	6,93,50,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	3,63,50,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	67,50,000=00
6.	Actual Cost Incurred during the Quarter	15,50,000=00
7.	Net amount at end of the Quarter	55,20,825=33
8.	Total expenditure on Project **till date**	8,17,80,029=00
9.	Cumulative fund collected till the end of Quarter in question	
10.	Cumulative expenditure done till the end of Quarter in question	

XI.	DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

Subodh Kumar Verma

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	01
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

XIV UNITS ALLOCATION DETAILS

Total Number of sanctioned apartments 1 BHK- 2 BHK - 3 BHK-32 4 BHK- Shop- Bungalow - Plot etc	Details of allotment made so far with Flat number/ Bungalow - Plot etc		Cancellation of flat allotment, If any with Flat number/ Bungalow – Plot etc
	FLAT NO.	FLAT TYPE	
	101	3BHK	
	102	3BHK	
	103	3BHK	
	104	3BHK	
	105	3BHK	
	106	3BHK	
	107	3BHK	
	108	3BHK	
	201	3BHK	
	202	3BHK	
	204	3BHK	
	204	3BHK	

Subodh Kumar Verma

	206	3BHK	
	207	3BHK	
	208	3BHK	
	304	3BHK	
	306	3BHK	

XV. BROCHURE /Prospectus

XVI Grievance Redressal Officer

Name : SUBODH KUMAR VERMA
Contact No : 9334471514
Email id : subodhverma08@gail.com
Address : RAJ COMPLEX NEW DAK BUNGLOW ROAD,PO.-GPO. PATNA -800001

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Subodh Kumar Verma

Signature of Promoter

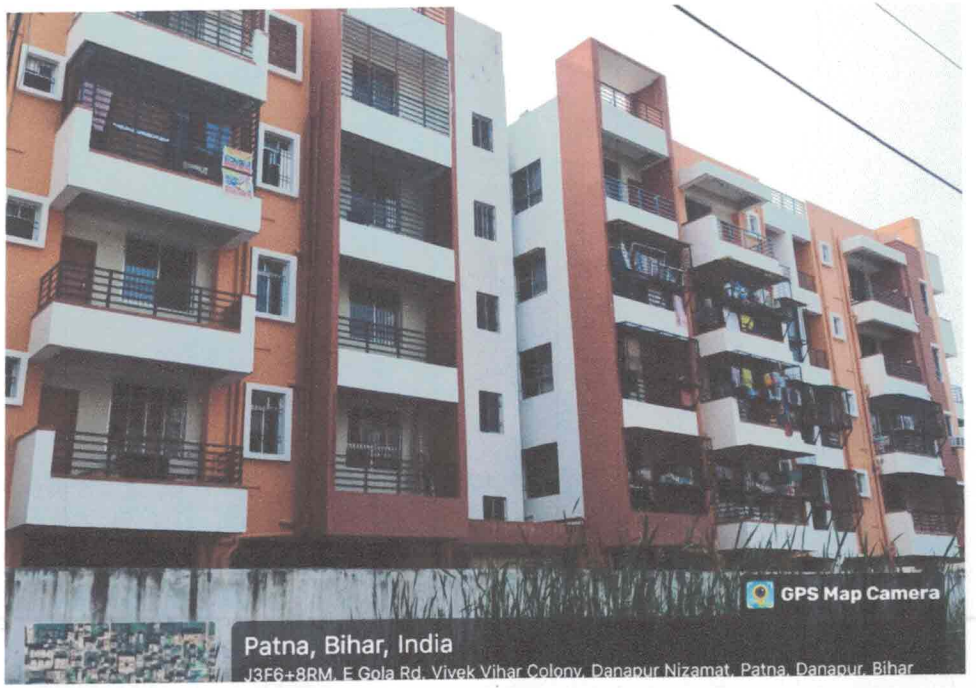
Name:

Date:


SHREE GANESH SARASWATI ENCLAVE
GPS Map Camera
Patna, Bihar, India
J3F6+8RM, E Gola Rd, Vivek Vihar Colony, Danapur Nizamat, Patna, Danapur, Bihar


GPS Map Camera
Patna, Bihar, India
J3F6+8RM, E Gola Rd, Vivek Vihar Colony, Danapur Nizamat, Patna, Danapur, Bihar


GPS Map Camera
Patna, Bihar, India
J3F6+8RM, E Gola Rd, Vivek Vihar Colony, Danapur Nizamat, Patna, Danapur, Bihar


GPS Map Camera
Patna, Bihar, India
J3F6+8RM, E Gola Rd, Vivek Vihar Colony, Danapur Nizamat, Patna, Danapur, Bihar
