PROJECT NAME –METRO CITY

PROMOTER NAME –DIRECT SELL BUILDCON PRIVATE LIMITED

RERA REGISTRATION NO. BRERAP00076-1/908/R-620/2019

QUARTERLY PROGRESS REPORT FOR RERA, BIHAR

Period – APRIL TO JUNE 2024

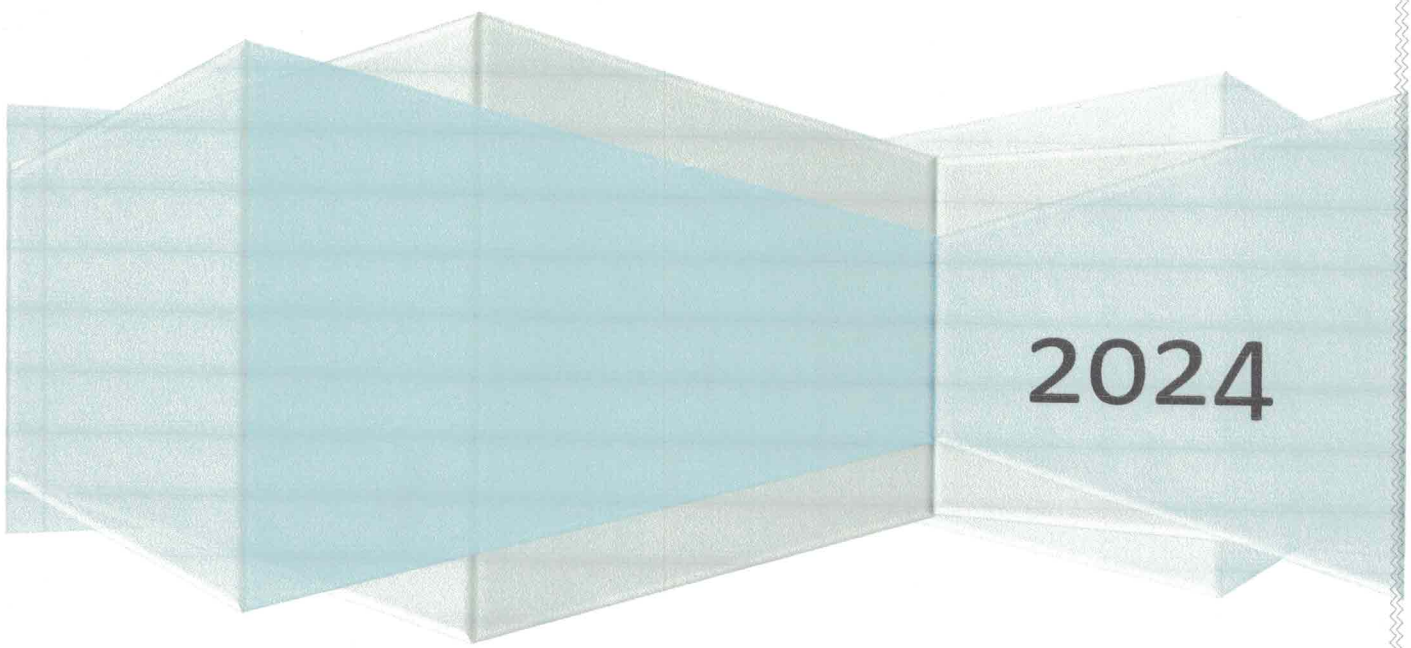

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending June of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U45209BR2017PTC033742	Name of Firm	DIRECT SELL BUILDCON PRIVATE LIMITED
Firm Address :	2ND FLOOR, RAMASHISH MARKET, RUKUNPURA , BAILEY ROAD, PATNA, BIHAR, INDIA - 800014		
Total Experience of promoter in Real Estate sector	07 YEARS		
Total Experience in Real Estate after Implementation of RERA	05 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	02	Residential- cum-Commercial Plotted Project

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP00076-1/908/R-620/2019	Name of Project/Phase of Registered Project	METRO CITY
Name of Promoter	DIRECT SELL BUILDCON PRIVATE LIMITED	Project Address	NH 722 VILLAGE-KARJA, REWA ROAD MUZAFFARPUR BIHAR
Name of Co-promoter	N/A		
Project Registration is valid up to	05/11/2023		
Starting date of Project or Phase of the Project	14/05/2019		
Type of Project or Phase of the Project	Plotted project		
Period of validity of map by the Competent Authority			

Direct Sell Buildcon

Director

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - 1. Booked / Allotted – 2. Sold-	Total Number of Apartments in Landowner's share - 3. Booked/ Allotted- Sold -
	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.				Percentage of booking	Percentage of booking

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
	N/A	1. Booked/Allotted -	
		2. Sold -	

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. _____(To beaded for each Building / Wing)

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	N/A	

Direct Sell Buildcon Pvt. Ltd

Director

2.	Basements (if any)	N/A	
3.	Podiums (if any)	N/A	
4.	Plinth	N/A	
5.	Stilt Floor	N/A	
6.	Slabs of Super Structure	N/A	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	N/A	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	N/A	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	N/A	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	N/A	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	N/A	

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

Direct Sell Buildcon Pvt. Ltd

Director

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths			
2.	Water Supply			
3.	Sewerage (Chamber, Line, Septic Tank, STP)			
4.	Storm Water Drains			
5.	Landscaping & Tree Planting			
6.	Street Lighting			
7.	Community Buildings			
8.	Treatment and Disposal of Sewage and Sullage Water			
9.	Solid Waste Management & Disposal			
10.	Water Conservation / Rain Water Harvesting			
11.	Energy Management			
12.	Fire Protection and Fire Safety Requirements			
13.	Closed Parking			
14.	Open Parking			
15.	Electrical Meter Room, Sub-Station, Receiving Station			
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

Direct Sell Buildcon Pvt. Ltd

Director

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths	YES	95%	
2.	Water Supply	NO		
3.	Sewerage Chambers Septic Tank	NO		
4	Drains	NO		
5.	Parks, Land Scaping and Tree Planting	YES	95%	
6.	Street Lighting	YES	95%	
7.	Disposal of sewage & sullage water	NO		
8.	Water conservation/Rain Water Harvesting	NO		
9.	Energy Management	NO		

IX.	GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT		
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

Direct Sell Buildcon Pvt. Ltd

Director

X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	3734904761
2.	Estimated Cost of the Project including land cost at the start of the Project	
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	
4.	Any Variation in Development Cost which is declared at the start of the Project .	
5.	Amount received during the Quarter	14,30,181=00
6.	Actual Cost Incurred during the Quarter	26,16,726=00
7.	Net amount at end of the Quarter	31,24,224=00
8.	Total expenditure on Project **till date**	
9.	Cumulative fund collected till the end of Quarter in question	
10.	Cumulative expenditure done till the end of Quarter in question	

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO

Direct Sell Buildcon Pvt. Ltd

Director

B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	02
2.	Agreement for Sale	02
3.	No. of possessions given to allottees	
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Direct Sell Buildcon Pvt. Ltd

Director

Signature of Promoter

Name:

Date:
