FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U45209BR2017PTC033742	Name of Firm	DIRECT SELL BUILDCON PRIVATE LIMITED
Firm Address :	2ND FLOOR, RAMASHISH MARKET, RUKUNPURA , BAILEY ROAD, PATNA, BIHAR, INDIA - 800014		
Total Experience of promoter in Real Estate sector	07 YEARS		
Total Experience in Real Estate after Implementation of RERA	05 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	02	Residential- cum-Commercial Plotted Project

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP00076-1/908/R-620/2019	Name of Project/Phase of Registered Project	METRO CITY
Name of Promoter	DIRECT SELL BUILDCON PRIVATE LIMITED	Project Address	NH 722 VILLAGE-KARJA, REWA ROAD MUZAFFARPUR BIHAR
Name of Co-promoter	N/A		
Project Registration is valid up to	05/11/2023		
Starting date of Project or Phase of the Project	14/05/2019		
Type of Project or Phase of the Project	Plotted project		
Period of validity of map by the Competent Authority			

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Direct Sell Buildcon Pvt. Ltd.

Director

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - 1. Booked / Allotted - 2. Sold-	Total Number of Apartments in Landowner's share - 3. Booked/ Allotted- Sold -
	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.	plot			Percentage of booking	Percentage of booking

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
	N/A	1. Booked/Allotted -	
		2. Sold -	

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. _____(To beaded for each Building / Wing)

Anjani Kumar

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	N/A	
2.	Basements (if any)	N/A	
3.	Podiums (if any)	N/A	
4.	Plinth	N/A	
5.	Stilt Floor	N/A	
6.	Slabs of Super Structure	N/A	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	N/A	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	N/A	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	N/A	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	N/A	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale.	N/A	

Direct Sell [illegible] Pvt. Ltd.

Director

	Any other activities		

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths			
2.	Water Supply			
3.	Sewerage (Chamber, Line, Septic Tank, STP)			
4.	Storm Water Drains			
5.	Landscaping & Tree Planting			
6.	Street Lighting			
7.	Community Buildings			
8.	Treatment and Disposal of Sewage and Sullage Water			
9.	Solid Waste Management & Disposal			
10.	Water Conservation / Rain Water Harvesting			
11.	Energy Management			
12.	Fire Protection and Fire Safety Requirements			
13.	Closed Parking			
14.	Open Parking			
15.	Electrical Meter Room, Sub-Station, Receiving Station			

Director

16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT				
		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths	YES	95%	
2.	Water Supply	NO		
3.	Sewerage Chambers Septic Tank	NO		
4	Drains	NO		
5.	Parks, Land Scaping and Tree Planting	YES	95%	
6.	Street Lighting	YES	95%	
7.	Disposal of sewage & sullage water	NO		
8.	Water conservation/Rain Water Harvesting	NO		
9.	Energy Management	NO		

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT			
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

Anjani Kumar

X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	3734904761
2.	Estimated Cost of the Project including land cost at the start of the Project	
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	
4.	Any Variation in Development Cost which is declared at the start of the Project .	
5.	Amount received during the Quarter	36,69,255=00
6.	Actual Cost Incurred during the Quarter	66,47,321=00
7.	Net amount at end of the Quarter	1,46,103=00
8.	Total expenditure on Project **till date**	
9.	Cumulative fund collected till the end of Quarter in question	
10.	Cumulative expenditure done till the end of Quarter in question	

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	03

Director

Director

2.	Agreement for Sale	04
3.	No. of possessions given to allottees	

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

XIV UNITS ALLOCATION DETAILS

Total Number of sanctioned apartments 1 BHK- 2 BHK - 3 BHK- 4 BHK- Shop- Bungalow - Plot etc	Details of allotment made so far with Flat number/ Bungalow - Plot etc	Cancellation of flat allotment, If any with Flat number/ Bungalow – Plot etc

XV. BROCHURE /Prospectus

XVI Grievance Redressal Officer

Name : PRABHAT KUMAR
Contact No : 9234874525
Email id : directsellbuildcon@gmail.com
Address : DIRECT SELL BUILDCON PRIVATE LIMITED,2ND FLOOR,RAMASHISH MARKET,RUKUNPURA,BAILEY ROAD,PATNA

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Anjani Kumar

Signature of Promoter

Name: ANJANI KUMAR

Date: 15/10/2024

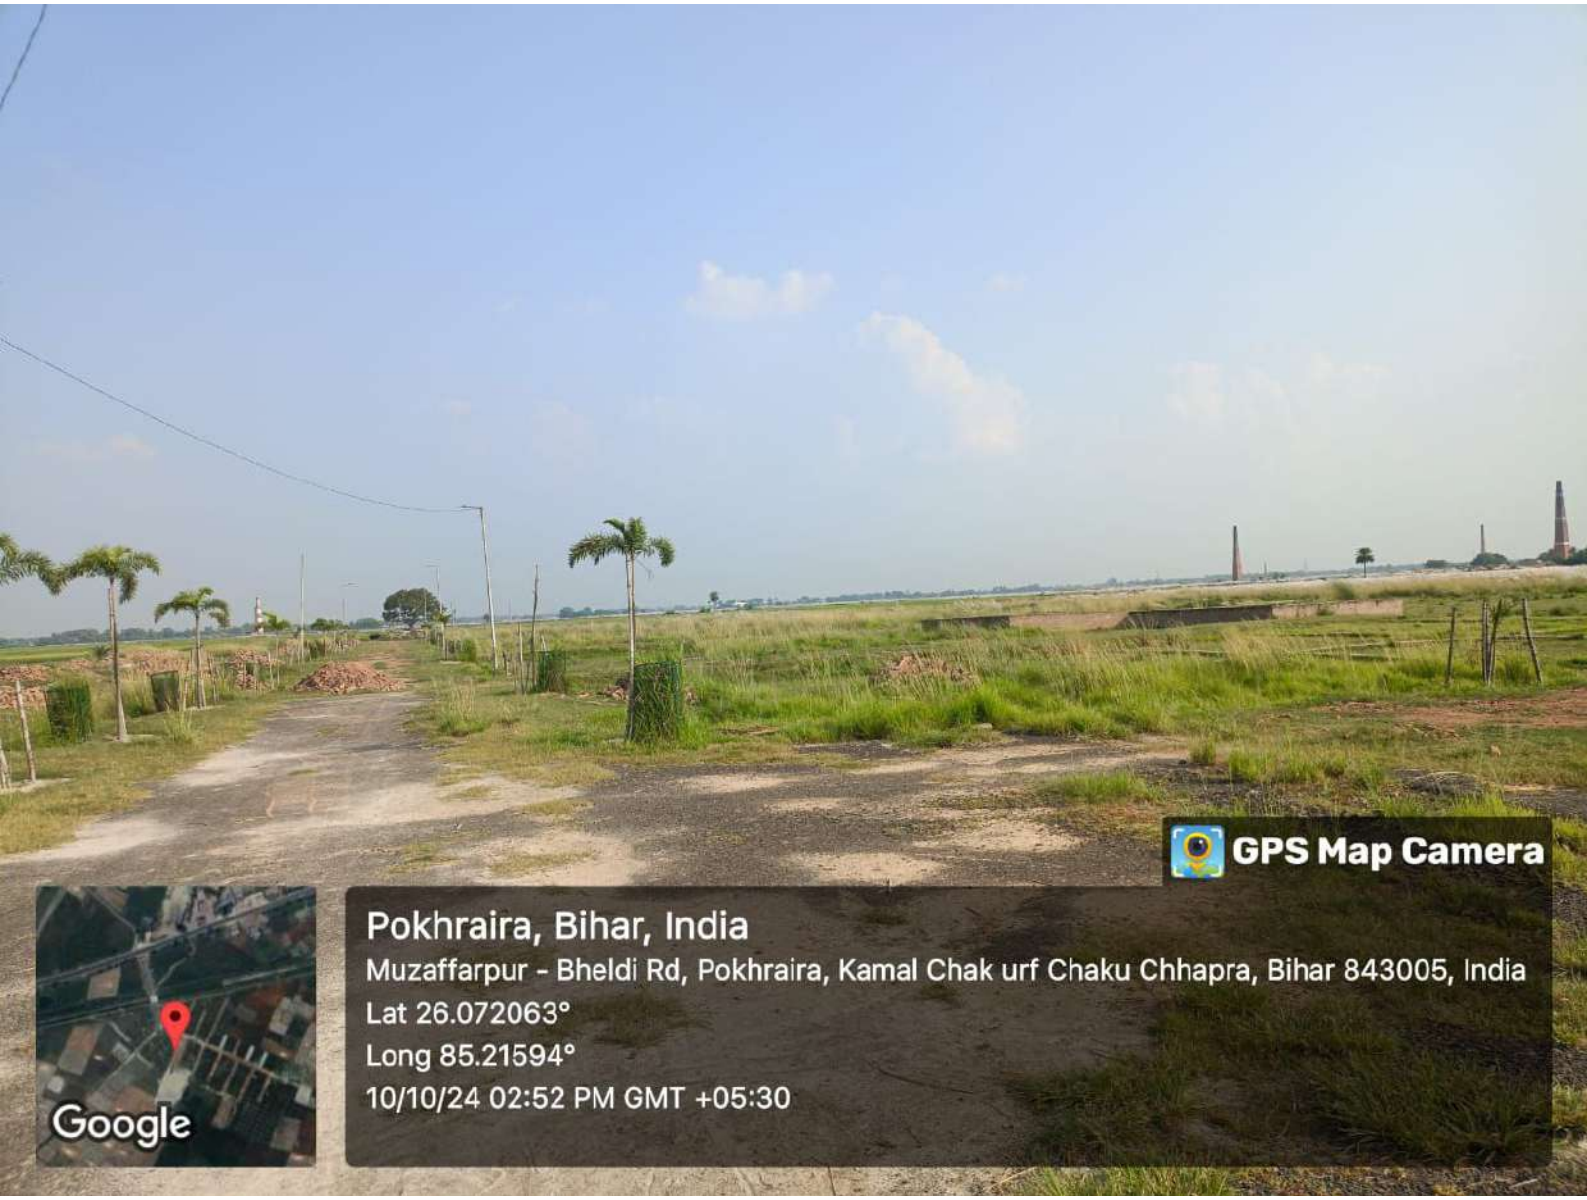
GPS Map Camera
Pokhraira, Bihar, India
Muzaffarpur - Bheldi Rd, Pokhraira, Kamal Chak urf Chaku Chhapra, Bihar 843005, India
Lat 26.072063°
Long 85.21594°
10/10/24 02:52 PM GMT +05:30
Google

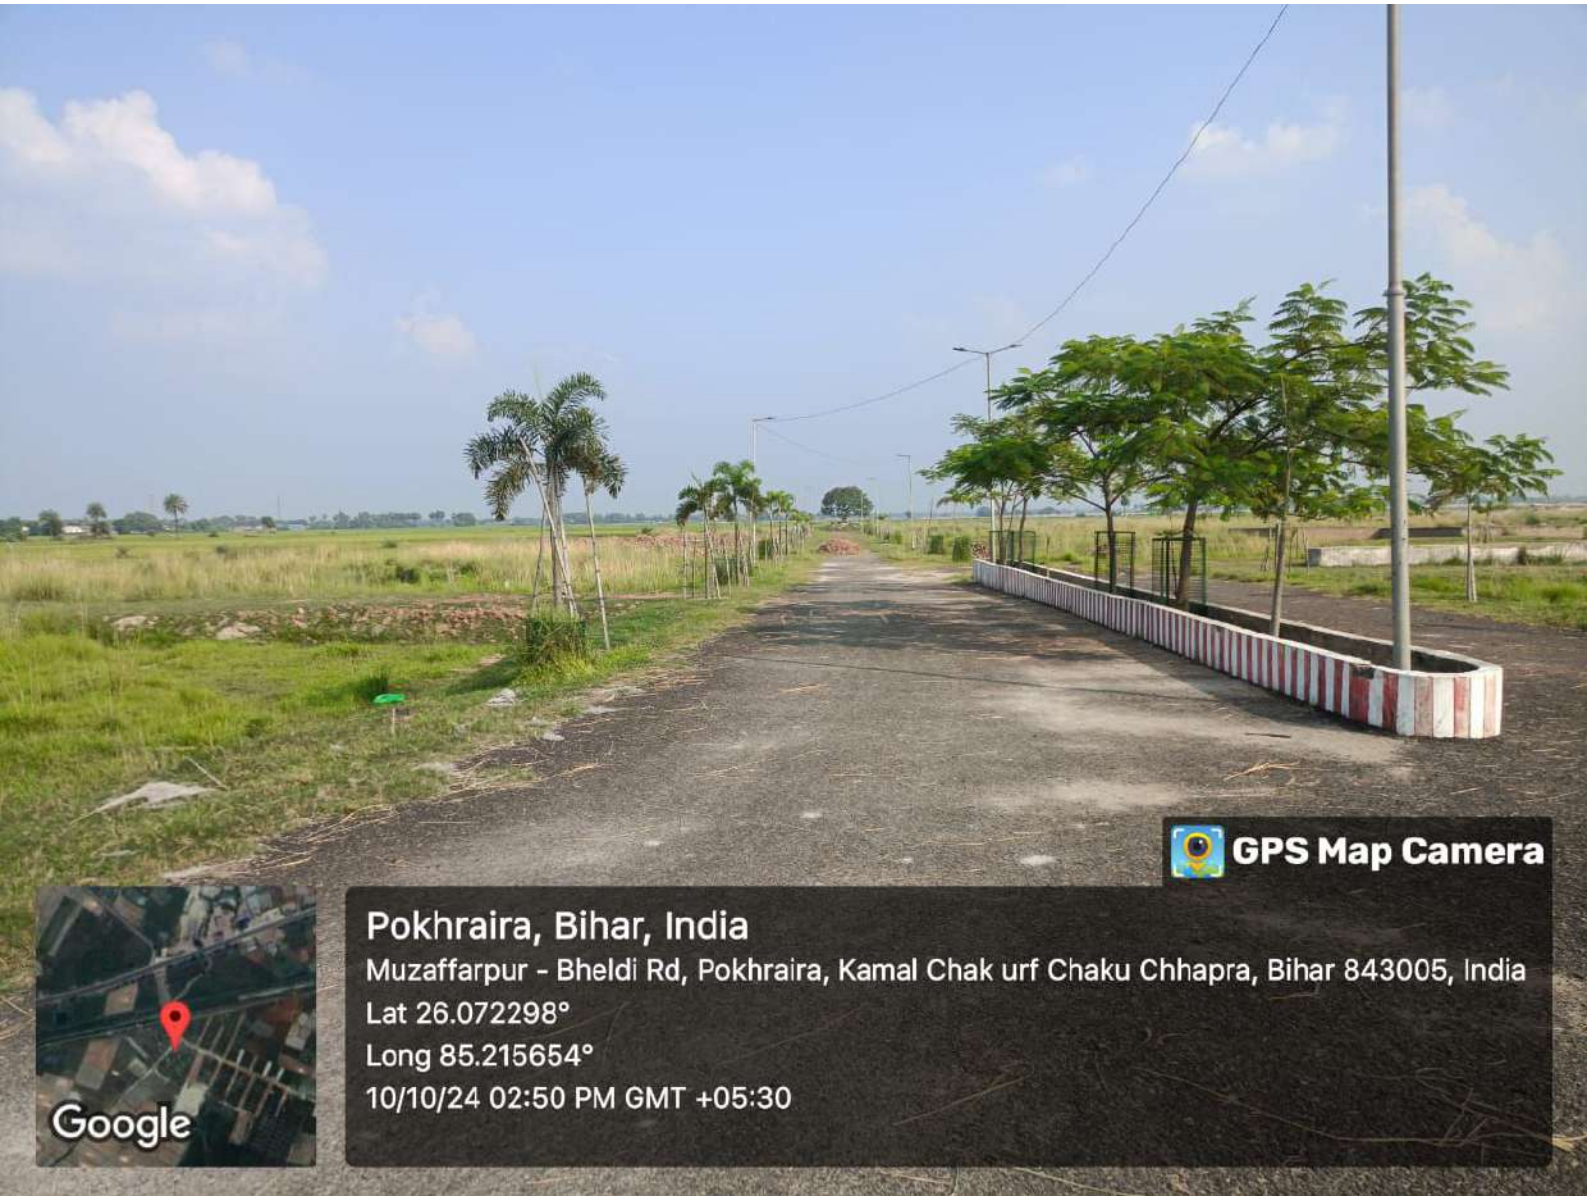
GPS Map Camera
Pokhraira, Bihar, India
Muzaffarpur - Bheldi Rd, Pokhraira, Kamal Chak urf Chaku Chhapra, Bihar 843005, India
Lat 26.072298°
Long 85.215654°
10/10/24 02:50 PM GMT +05:30
Google


GPS Map Camera
Muzaffarpur, Bihar, India
36F8+GGG, NH-102, Muzaffarpur, Kamal Chak urf Chaku Chhapra, Bihar 844121, India
Lat 26.072537°
Long 85.215554°
10/10/24 02:49 PM GMT +05:30
Google


METRO CITY
GPS Map Camera
Muzaffarpur, Bihar, India
36F8+GGG, NH-102, Muzaffarpur, Kamal Chak urf Chaku Chhapra, Bihar 844121, India
Lat 26.073362°
Long 85.215172°
10/10/24 02:45 PM GMT +05:30
Google
