FORM-7

[REGULATION-9]

Quarterly Progress Report for quarter ending Apr-Jun of 2023 (Year)

I. PARTICULARS OF PROJECT	
Project Registration Number	BRERAP00497-7/35/R-1142/2021
Name of Project/Phase of Registered Project	SANRACHNA HEIGHTS
Name of Promoter	SANRACHNA HOMES PVT. LTD.
Project Address	KHATA NO.- 430, TAUZI NO.- 5406, THANA NO.- 21, MAUZA- DANAPUR SAHJADPUR, PLOT NO.- 1639 P, DANAPUR, DIST.- PATNA
Name of Co-promoter	NA
Project Registration is valid up to	01/04/2025
Starting date of Project or Phase of the Project	01/04/2021
Type of Project or Phase of the Project	Residential/Group Housing
Period of validity of map by the Competent Authority	Three Years from the date of passing of MAP

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building/Block Number	Apartment Type	Carpet Area (In Sqft)	Total Number of sanctioned apartments	Total Number of Apartment
Sanrachna Heights	3 BHK	967.00	45	1. Booked/ Alloted - 24 2. Sold – 01
Sanrachna Heights	3 BHK	937.00	10	
Sanrachna Heights	3 BHK	940.00	05	
Sanrachna Heights	3 BHK	1006.00	05	

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of SanctionedGarages	Total Number of Garages:	
Sanrachna Heights	No Garages available	1. Booked/Allotted - 2. Sold -	

IV. DETAILS OF BUILDING APPROVALS					
(If already filed along with Registration Application, then there is no need of further filing)					
S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

V. Construction Progress of the Project

1. Plan Case No. 33/20-21 (Sanrachna Heights) (To be added for each Building / Wing)

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	**100%**
2.	Basements (if any)	**100%**
3.	Podiums (if any)	**NA**
4.	Plinth	**100%**
5.	Stilt Floor	**100%**
6.	Slabs of Super Structure	**100%**
7.	Internal walls Flats /Premises.	**100%**
8.	Internal Plaster & Putty within Flats /Premises	**60%**
9.	Floorings within Flats /Premises	**90%**
10.	Doors and Windows within Flats /Premises	**40%**
11.	Sanitary Fittings within the Flat/Premises	**40%**
12.	Electrical Fittings within the Flat/Premises	**35%**
13.	Staircases, Lifts Walls and Lobbies at each Floor level	**90%**
14.	Overhead and Underground Water Tanks.	**100%**
15.	External plumbing	**90%**

16.	External plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	**75%**
17.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as my be required to complete project as per specifications in Agreement of Sale. Any other activities.	**50%**

VI. Amenities and Common Area and External Infrastructure Development Works)				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	No	**NA**	
2.	Water Supply	Yes	90%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	Yes	40%	
4.	Storm Water Drains	No		
5.	Landscaping & Tree Planting	No		
6.	Street Lighting	No		
7.	Community Buildings	No		
8.	Treatment and Disposal of Sewage and Sullage Water	No		
9.	Solid Waste Management & Disposal	No		
10.	Water Conservation / RainWater Harvesting	No		
11.	Energy Management	No		
12.	Fire Protection and FireSafety Requirements	Yes	**60%**	

13.	Closed Parking	Yes	70%	
14.	Open Parking	No		
15.	Electrical Meter Room, Sub-Station, Receiving Station	No		
16.	Others (Option to AddMore)	No		

VII. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT		
(A)	**S. No.**	**Particulars**
	1.	**Front Elevation.-** Attached Below
	2.	**Rear Elevation.-** Attached Below
	3.	**Side Elevation.-** Attached Below
(B)		**Photograph of each floor**


VIII. Financial Progress of the Project

S.No.	Particulars	Amount (in Rs.)
1	Project Account No.	3110201004180
2	Estimated Cost of the Project including land cost at the start of the Quarter (In Lakh)	1,210.00/-
3	Amount received during the Quarter	2,56,33,236.00/-
4	Actual Cost Incurred during the Quarter	2,43,20,500.00/-
5	Net amount at end of the Quarter	85,780.86/-
6	Total expenditure on Project **till date**	11,53,67,254.00/-
7	Cumulative fund collected till the end of Quarter in question	12,62,61,251.20/-
8	Cumulative expenditure done till the end of Quarter in question	11,53,67,254.00/-

IX. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

X. MISCELLANEOUS		
A	List of Legal Cases (if any)	
1.	Case No.	NA
2.	Name of Parties	NA
B	Sale/Agreement for Saleduring the Quarter	
1.	Sale Deed	01
2.	Agreement for Sale	14

XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART
Weather the project in progress is as per time schedule or lagging behind?

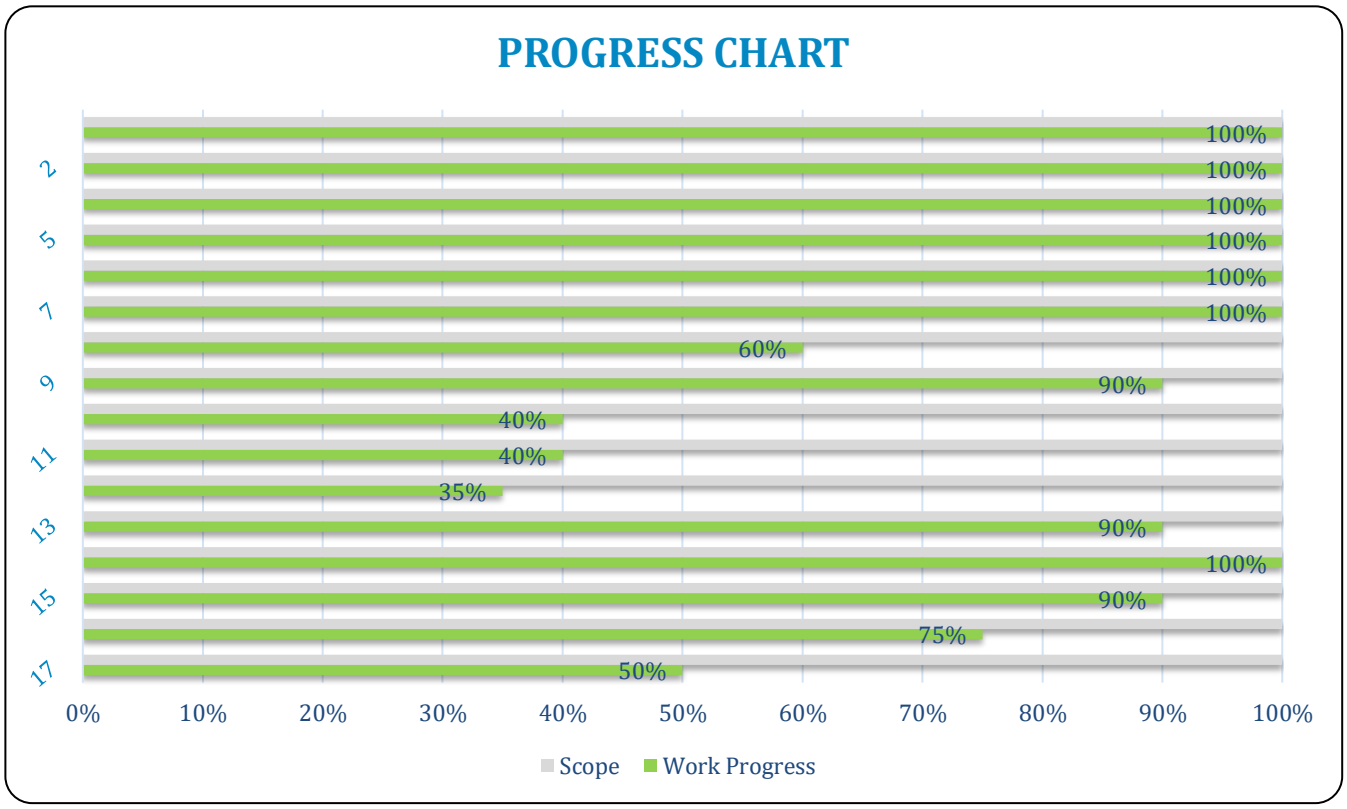



Project Site Photographs

Front Elevation




GPS Map Camera
Patna, Bihar, India
Vivek Vihar Colony, Danapur Nizamat, J3C5+R95, Yadav Colony, Vivek Vihar Colony, Patna, Bihar 801503, India
Lat 25.62199°
Long 85.05855°
06/-/2023 04:09 PM GMT +05:30
Google

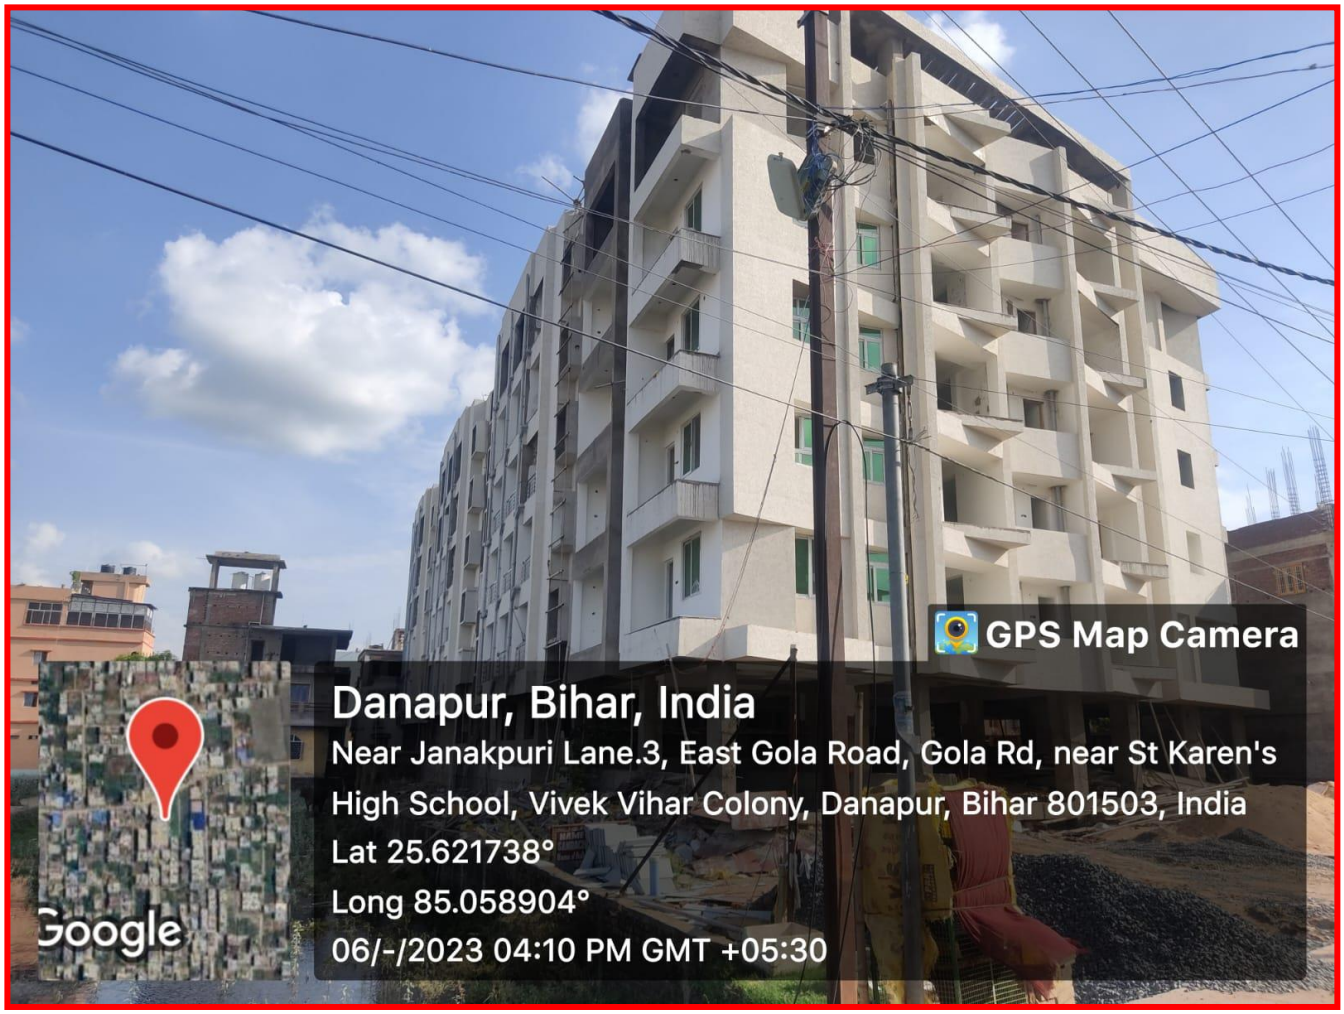
GPS Map Camera
Danapur, Bihar, India
Near Janakpuri Lane.3, East Gola Road, Gola Rd, near St Karen's High School, Vivek Vihar Colony, Danapur, Bihar 801503, India
Lat 25.621738°
Long 85.058904°
06/-/2023 04:10 PM GMT +05:30
Google

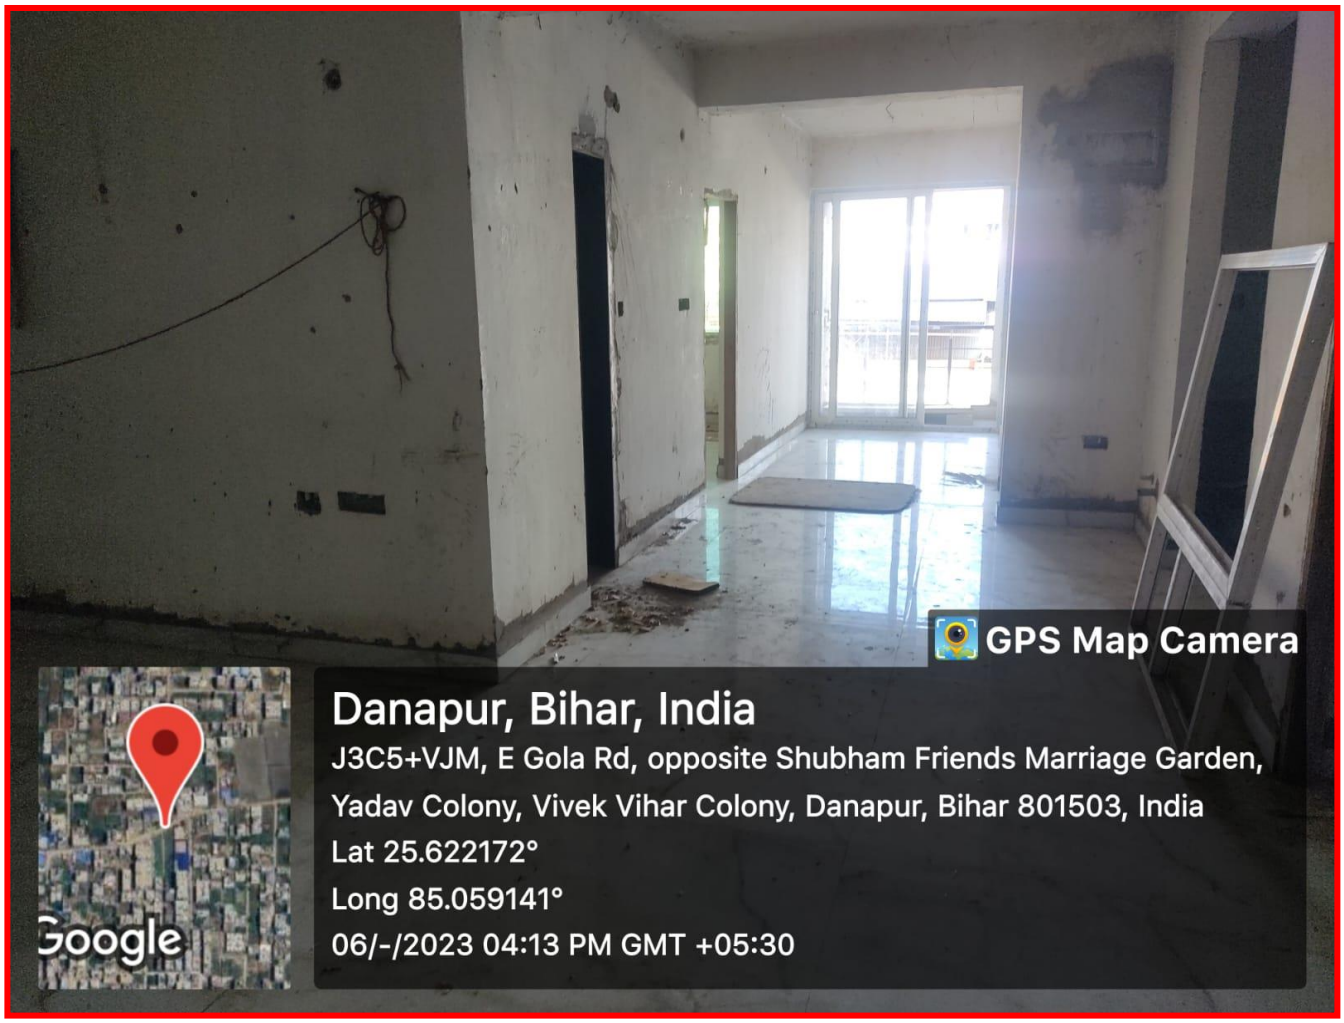

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Signature of Promoter
Sanrachna Homes Pvt. Ltd.

SANRACHNA HOMES PVT. LTD.
Director

Director
Date :
