FORM-7

[REGULATION-9]

Quarterly Progress Report for quarter ending Jul-Sep of 2023 (Year)

I. PARTICULARS OF PROJECT	
Project Registration Number	BRERAP05738-5/131/R-1318/2022
Name of Project/Phase of Registered Project	SAI LAXMI COMPLEX
Name of Promoter	MAITREYEE MAHANIRMAN LLP.
Project Address	KHATA NO- 41, SURVEY PLOT NO.- 74, THANA NO.- 17, TAUZI NO- 5852, AT MAUZA- RUSTAMPUR SAHPUR/SIKANDARPUR, THANA - DANAPUR,PLOT No.- 74, DANAPUR, DIST.- PATNA
Name of Co-promoter	NA
Project Registration is valid up to	17/04/2024
Starting date of Project or Phase of the Project	07/09/2021
Type of Project or Phase of the Project	Residential/Group Housing
Period of validity of map by the Competent Authority	Three Years from the date of passing of MAP

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building/Block Number	Apartment Type	Carpet Area (In Sqft)	Total Number of sanctioned apartments	Total Number of Apartment
Sai Laxmi Complex	3 BHK	891.00	22	1. Booked—04 2. Cancelled—00
Sai Laxmi Complex	2 BHK	612.00	11	

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of SanctionedGarages	Total Number of Garages:	
Sai Laxmi Complex	No Garages available	1. Booked/Allotted - 2. Sold -	

For Maitreyee Mahanirman LLP

Designated Partner

IV. DETAILS OF BUILDING APPROVALS					
(If already filed along with Registration Application, then there is no need of further filing)					
S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

V. Construction Progress of the Project

1. Plan Case Number-16/21-22 (Sai Laxmi Complex) (To be added for each Building / Wing)

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	100%
2.	Basements (if any)	30%
3.	Podiums (if any)	NA
4.	Plinth	100%
5.	Stilt Floor	70%
6.	Slabs of Super Structure	28%
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0%
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	8%
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%

For Maitreyee Mahanirman LLP

Designated Partner

11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as my be required to complete project as per specifications in Agreement of Sale. Any other activities.	**11%**

VI.	**(Amenities and Common Area and External Infrastructure Development Works)**			
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	No		
2.	Water Supply	Yes	50%	Pump Installed
3.	Sewerage (Chamber, Line, Septic Tank, STP)	Yes	0%	
4.	Storm Water Drains	No		
5.	Landscaping & Tree Planting	No		
6.	Street Lighting	No		
7.	Community Buildings	No		
8.	Treatment and Disposal of Sewage and Sullage Water	No		
9.	Solid Waste Management & Disposal	No		
10.	Water Conservation / RainWater Harvesting	No		
11.	Energy Management	No		
12.	Fire Protection and FireSafety Requirements	No		
13.	Closed Parking	Yes	50%	

For Maitreyee Mahanirman LLP

Rambabu Reddy

Designated Partner

14.	Open Parking	No		
15.	Electrical Meter Room, Sub-Station, Receiving Station	No		
16.	Others (Option to AddMore)	No		

VII. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT		
(A)	**S. No.**	**Particulars**
	1.	**Front Elevation.-** Attached Below
	2.	**Rear Elevation.-** Attached Below
	3.	**Side Elevation.-** Attached Below
(B)		**Photograph of each floor**

VIII. Financial Progress of the Project

S.No.	Particulars	Amount (in Rs.)
1	Project Account No.	19230200003558
2	Estimated Cost of the Project including land cost at the start of the Quarter (In Lakh)	609.50/-
3	Amount received during the Quarter	0.00/-
4	Actual Cost Incurred during the Quarter	5,37,396.05/-
5	Net amount at end of the Quarter	0.00/-
6	Total expenditure on Project **till date**	1,91,04,037.69/-
7	Cumulative fund collected till the end of Quarter in question	65,09,000.00/-
8	Cumulative expenditure done till the end of Quarter in question	1,91,04,037.69/-

IX. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED


For Maitreyee Mahanirman LLP

Rambabu Roy

Designated Partner

X. MISCELLANEOUS		
A	List of Legal Cases (if any)	
1.	Case No.	NA
2.	Name of Parties	NA
B	Sale/Agreement for Saleduring the Quarter	
1.	Sale Deed	
2.	Agreement for Sale	03

XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART
Weather the project in progress is as per time schedule or lagging behind?

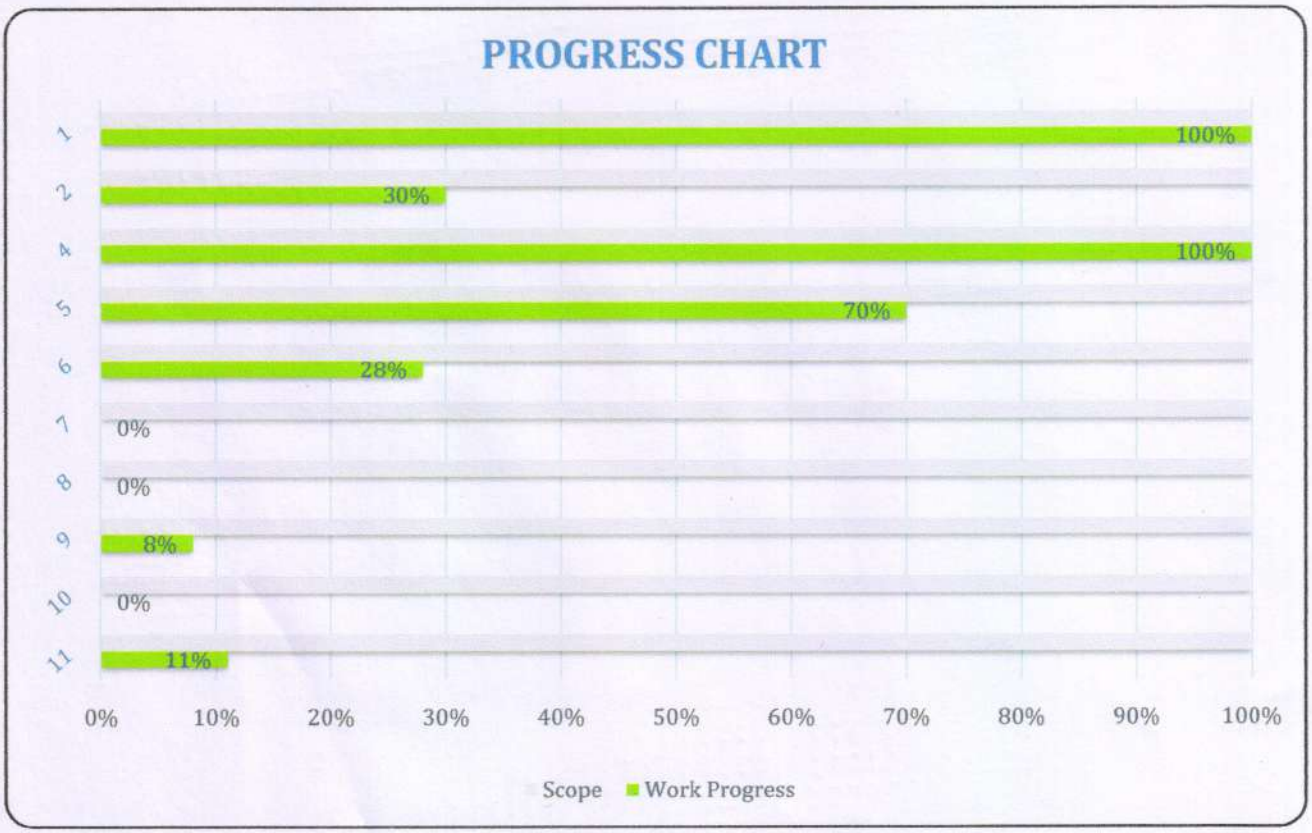


For Maitreyee Mahanirman LLP

Rambabu Roy

Designated Partner

Project Site Photographs

Front Elevation

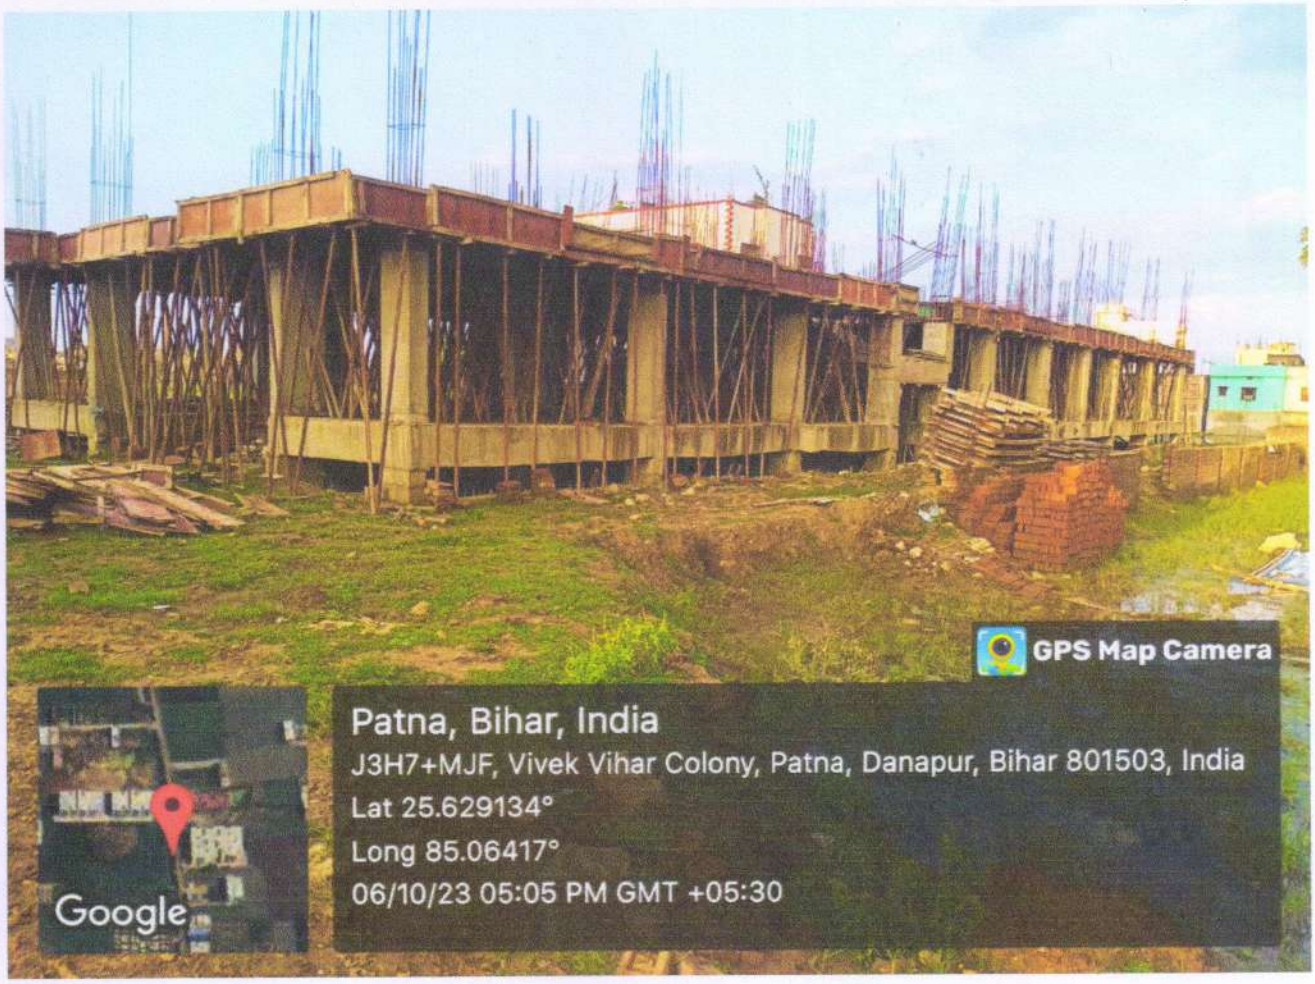

For Maitreyee Mahanirman LLP

Rambabu Roy

Designated Partner

Side Elevation



Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Signature of Promoter

Maitreyee Mahanirman LLP.

For Maitreyee Mahanirman LLP

Rambabu Rg

Designated Partner

Partner

Date :

For Maitreyee Mahanirman LLP

Rambabu Rg

Designated Partner
