FORM-7

[REGULATION-9]

Quarterly Progress Report for quarter ending March of 2024

I. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP0001170-01/1128/R-935/2020	Name of Project/Phaseof Registered Project	SHANGRILA VILLAGE
Name of Promoter	YASH LAXMI ENTERPRISES PVT LTD	Project Address	MAUZA-GANESHPUR, ANCHAL MUSHAHRI THANA-AHIYAPUR, MUZAFFARPUR
Name of Co-promoter	N/A		
Project Registration is valid up to	31/12/2024		
Starting date of Project or Phaseof the Project	29/04/2020		
Type of Project or Phase of theProject	Residential		
Period of validity of map by the Competent Authority	3 YEARS		

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS				
Building/Block Number	Apartment Type	Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments –
01 TO 05 BLOCK	1. 1 BHK - 2. 2 BHK, - 3. 3 BHK - 4. Shop - 5.Bungalow - 6. Plot etc. -		140	1. Booked/ Allotted - 6 2. Sold -0

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES			
Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages: 1. Booked/Allotted -	6
01 TO 05 BLOCK	Open -60 and Covered -120=180	2. Sold -	0

YASH LAXMI ENTERPRISES P. LTD.

M. Director

IV. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of Further filing)

S.NO.	Name of the Approval / N.O.C. / Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval (S), if any, required for the Project				

V. Construction Progress of the Project

1. Building / Wing / Layout Number A_____(To beaded for each Building / Wing)

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	1st and 2nd Block -100%
2.	Basements (if any)	NO
3.	Podiums (if any)	1st Block-100%
4.	Plinth	1st Block-100%
5.	Stilt Floor	1st, 2nd, 3rd and 4th floor only 1st Block -100% and 2nd Block-1st and 2nd floor.
6.	Slabs of Super Structure	60%
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	25%
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%

YASH LAXMI ENTERPRISES P. LTD.

M. Director

9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	13%
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as my be required to complete project as per specifications in Agreement of Sale. Any other activities.	0%

VI. Amenities and Common Area and External Infrastructure Development Works)				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES		
2.	Water Supply	YES	10%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	
4.	Storm Water Drains	YES	0%	
5.	Landscaping & Tree Planting	YES	0%	
6.	Street Lighting	YES	0%	
7.	Community Buildings	YES	0%	

YASH LAXMI ENTERPRISES P. LTD.

M. Director

8.	Treatment and Disposal of Sewage and Sullage Water	YES	0%	
9.	Solid Waste Management & Disposal	YES	0%	
10.	Water Conservation / Rain Water Harvesting	YES	0%	
11.	Energy Management	YES	0%	
12.	Fire Protection and Fire Safety Requirements	YES	0%	
13.	Closed Parking	YES	0%	
14.	Open Parking	YES	0%	
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	
16.	Others (Option to Add More)			

VI. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
1.	Internal Roads & Footpaths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Landscaping and Tree Planning			
6.	Street Lighting			
7.	Disposal of sewage & Sullage Water			
8.	Water conservation/ Rain Water Harvesting			

YASH LAXMI ENTERPRISES P. LTD.

M. Director

9.	Energy Management			

VII. GEO TAGGED AND DATE PHOTOGRAPH OF (EACH BLOCK) OF THE PROJECT			
(A)	Sr. No.		
	1.	Front Elevation.	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

VIII. Financial Progress of the Project		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	3787024366
2.	Estimated Cost of the Project including land cost at the start of the Project	2750 lakh
3.	Amount received during the Quarter (Loan and from Customers)	79,69,800=00
4.	Actual Cost Incurred during the Quarter	85,90,761=00
5.	Net amount at end of the Quarter	76,95,100=00
6.	Total expenditure on Project **till date**	3,12,72,024=00
7.	Cumulative fund Collected till the end of Quarter in question	
8.	Cumulative expenditure done till the end of Quarter in question	

IX. Details of Mortgage or Charge if any created

X. MISCELLANEOUS		
A	List of Legal Cases (if any)	
1.	Case No.	NO

YASH LAXMI ENTERPRISES P. LTD.

M. Director

2.	Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	01
XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

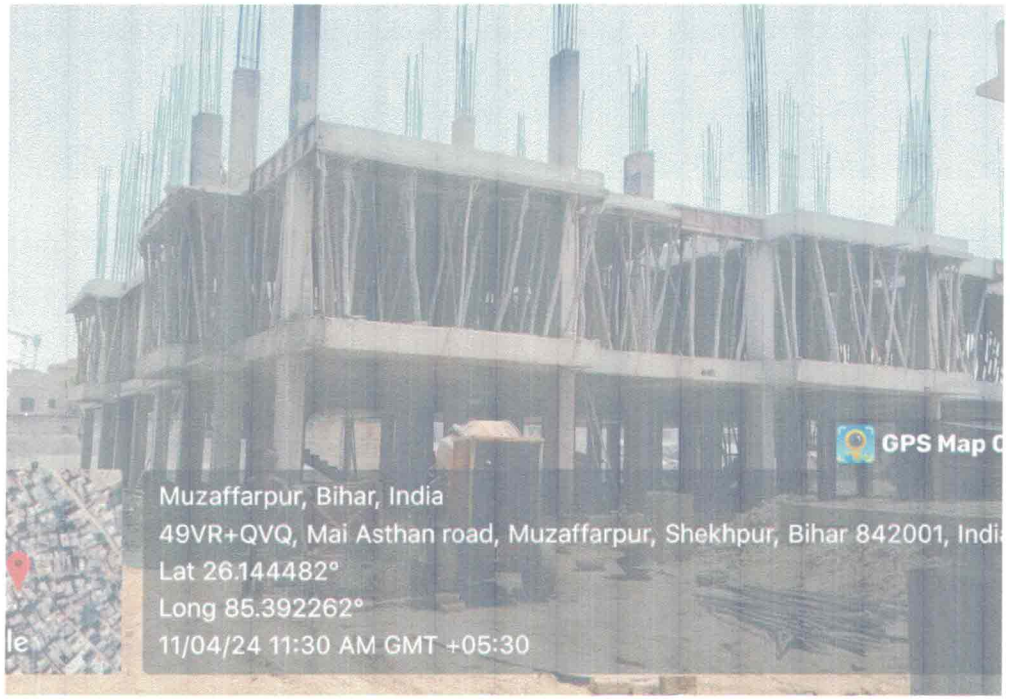
YASH LAXMI ENTERPRISES P. LTD.

M. Director

Signature of Promoter

Name:

Date:


GPS Map C
Muzaffarpur, Bihar, India
49VR+QVQ, Mai Asthan road, Muzaffarpur, Shekhpur, Bihar 842001, Indi
Lat 26.144482°
Long 85.392262°
11/04/24 11:30 AM GMT +05:30


GPS Map C
Muzaffarpur, Bihar, India
49VR+QVQ, Mai Asthan road, Muzaffarpur, Shekhpur, Bihar 842001, Indi
Lat 26.144482°
Long 85.392262°
11/04/24 11:38 AM GMT +05:30


GPS Map Camera
Muzaffarpur, Bihar, India


GPS Map C
Muzaffarpur, Bihar, India
49VR+QVQ, Mai Asthan road, Muzaffarpur, Shekhpur, Bihar 842001, Indi
Lat 26.144482°
Long 85.392262°
11/04/24 11:30 AM GMT +05:30
