QUARTERLY PROGRESS REPORT FOR RERA BIHAR

Jan - Mar, 2021

ABSTRACT

This report documents and describes the updates on project work progress, with updates on status of financials, bookings in the project along with status of the approvals for the quarter.

PROJECT NAME

MIRA REGENCY

PROMOTER NAME

UNIVERSAL GREEN HEIGHTS LLP

RERA REGISTRATION NO.

BRERAP31918-1/949/R-628/2019

Report Drafted by Limpid Construction Consulting LLP using information provided by promoter

PROJECT QUARTERLY PROGRESS STATUS

Quarter: Jan-Mar, 2021

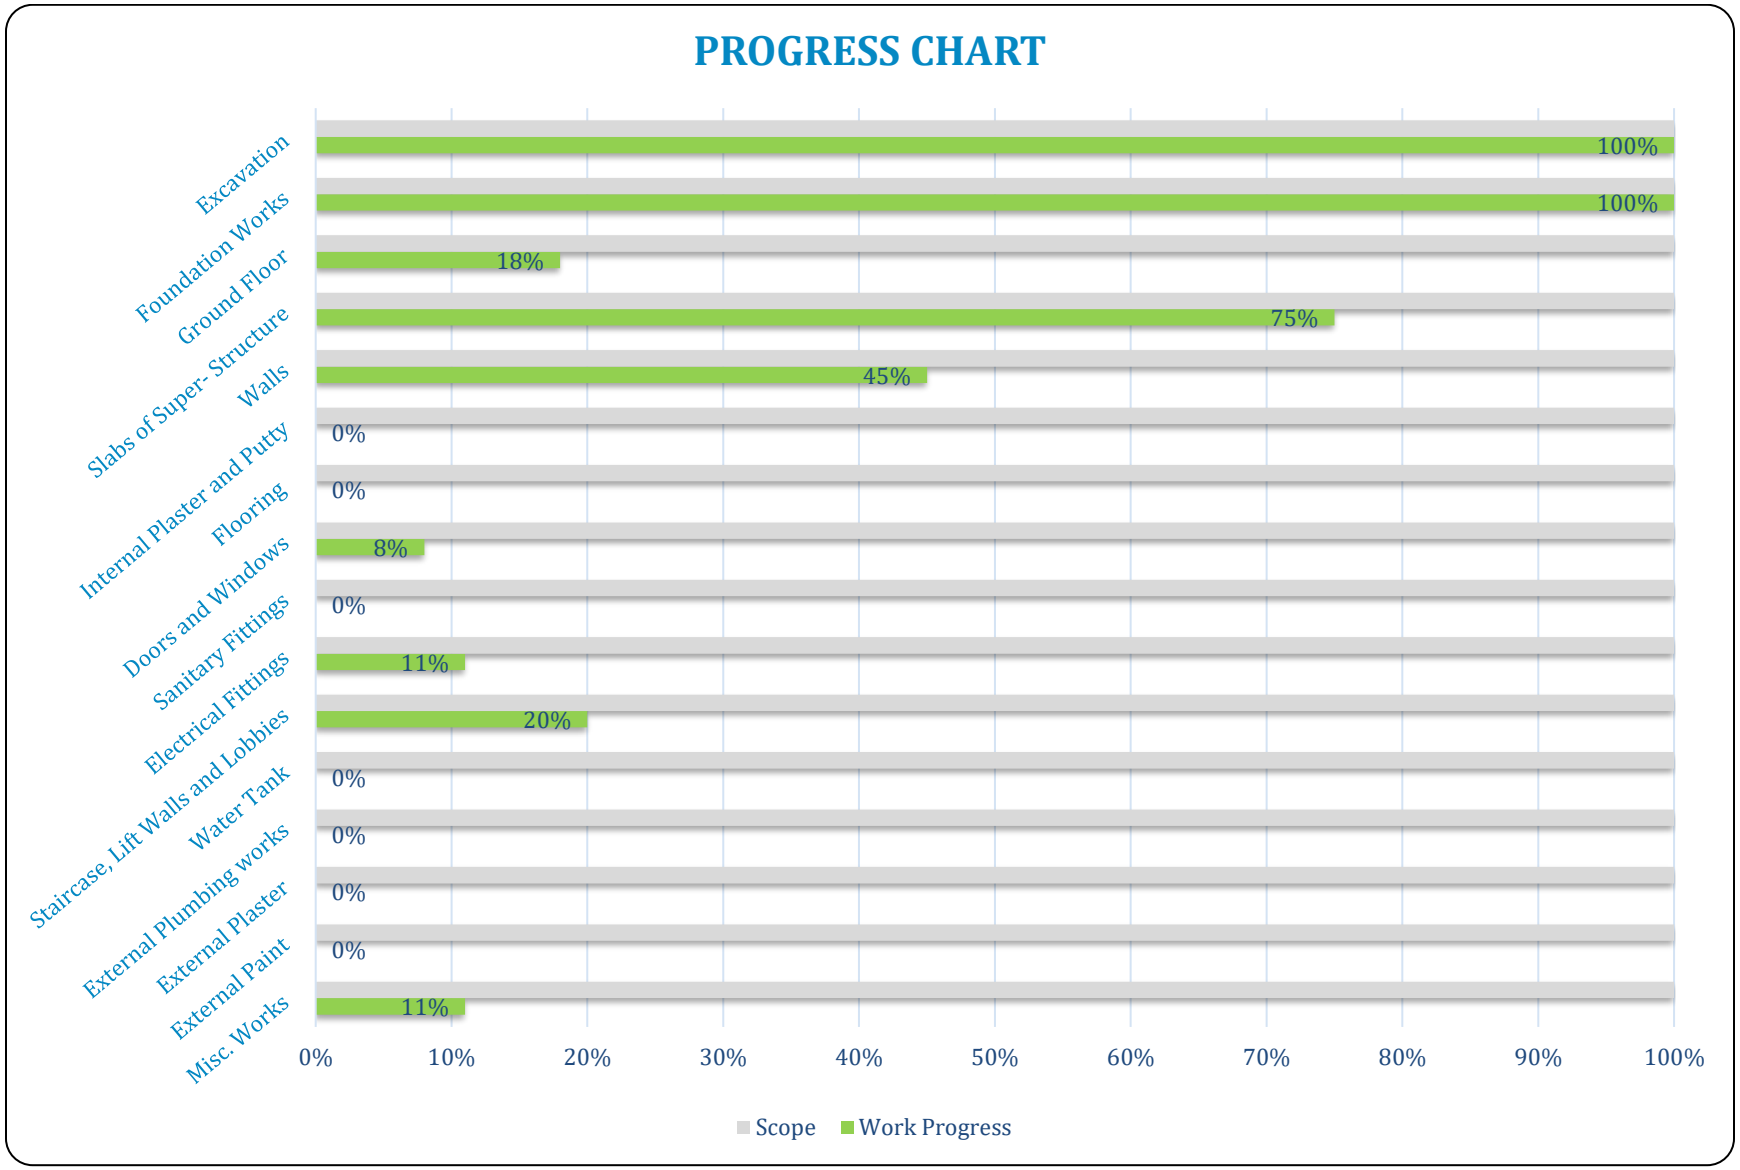
Project Description: *A Residential building project consisting of B+G+6 floors and 40 flats.*

Progress Update of each Block/Wing separately

S. No.	Task/Activity	Applicable (Yes/No)	Percentage of Work Done	Remarks
1	Excavation	Yes	100%	Overall Excavation works complete.
2	Foundation Works	Yes	100%	Overall Foundation works complete.
3	Ground floor	Yes	18%	Retaining Wall Construction is almost complete.
4	Slabs of super- structure	Yes	75%	Slab casting almost complete.
5	Walls	Yes	45%	Brick work under progress in all floor.
6	Internal Plaster& Putty	Yes	0%	
7	Flooring inside units and common areas	Yes	0%	
8	Doors and Window to each of unit and common areas	Yes	8%	Door frame installation under progress in full swing.
9	Sanitary fittings within the unit including water proofing and plumbing	Yes	0%	
10	Electrical fitting within the unit	Yes	11%	Conduit & Pipe laying under progress.
11	Staircase, lift walls and lobbies at each floor	Yes	20%	Staircase upto terrace floor completed, Lift wall from 1st to 6th floor near about to completion, Lobby construction under progress in full swing.
12	Water tank	Yes	0%	
13	External Plumbing works and completion of terrace with waterproofing of the building if specified.	Yes	0%	

Progress Update of each Block/Wing separately

S. No.	Task/Activity	Applicable (Yes/No)	Percentage of Work Done	Remarks
14	External Plaster	Yes	0%	
15	External Paint	Yes	0%	
16	Installation of lifts water pumps, firefighting fittings as NOC, Electricals fittings to the common areas, electro mechanic equipment, finishing to the entrance lobby, plinth protection, paving of areas, compound walls and other requirements as may be required to obtain completion/occupancy certificate. (Misc. Works)	Yes	11%	Pump is installed.


PROGRESS CHART
Excavation
Foundation Works
Ground Floor
Slabs of Super- Structure
Walls
Internal Plaster and Putty
Flooring
Doors and Windows
Sanitary Fittings
Electrical Fittings
Staircase, Lift Walls and Lobbies
Water Tank
External Plumbing works
External Plaster
External Paint
Misc. Works
100%
100%
18%
75%
45%
0%
0%
8%
0%
11%
20%
0%
0%
0%
0%
11%
0%
10%
20%
30%
40%
50%
60%
70%
80%
90%
100%
Scope
Work Progress

Progress Update for Common Areas, Facilities and Amenities in the Project

S. No.	Description	Applicable (Yes/No)	Percentage of Work Done	Remarks
1	Compound Walls	Yes	80%	Compound wall structure near about to complete.
2	Water supply	Yes	0%	

Update on number and types of flats/plots booked during the quarter

S.No	Unit Type	Total No. of Units in builder's Share	No. of Flats / Plot Booked				No. of Garages/ Covered Parking Booked			
			Opening Balance	Booked in the quarter	Cancelled in the quarter	Closing Balance	Opening Balance	Booked in the quarter	Cancelled in the quarter	Closing Balance
1	3 BHK	20	8	2	0	10	8	2	0	10

Status of financials in the project up to 31st March, 2021

S.No.	Description	Amount (in Rs.)
1	Amounts received from allottees against booking of units(for builder's share)	3,49,63,809.62
2	Expenditure done towards completion of project	3,48,63,356.81
3	Balance in Designated Bank A/c as on this quarter end	11,98,607.00

Status of Approvals

A. Approval Received

S. No.	Description	Date of Receipt
1	Fire NOC	28.04.18
2	Sanctioning of Building Plan	05.01.19
3	RERA Registration	20.05.19

B. Approval Applied

S. No.	Description	Expected Date
NA	NA	NA

C. Approvals to be applied

S. No.	Description	Expected Date of application
NA	NA	NA

D. Modifications amendments or revisions, if any, issued by competent authority with regard to any sanctioned plans, layout plans, specifications, license, permit or approval for the project - NA

Project Site Photographs



