QUARTERLY PROGRESS REPORT FOR RERA BIHAR

Apr - Jun, 2021

ABSTRACT

This report documents and describes the updates on project work progress, with updates on status of financials, bookings in the project along with status of the approvals for the quarter.

PROJECT NAME

AADHVIK BIMLA ENCLAVE

PROMOTER NAME

AADHVIK HOUSING PVT. LTD.

RERA REGISTRATION NO.

BRERAP20338-1/971/R-707/2019

Report Drafted by Limpid Construction Consulting LLP using information provided by promoter

PROJECT QUARTERLY PROGRESS STATUS

Quarter: Apr-Jun, 2021

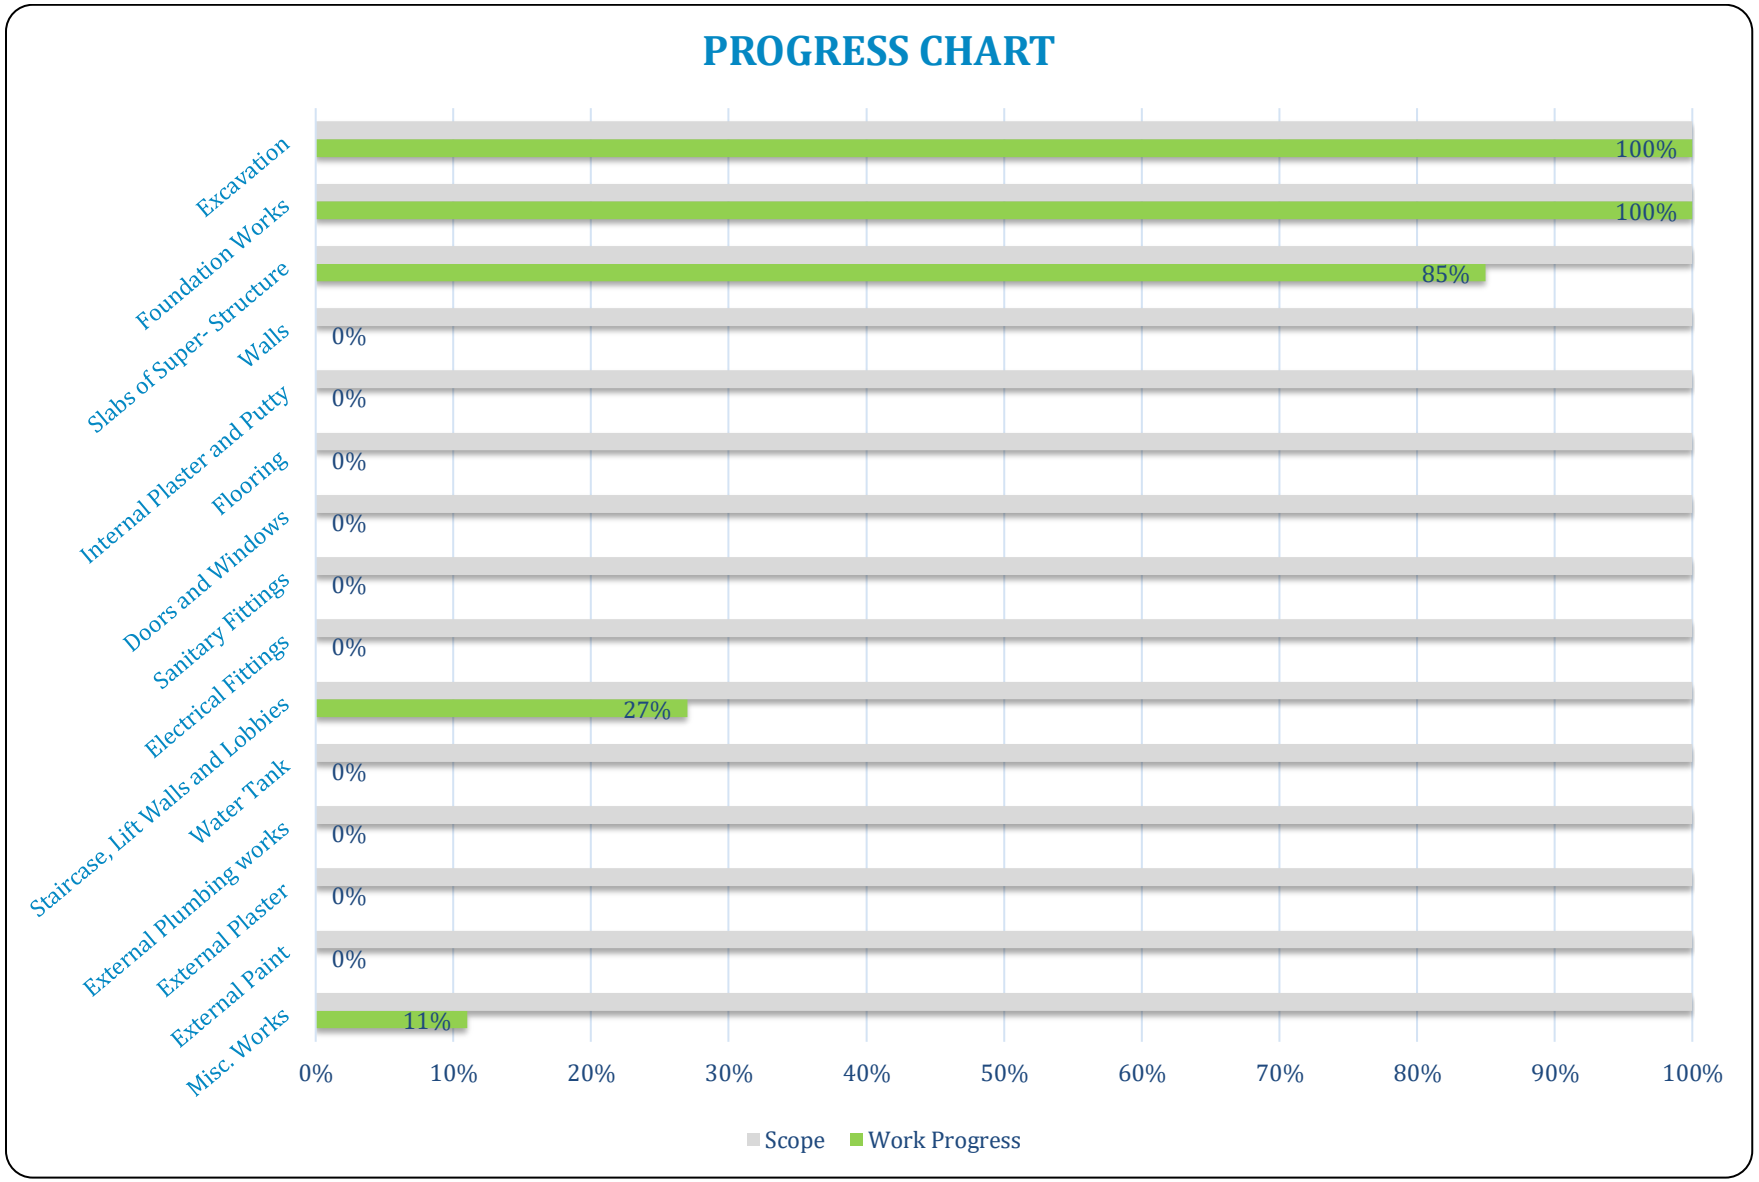
Project Description: *With pleasant surroundings and environmental cleanliness in abundance, this locality is best suited to get settled into. The project is G+4 floors respectively.*

Progress Update of each Block/Wing separately

S. No.	Task/Activity	Applicable (Yes/No)	Percentage of Work Done	Remarks
1	Excavation	Yes	100%	Overall excavation works complete.
2	Foundation Works	Yes	100%	Overall foundation works complete.
3	Slabs of structure	Yes	85%	Slab casting till 4th floor complete and for terrace floor shuttering work near about to completion.
4	Walls	Yes	0%	Brick work yet to start.
5	Internal Plaster & Putty	Yes	0%	
6	Flooring inside units and common areas	Yes	0%	
7	Doors and Window to each of unit and common areas	Yes	0%	
8	Sanitary fittings within the unit including water proofing and plumbing	Yes	0%	
9	Electrical fitting within the unit	Yes	0%	
10	Staircase, lift walls and lobbies at each floor	Yes	27%	Staircase structure complete till 4th floor.
11	Water tank	Yes	0%	
12	External Plumbing works and completion of terrace with waterproofing of the building if specified.	Yes	0%	
13	External Plaster	Yes	0%	

Progress Update of each Block/Wing separately

S. No.	Task/Activity	Applicable (Yes/No)	Percentage of Work Done	Remarks
14	External Paint	Yes	0%	
15	Installation of lifts water pumps, firefighting fittings as NOC, Electricals fittings to the common areas, electro mechanic equipment, finishing to the entrance lobby, plinth protection, paving of areas, compound walls and other requirements as may be required to obtain completion/occupancy certificate. (Misc. Works)	Yes	11%	Pump is installed.


PROGRESS CHART
Excavation
Foundation Works
Slabs of Super- Structure
Walls
Internal Plaster and Putty
Flooring
Doors and Windows
Sanitary Fittings
Electrical Fittings
Staircase, Lift Walls and Lobbies
Water Tank
External Plumbing works
External Plaster
External Paint
Misc. Works
100%
100%
85%
0%
0%
0%
0%
0%
0%
27%
0%
0%
0%
0%
11%
0%
10%
20%
30%
40%
50%
60%
70%
80%
90%
100%
Scope
Work Progress

Progress Updatefor Common Areas, Facilities and Amenities in the Project

S. No.	Description	Applicable (Yes/No)	Percentage of Work Done	Remarks
1	Compound Walls	Yes	50%	Construction of compound walls complete.
2	Water supply	Yes	40%	Boring works complete and supply pipes installation balance.

Update on number and types of flats/plots booked during the quarter for Block A & B

S.No	Unit Type	Total No. of Units in builder's Share	No. of Flats / Plot Booked				No. of Garages/ Covered Parking Booked			
			Opening Balance	Booked in the quarter	Cancelled in the quarter	Closing Balance	Opening Balance	Booked in the quarter	Cancelled in the quarter	Closing Balance
1	2BHK	2	0	0	0	0	0	0	0	0
2	3BHK	6	1	0	0	1	1	0	0	1

Status of financials in the project up to 30th June, 2021

S.No.	Description	Amount in Rs.
1	Amounts received from allottees against booking of units(for builder's share) Incl. GST	20,90,700/-
2	Expenditure done towards completion of project	92,51,170/-
3	Balance in Designated Bank A/c as on this quarter end	0.00/-

Status of Approvals

A. Approval Received

S. No.	Description	Date of Receipt
1	Sanctioning of Building Plan	14.02.19
2	RERA Registration	09.08.19

B. Approval Applied

S. No.	Description	Expected Date
NA	NA	NA

C. Approvals to be applied

S. No.	Description	Expected Date of application
NA	NA	NA

D. Modifications amendments or revisions, if any, issued by competent authority with regard to any sanctioned plans, layout plans, specifications, license, permit or approval for the project - NA

Project Site Photographs



